


PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA



Date: 09-04-16 6:00 PM
Sheet: 1 / 2

Task

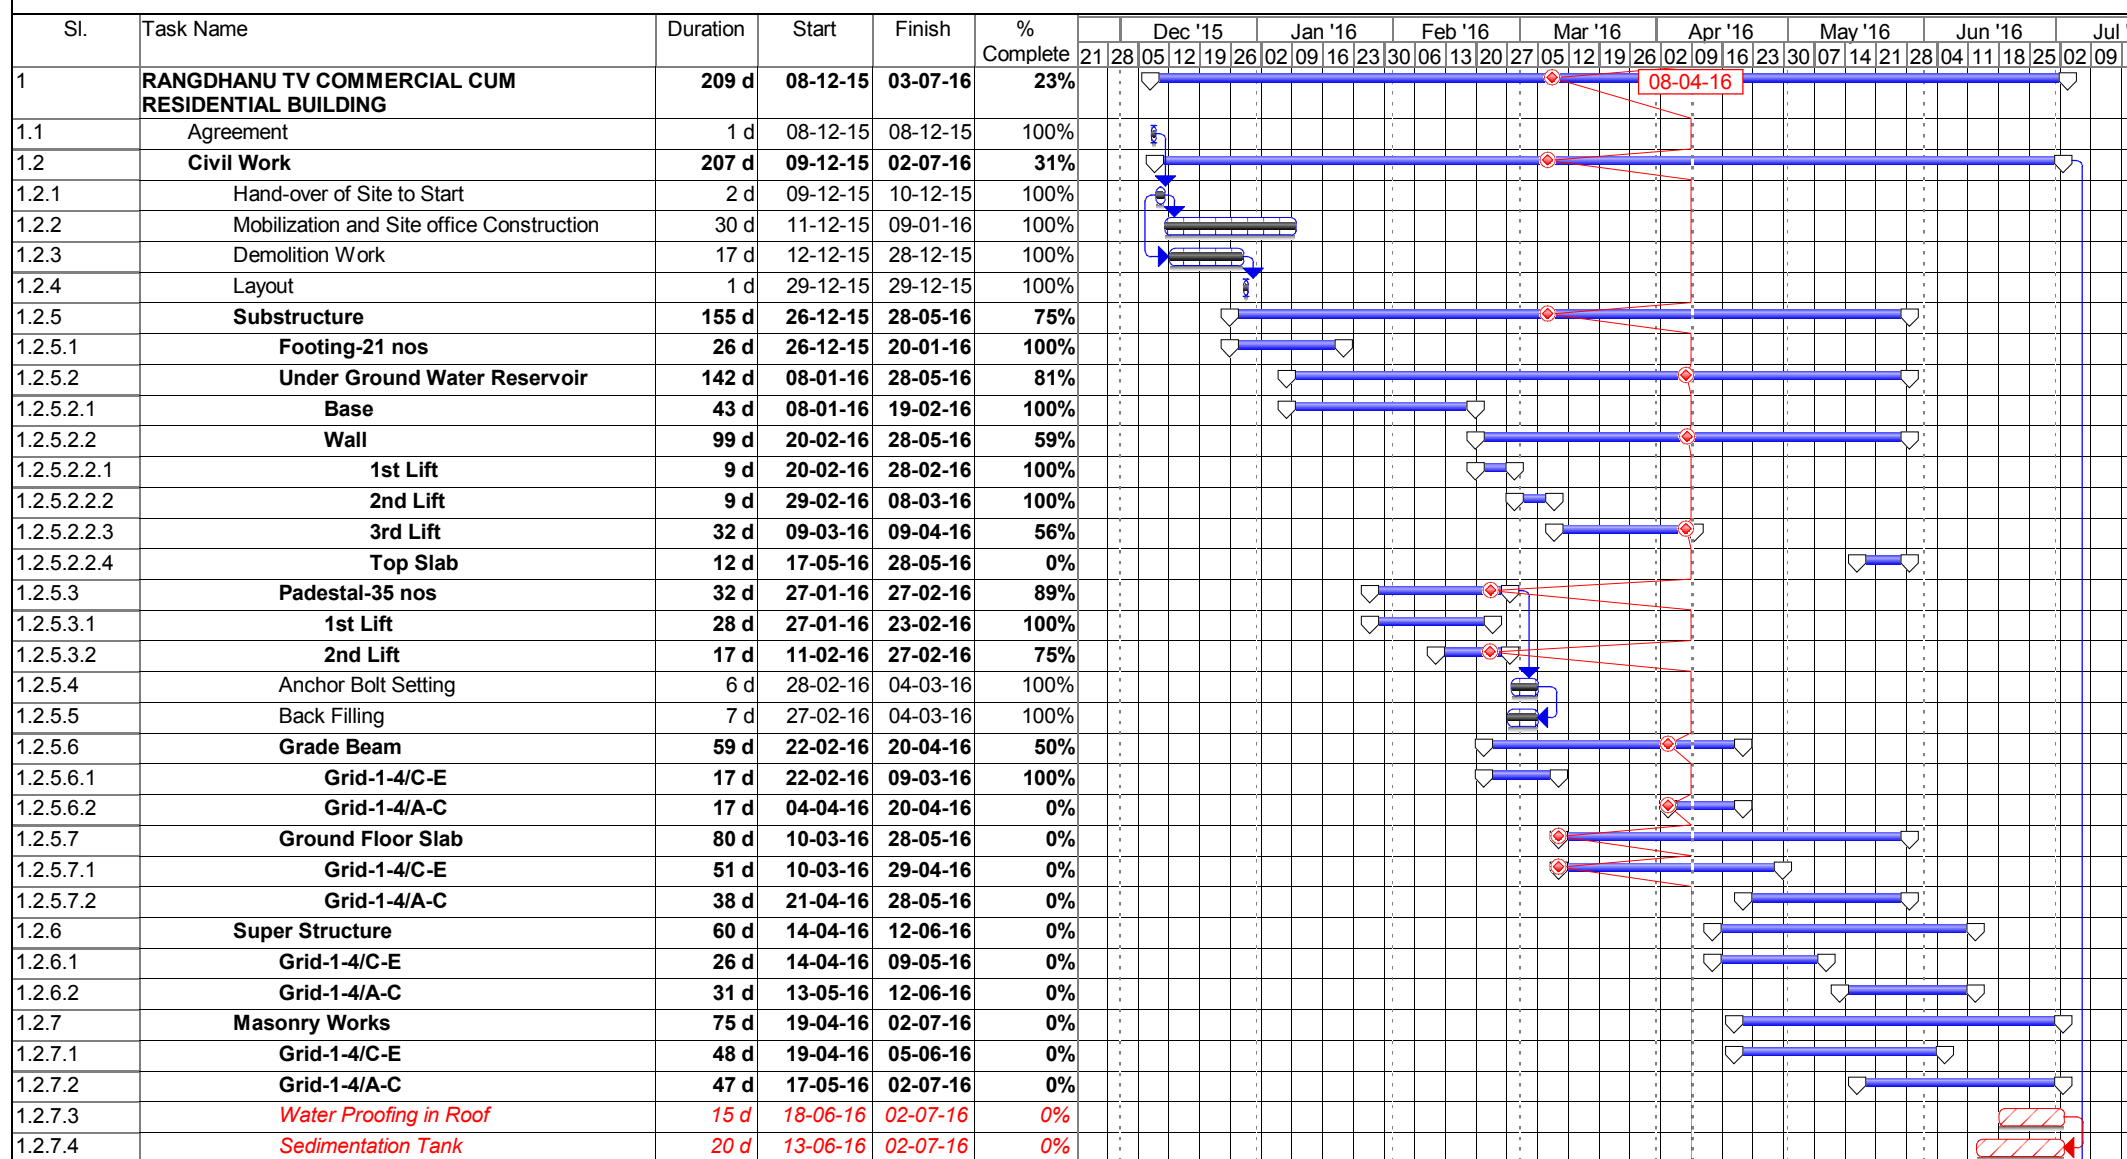

Summary



Rolled Up Progress



Critical Task



Rolled Up Task



Project Summary



Progress




Rolled Up Critical Task



Group By Summary



PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA

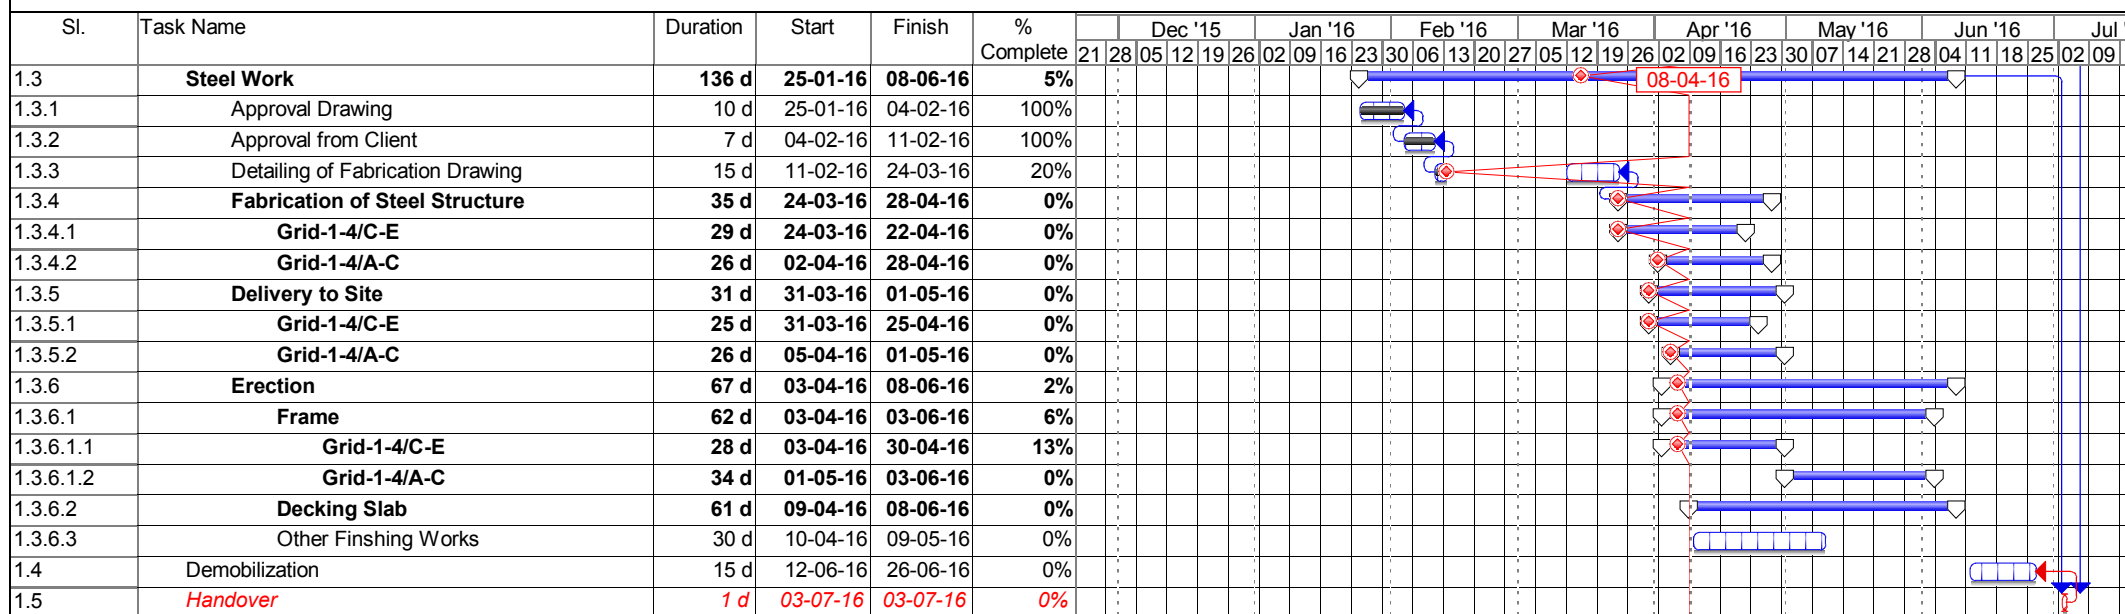

Date: 09-04-16 6:00 PM
Sheet:2 /2

Task



Summary



Rolled Up Progress



Critical Task



Rolled Up Task



Project Summary



Progress




Rolled Up Critical Task



Group By Summary



PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA

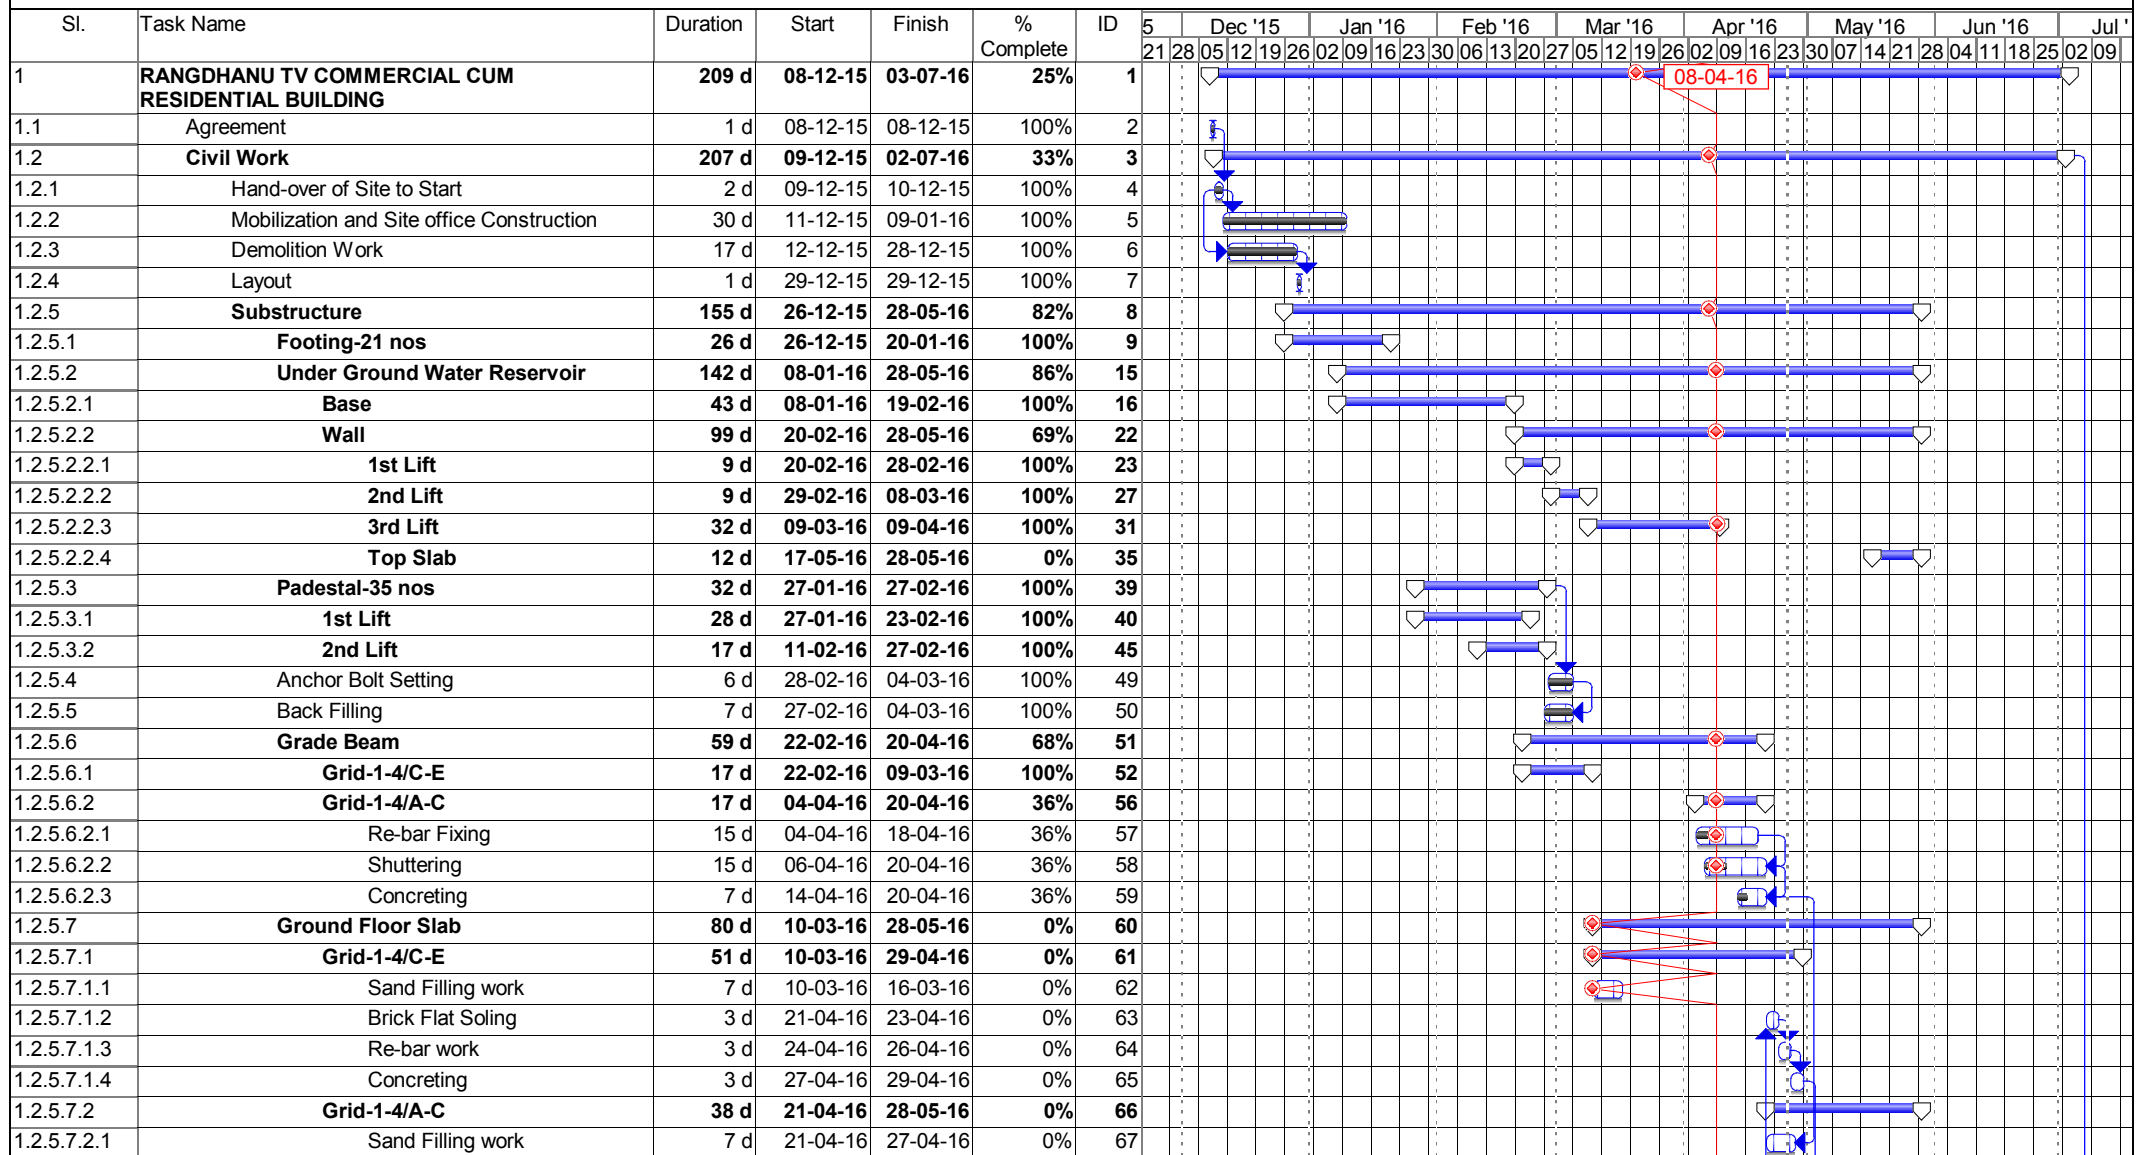

Date: 26-04-16 1:08 PM
Sheet:1 /9

Task



Summary



Rolled Up Progress



Critical Task



Rolled Up Task



Project Summary



Progress



Rolled Up Critical Task



Group By Summary



PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA

Sl.	Task Name	Duration	Start	Finish	% Complete	ID	5	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09
1.2.5.7.2.2	Brick Flat Soling	3 d	20-05-16	22-05-16	0%	68																																			
1.2.5.7.2.3	Re-bar work	3 d	23-05-16	25-05-16	0%	69																																			
1.2.5.7.2.4	Concreting	3 d	26-05-16	28-05-16	0%	70																																			
1.2.6	Super Structure	60 d	14-04-16	12-06-16	0%	71																																			
1.2.6.1	Grid-1-4/C-E	26 d	14-04-16	09-05-16	0%	72																																			
1.2.6.1.1	1st Floor Bontek Slab	4 d	14-04-16	17-04-16	0%	73																																			
1.2.6.1.1.1	Rebar	3 d	14-04-16	16-04-16	0%	74																																			
1.2.6.1.1.2	Concreting	2 d	16-04-16	17-04-16	0%	75																																			
1.2.6.1.2	2nd Floor Bontek Slab	4 d	15-04-16	18-04-16	0%	76																																			
1.2.6.1.2.1	Rebar	3 d	15-04-16	17-04-16	0%	77																																			
1.2.6.1.2.2	Concreting	2 d	17-04-16	18-04-16	0%	78																																			
1.2.6.1.3	3rd Floor Bontek Slab	4 d	19-04-16	22-04-16	0%	79																																			
1.2.6.1.3.1	Rebar	3 d	19-04-16	21-04-16	0%	80																																			
1.2.6.1.3.2	Concreting	2 d	21-04-16	22-04-16	0%	81																																			
1.2.6.1.4	4th Floor Bontek Slab	4 d	20-04-16	23-04-16	0%	82																																			
1.2.6.1.4.1	Rebar	3 d	20-04-16	22-04-16	0%	83																																			
1.2.6.1.4.2	Concreting	2 d	22-04-16	23-04-16	0%	84																																			
1.2.6.1.5	5th Floor Bontek Slab	4 d	25-04-16	28-04-16	0%	85																																			
1.2.6.1.5.1	Rebar	3 d	25-04-16	27-04-16	0%	86																																			
1.2.6.1.5.2	Concreting	2 d	27-04-16	28-04-16	0%	87																																			
1.2.6.1.6	6th Floor Bontek Slab	4 d	26-04-16	29-04-16	0%	88																																			
1.2.6.1.6.1	Rebar	3 d	26-04-16	28-04-16	0%	89																																			
1.2.6.1.6.2	Concreting	2 d	28-04-16	29-04-16	0%	90																																			
1.2.6.1.7	7th Floor Bontek Slab	4 d	01-05-16	04-05-16	0%	91																																			
1.2.6.1.7.1	Rebar	3 d	01-05-16	03-05-16	0%	92																																			
1.2.6.1.7.2	Concreting	2 d	03-05-16	04-05-16	0%	93																																			
1.2.6.1.8	8th Floor Bontek Slab	4 d	02-05-16	05-05-16	0%	94																																			
1.2.6.1.8.1	Rebar	3 d	02-05-16	04-05-16	0%	95																																			
1.2.6.1.8.2	Concreting	2 d	04-05-16	05-05-16	0%	96																																			
1.2.6.1.9	9th Floor Bontek Slab	4 d	04-05-16	07-05-16	0%	97																																			
1.2.6.1.9.1	Rebar	3 d	04-05-16	06-05-16	0%	98																																			
1.2.6.1.9.2	Concreting	2 d	06-05-16	07-05-16	0%	99																																			
1.2.6.1.10	Roof Top Bontek Slab	4 d	06-05-16	09-05-16	0%	100																																			
1.2.6.1.10.1	Rebar	3 d	06-05-16	08-05-16	0%	101																																			
1.2.6.1.10.2	Concreting	2 d	08-05-16	09-05-16	0%	102																																			
1.2.6.2	Grid-1-4/A-C	31 d	13-05-16	12-06-16	0%	103																																			

Date: 26-04-16 1:08 PM
Sheet:2 /9

Task



Summary



Rolled Up Progress



Critical Task



Rolled Up Task



Project Summary



Progress



Rolled Up Critical Task



Group By Summary



**PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM
RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA**

[illegible]

Date: 26-04-16 1:08 PM
Sheet:3 /9

Progress



Rolled Up Critical Task



Group By Summary



**PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM
RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA**

Sl.	Task Name	Duration	Start	Finish	% Complete	ID	5	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09
1.2.7.1.2.1	Brick Work	15 d	19-04-16	03-05-16	0%	140																																			
1.2.7.1.2.2	Plaster	10 d	01-05-16	10-05-16	0%	141																																			
1.2.7.1.3	2nd Floor	22 d	23-04-16	14-05-16	0%	142																																			
1.2.7.1.3.1	Brick Work	15 d	23-04-16	07-05-16	0%	143																																			
1.2.7.1.3.2	Plaster	10 d	05-05-16	14-05-16	0%	144																																			
1.2.7.1.4	3rd Floor	22 d	24-04-16	15-05-16	0%	145																																			
1.2.7.1.4.1	Brick Work	15 d	24-04-16	08-05-16	0%	146																																			
1.2.7.1.4.2	Plaster	10 d	06-05-16	15-05-16	0%	147																																			
1.2.7.1.5	4th Floor	22 d	29-04-16	20-05-16	0%	148																																			
1.2.7.1.5.1	Brick Work	15 d	29-04-16	13-05-16	0%	149																																			
1.2.7.1.5.2	Plaster	10 d	11-05-16	20-05-16	0%	150																																			
1.2.7.1.6	5th Floor	22 d	30-04-16	21-05-16	0%	151																																			
1.2.7.1.6.1	Brick Work	15 d	30-04-16	14-05-16	0%	152																																			
1.2.7.1.6.2	Plaster	10 d	12-05-16	21-05-16	0%	153																																			
1.2.7.1.7	6th Floor	27 d	05-05-16	31-05-16	0%	154																																			
1.2.7.1.7.1	Brick Work	20 d	05-05-16	24-05-16	0%	155																																			
1.2.7.1.7.2	Plaster	10 d	22-05-16	31-05-16	0%	156																																			
1.2.7.1.8	7th Floor	27 d	06-05-16	01-06-16	0%	157																																			
1.2.7.1.8.1	Brick Work	20 d	06-05-16	25-05-16	0%	158																																			
1.2.7.1.8.2	Plaster	10 d	23-05-16	01-06-16	0%	159																																			
1.2.7.1.9	8th Floor	27 d	08-05-16	03-06-16	0%	160																																			
1.2.7.1.9.1	Brick Work	20 d	08-05-16	27-05-16	0%	161																																			
1.2.7.1.9.2	Plaster	10 d	25-05-16	03-06-16	0%	162																																			
1.2.7.1.10	9th Floor	27 d	10-05-16	05-06-16	0%	163																																			
1.2.7.1.10.1	Brick Work	20 d	10-05-16	29-05-16	0%	164																																			
1.2.7.1.10.2	Plaster	10 d	27-05-16	05-06-16	0%	165																																			
1.2.7.2	Grid-1-4/A-C	47 d	17-05-16	02-07-16	0%	166																																			
1.2.7.2.1	Ground Floor	27 d	17-05-16	12-06-16	0%	167																																			
1.2.7.2.1.1	Brick Work	20 d	17-05-16	05-06-16	0%	168																																			
1.2.7.2.1.2	Plaster	10 d	03-06-16	12-06-16	0%	169																																			
1.2.7.2.2	1st Floor	22 d	19-05-16	09-06-16	0%	170																																			
1.2.7.2.2.1	Brick Work	15 d	19-05-16	02-06-16	0%	171																																			
1.2.7.2.2.2	Plaster	10 d	31-05-16	09-06-16	0%	172																																			
1.2.7.2.3	2nd Floor	22 d	24-05-16	14-06-16	0%	173																																			
1.2.7.2.3.1	Brick Work	15 d	24-05-16	07-06-16	0%	174																																			
1.2.7.2.3.2	Plaster	10 d	05-06-16	14-06-16	0%	175																																			

Date: 26-04-16 1:08 PM
Sheet:4 /9

Task



Summary



Rolled Up Progress



Critical Task



Rolled Up Task



Project Summary



Progress



Rolled Up Critical Task



Group By Summary



**PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM
RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA**

Sl.	Task Name	Duration	Start	Finish	% Complete	ID	5 21	Dec '15 28	05 12	19 26	Jan '16 02	09 16	23 30	Feb '16 06 13	20 27	Mar '16 05 12	19 26	Apr '16 02 09	16 23	May '16 30 07	14 21	Jun '16 28 04	11 18	25 02	Jul '16 09
1.2.7.2.4	3rd Floor	22 d	26-05-16	16-06-16	0%	176												08-04-16							
1.2.7.2.4.1	Brick Work	15 d	26-05-16	09-06-16	0%	177																			
1.2.7.2.4.2	Plaster	10 d	07-06-16	16-06-16	0%	178																			
1.2.7.2.5	4th Floor	22 d	31-05-16	21-06-16	0%	179																			
1.2.7.2.5.1	Brick Work	15 d	31-05-16	14-06-16	0%	180																			
1.2.7.2.5.2	Plaster	10 d	12-06-16	21-06-16	0%	181																			
1.2.7.2.6	5th Floor	22 d	02-06-16	23-06-16	0%	182																			
1.2.7.2.6.1	Brick Work	15 d	02-06-16	16-06-16	0%	183																			
1.2.7.2.6.2	Plaster	10 d	14-06-16	23-06-16	0%	184																			
1.2.7.2.7	6th Floor	26 d	07-06-16	02-07-16	0%	185																			
1.2.7.2.7.1	Brick Work	19 d	07-06-16	25-06-16	0%	186																			
1.2.7.2.7.2	Plaster	10 d	23-06-16	02-07-16	0%	187																			
1.2.7.2.8	7th Floor	24 d	09-06-16	02-07-16	0%	188																			
1.2.7.2.8.1	Brick Work	17 d	09-06-16	25-06-16	0%	189																			
1.2.7.2.8.2	Plaster	10 d	23-06-16	02-07-16	0%	190																			
1.2.7.2.9	8th Floor	21 d	12-06-16	02-07-16	0%	191																			
1.2.7.2.9.1	Brick Work	14 d	12-06-16	25-06-16	0%	192																			
1.2.7.2.9.2	Plaster	10 d	23-06-16	02-07-16	0%	193																			
1.2.7.2.10	9th Floor	20 d	13-06-16	02-07-16	0%	194																			
1.2.7.2.10.1	Brick Work	15 d	13-06-16	27-06-16	0%	195																			
1.2.7.2.10.2	Plaster	10 d	23-06-16	02-07-16	0%	196																			
1.2.7.3	Water Proofing in Roof	15 d	18-06-16	02-07-16	0%	197																			
1.2.7.4	Sedimentation Tank	20 d	13-06-16	02-07-16	0%	198																			
1.3	Steel Work	136 d	25-01-16	08-06-16	5%	199																			
1.3.1	Approval Drawing	10 d	25-01-16	04-02-16	100%	200																			
1.3.2	Approval from Client	7 d	04-02-16	11-02-16	100%	201																			
1.3.3	Detailing of Fabrication Drawing	15 d	11-02-16	24-03-16	20%	202																			
1.3.4	Fabrication of Steel Structure	35 d	24-03-16	28-04-16	0%	203																			
1.3.4.1	Grid-1-4/C-E	29 d	24-03-16	22-04-16	0%	204																			
1.3.4.1.1	Column-1st Splice	7 d	24-03-16	31-03-16	0%	205																			
1.3.4.1.2	Beam-1st Floor	7 d	24-03-16	31-03-16	0%	206																			
1.3.4.1.3	Beam-2nd Floor	7 d	24-03-16	31-03-16	0%	207																			
1.3.4.1.4	Column-2nd Splice	7 d	29-03-16	05-04-16	0%	208																			
1.3.4.1.5	Beam-3rd Floor	7 d	29-03-16	05-04-16	0%	209																			
1.3.4.1.6	Beam-4th Floor	7 d	29-03-16	05-04-16	0%	210																			
1.3.4.1.7	Column-3rd Splice	7 d	03-04-16	10-04-16	0%	211																			

Date: 26-04-16 1:08 PM
Sheet:5 /9

Task



Summary



Rolled Up Progress



Critical Task



Rolled Up Task



Project Summary



Progress



Rolled Up Critical Task



Group By Summary



**PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM
RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA**

[illegible]

Date: 26-04-16 1:08 PM
Sheet:6 /9



**PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM
RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA**

Sl.	Task Name	Duration	Start	Finish	% Complete	ID	5		Dec '15					Jan '16					Feb '16					Mar '16					Apr '16					May '16					Jun '16					Jul '16																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
							21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
1.3.5.1.11	Beam-7th Floor	3 d	16-04-16	19-04-16	0%	248																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													

Date: 26-04-16 1:08 PM
Sheet: 7 / 9

**PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM
RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA**

Sl.	Task Name	Duration	Start	Finish	% Complete	ID	5 21	Dec '15 28	05 12	19 26	Jan '16 02	09 16	23 30	Feb '16 06	13 20	27	Mar '16 05	12 19	26	Apr '16 02	09 16	23 30	May '16 07	14	21	28	Jun '16 04	11	18	25	Jul '16 02
1.3.6.1.1.13	Column-5th Splice	2 d	25-04-16	26-04-16	0%	284														08-04-16											
1.3.6.1.1.14	Beam-9th Floor	2 d	27-04-16	28-04-16	0%	285																									
1.3.6.1.1.15	Beam-Roof Top	2 d	29-04-16	30-04-16	0%	286																									
1.3.6.1.2	Grid-1-4/A-C	34 d	01-05-16	03-06-16	0%	287																									
1.3.6.1.2.1	Column-1st Splice	3 d	01-05-16	03-05-16	0%	288																									
1.3.6.1.2.2	Beam-1st Floor	2 d	04-05-16	05-05-16	0%	289																									
1.3.6.1.2.3	Beam-2nd Floor	2 d	06-05-16	07-05-16	0%	290																									
1.3.6.1.2.4	Column-2nd Splice	3 d	08-05-16	10-05-16	0%	291																									
1.3.6.1.2.5	Beam-3rd Floor	2 d	11-05-16	12-05-16	0%	292																									
1.3.6.1.2.6	Beam-4th Floor	2 d	13-05-16	14-05-16	0%	293																									
1.3.6.1.2.7	Column-3rd Splice	3 d	15-05-16	17-05-16	0%	294																									
1.3.6.1.2.8	Beam-5th Floor	2 d	18-05-16	19-05-16	0%	295																									
1.3.6.1.2.9	Beam-6th Floor	2 d	20-05-16	21-05-16	0%	296																									
1.3.6.1.2.10	Column-4th Splice	3 d	22-05-16	24-05-16	0%	297																									
1.3.6.1.2.11	Beam-7th Floor	2 d	25-05-16	26-05-16	0%	298																									
1.3.6.1.2.12	Beam-8th Floor	2 d	27-05-16	28-05-16	0%	299																									
1.3.6.1.2.13	Column-5th Splice	3 d	29-05-16	31-05-16	0%	300																									
1.3.6.1.2.14	Beam-9th Floor	2 d	01-06-16	02-06-16	0%	301																									
1.3.6.1.2.15	Beam-Roof Top	1 d	03-06-16	03-06-16	0%	302																									
1.3.6.2	Decking Slab	61 d	09-04-16	08-06-16	0%	303																									
1.3.6.2.1	Grid-1-4/C-E	27 d	09-04-16	05-05-16	0%	304																									
1.3.6.2.1.1	1st Floor	5 d	09-04-16	13-04-16	0%	305																									
1.3.6.2.1.2	2nd Floor	5 d	10-04-16	14-04-16	0%	306																									
1.3.6.2.1.3	3rd Floor	5 d	14-04-16	18-04-16	0%	307																									
1.3.6.2.1.4	4th Floor	5 d	15-04-16	19-04-16	0%	308																									
1.3.6.2.1.5	5th Floor	5 d	20-04-16	24-04-16	0%	309																									
1.3.6.2.1.6	6th Floor	5 d	21-04-16	25-04-16	0%	310																									
1.3.6.2.1.7	7th Floor	5 d	26-04-16	30-04-16	0%	311																									
1.3.6.2.1.8	8th Floor	5 d	27-04-16	01-05-16	0%	312																									
1.3.6.2.1.9	9th Floor	3 d	01-05-16	03-05-16	0%	313																									
1.3.6.2.1.10	Roof Top	3 d	03-05-16	05-05-16	0%	314																									
1.3.6.2.2	Grid-1-4/A-C	32 d	08-05-16	08-06-16	0%	315																									
1.3.6.2.2.1	1st Floor	5 d	08-05-16	12-05-16	0%	316																									
1.3.6.2.2.2	2nd Floor	5 d	10-05-16	14-05-16	0%	317																									
1.3.6.2.2.3	3rd Floor	5 d	15-05-16	19-05-16	0%	318																									
1.3.6.2.2.4	4th Floor	5 d	17-05-16	21-05-16	0%	319																									

Date: 26-04-16 1:08 PM
Sheet:8 /9

Progress



Rolled Up Critical Task



Group By Summary



**PROGRAM (REV-3.0) AND PROGRESS OF CONSTRUCTION OF G+8-STORIED COMERCIAL CUM
RESIDENTIAL BUILDING FOR RANGDHANU MEDIA LTD. AT GULSHAN, DHAKA**

[illegible]

Date: 26-04-16 1:08 PM
Sheet: 9 / 9

Task	
Critical Task	
Progress	

Summary	
Rolled Up Task	
Rolled Up Critical Task	

Rolled Up Progress	
Project Summary	
Group By Summary	
