

WEEKLY PROJECT REPORT-044



AS ON 18 JUL 2012

PROJECT SUMMARY AS ON: 18 JUL 2012

- Program is 91 days delayed from master program as on 18th Jul 2012. Still delay time is increasing and 11 days more lag in 10th floor roof slab casting. But it should be controlled.
- Still no signature by MEP in Work Inspection Request (WIR) before slab casting.
- Manpower is same as before.
- An incident was happened and a safety precaution was taken immediately to protect same incident in future.

WEEKLY CHECK-LIST FOR PROGRAM AS ON: 18-07-2012



Name of Sub-Contractor:	Sohel Enterprise
-------------------------	------------------

WBS					
Task Name	12 th floor slab and beam casting Complete				
Schedule Finish	12/04/2012	Actual Finish:	12/07/2012	Time Lag:	91
Causes of Delay					

WBS					
Task Name	12 th Floor slab & Beam Shuttering complete				
Actual Start		Actual Finish:	11/07/2012	Time Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

Remarks: (Penalty/ Award) to be filled by Project Incharge

Suuggestion/ Advice:

Slab casting is delayed 91 days from master program which is 11 days more delay from previous slab.

Consultant


Chief Engineer

Project Incharge

Chief Engineer

Director

Delay of Roof Slab Casting

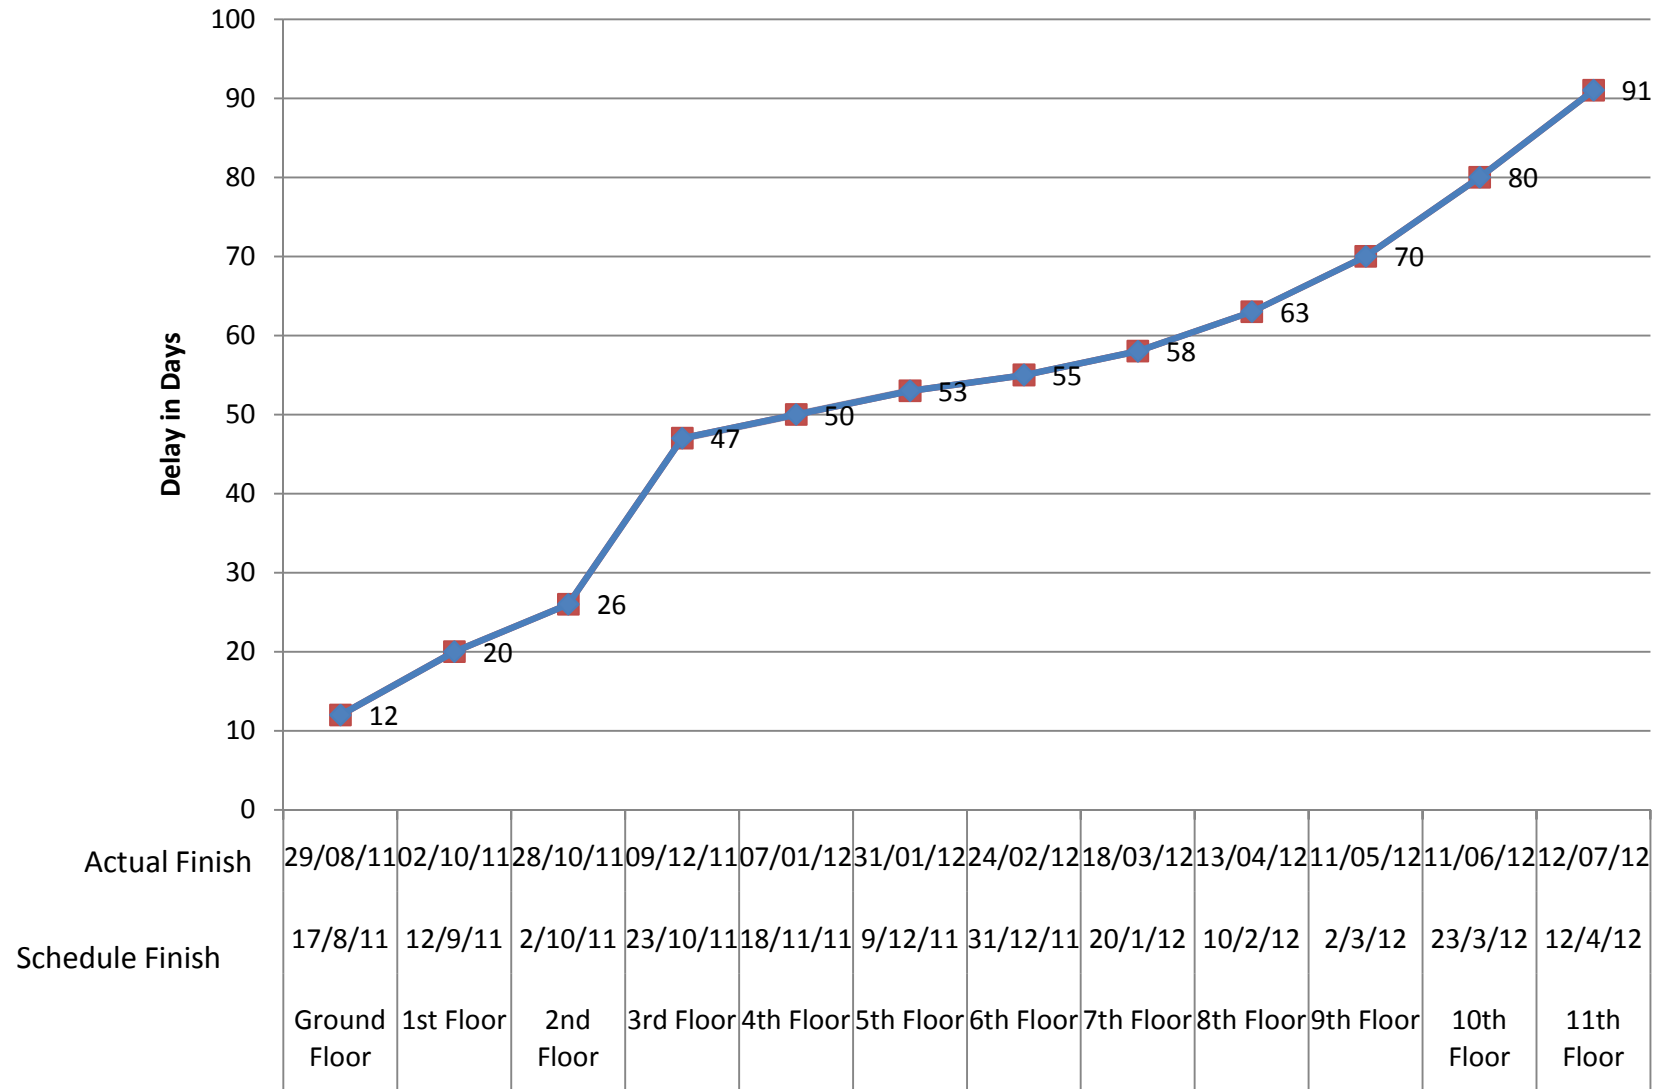

Ekushey Bhaban-Superstructure-Progress

Sl.	Task Name	Duration	Start	Finish	Actual Finish	% Compl	'12	Apr '12	May '12	Jun '12	Jul '12	Aug '12	Sep '12	Oct '12	Nov '12
							1/08/05/01/08/05/02/09/06/03/00/07/03/00/07/04/01/08/05/02/09/05/02/09/06/02/09/06/03/00/07/14/11/18/14/11/18/15/1								
1	Ekushey Bhaban	442 d	28/07/11	18/11/12	NA	6%						18/07/12			
1.1	Superstructure	300 d	28/07/11	14/06/12	NA	85%									
1.1.1	Ground Floor	20 d	28/07/11	17/08/11	29/08/11	100%									
1.1.2	1st Floor	20 d	18/08/11	12/09/11	02/10/11	100%									
1.1.3	2nd Floor	20 d	13/09/11	02/10/11	28/10/11	100%									
1.1.4	3rd Floor	20 d	03/10/11	23/10/11	09/12/11	100%									
1.1.5	4th Floor	20 d	24/10/11	18/11/11	07/01/12	100%									
1.1.6	5th Floor	20 d	19/11/11	09/12/11	31/01/12	100%									
1.1.7	6th Floor	20 d	10/12/11	31/12/11	24/02/12	100%									
1.1.8	7th Floor	20 d	01/01/12	20/01/12	18/03/12	100%									
1.1.9	8th Floor	20 d	21/01/12	10/02/12	18/04/12	100%									
1.1.10	9th Floor	20 d	11/02/12	02/03/12	11/05/12	100%									
1.1.11	10th Floor	20 d	03/03/12	23/03/12	11/06/12	100%									
1.1.12	11th Floor	20 d	24/03/12	12/04/12	12/07/12	100%									
1.1.12.1	Layout Work	1 d	24/03/12	24/03/12	NA	100%									
1.1.12.2	Column (17 nos): Lift-1	4 d	25/03/12	28/03/12	NA	100%									
1.1.12.3	Column (17 nos): Lift-2	4 d	29/03/12	01/04/12	NA	100%									
1.1.12.4	Lift Core: Lift-1	5 d	25/03/12	29/03/12	NA	100%									
1.1.12.5	Lift Core: Lift-2	4 d	30/03/12	02/04/12	NA	100%									
1.1.12.6	Stair Case (2 nos)-Flight-1	8 d	26/03/12	02/04/12	NA	100%									
1.1.12.7	Stair Case (2 nos)-Flight-2	8 d	05/04/12	12/04/12	NA	100%									
1.1.12.8	Roof Slab	10 d	03/04/12	12/04/12	NA	100%									
1.1.12.8.1	Formwork	5 d	03/04/12	07/04/12	11/07/12	100%									
1.1.12.8.2	Re-bar	3 d	08/04/12	10/04/12	NA	100%									
1.1.12.8.3	MEP Work	2 d	10/04/12	11/04/12	NA	100%									
1.1.12.8.4	Inspection	1 d	11/04/12	11/04/12	NA	100%									
1.1.12.8.5	Concrete	1 d	12/04/12	12/04/12	12/07/12	100%									
1.1.13	12th Floor	20 d	13/04/12	04/05/12	NA	39%									
1.1.13.1	Layout Work	1 d	13/04/12	13/04/12	NA	100%									
1.1.13.2	Column (17 nos): Lift-1	4 d	15/04/12	18/04/12	NA	100%									
1.1.13.2.1	Re-bar	1 d	15/04/12	15/04/12	NA	100%									
1.1.13.2.2	Formwork	2 d	16/04/12	17/04/12	NA	100%									
1.1.13.2.3	Concrete	1 d	18/04/12	18/04/12	NA	100%									
1.1.13.3	Column (17 nos): Lift-2	4 d	19/04/12	22/04/12	NA	0%									
1.1.13.3.1	Re-bar	1 d	19/04/12	19/04/12	NA	0%									
1.1.13.3.2	Formwork	2 d	20/04/12	21/04/12	NA	0%									
1.1.13.3.3	Concrete	1 d	22/04/12	22/04/12	NA	0%									
1.1.13.4	Lift Core: Lift-1	5 d	15/04/12	19/04/12	NA	100%									
1.1.13.4.1	Re-bar	2 d	15/04/12	16/04/12	NA	100%									
1.1.13.4.2	Formwork	2 d	17/04/12	18/04/12	NA	100%									

Project: Ekushey Bhaban - Superstruc
Date: 06/10/12

Task

Critical Task

Progress



Summary



Rolled Up Task



Rolled Up Critical Task



Rolled Up Progress



Project Summary



Group By Summary



WEEEEKLY CHECK-LIST FOR **QUALITY** AS ON: 18-07-2012

CITYSCAPE 

Name of Sub-contractor:

Sohel Enterprise

Remarks on Shuttering: (Attach Photograph) to be filled by Project Incharge

Remarks on Re-bar Work: (Attach Photograph) to be filled by Project Incharge

Remarks on Concreting : (Attach Photograph) to be filled by Project Incharge

Suggestion/ Advice:

WIR attached but no signature of MEP Consultant.

Consultant

Chief Engineer

Project Incharge

Chief Engineer

Director

3018

R & D 0.0, Date of Issue : Nov, 2010 Doc No. CIL R & D WIR 002	CITYSCAPE INTERNATIONAL LIMITED	
--	--	--

WORK INSPECTION REQUEST <small>(To submit by Contractor 48 hours before Concreting)</small>			
Description of Work : <u>12th floor Beam Slab casting work</u>			
Location/ Grid : <u>A to G and</u>	Level : <u>+124</u>	Date of Concreting :	
<small>(A Drawing with Marking/ Highlighting must be submitted)</small>		Time of Concreting : <u>10.07.12</u>	
Submitted By:			
Company : <u>Rasem Tech Limited Schel Enterprise</u>		Signature : <u>Rasem</u>	
Name : <u>Md. Forhad Rahman</u>			
Designation : <u>contractor</u>	Date : <u>10/07/12</u>		

WORK INSPECTION REPORT			
<div style="display: flex; justify-content: space-around;"> Reinforcement <input checked="" type="checkbox"/> OK Formwork <input checked="" type="checkbox"/> OK Proping/Supporting <input checked="" type="checkbox"/> OK </div>			
Comments :			
Inspected By			
Company : <u>Cityscape International Limited</u>		Signature : <u>[Signature]</u>	
Name : <u>Md. Moheddin</u>			
Designation : <u>Engineering</u>	Date : <u>10/07/12</u>		

MEP CLEARANCE			
<div style="display: flex; justify-content: space-around;"> Not Applicable <input type="checkbox"/> Completed <input type="checkbox"/> Not Completed <input type="checkbox"/> </div>			
Clearanced By			
Company : <u>Cityscape International Limited</u>		Signature :	
Name :			
Designation :	Date :		

APPROVAL FOR CONCRETING			
Comments :			
<div style="display: flex; justify-content: space-around;"> Approved <input type="checkbox"/> Approved with Comments <input type="checkbox"/> Not Approved <input type="checkbox"/> </div>			
Inspected By			
Company : <u>Cityscape International Limited</u>		Signature : <u>[Signature]</u>	
Name : <u>Rashid</u>			
Designation : <u>IE</u>	Date : <u>10/7</u>		

WEEKLY CHECK-LIST FOR SAFETY AS ON: 18-07-2012

CITYSCAPE

Name of Sub-Contractor:	Sohel enterprise.
-------------------------	-------------------

List of Safety Materials issued:

Safety Shoe	145	pairs
Helmet	223	nos.
T-shirt	263	nos.

Induction:

Total Labour:		Inducted:	113		
Tool Box Meeting (Weekly Safety Meeting) no.:				Date:	

Safety Violation: (Attach Photograph)

Warning	No. of Persons
1st Warning :	12
2nd Warning with Fine:	3
Termination:	

Safety Award: (Attach Photograph)

Induction ID:		Trade	Cleaner
Name:			

Accidents/ Injury:

--

House Keeping

--

Remarks: to be filled by Project Incharge

--

Suggestion/ Advice:

One incident happened and taking precaution to protect the same incident in future. Picture attached.
_____ Consultant
_____ Chief Engineer

Project Incharge

Chief Engineer

Director

তারিখ: জুলাই ১০, ২০১২

প্রতি

সোহেল এন্টারপ্রাইজ

স্বাধিকারী: মোঃ ফজলুর রহমান

বিষয়: কাজ করতে গিয়ে পাশের বাড়ির লাইট ভাঙ্গা প্রশংগে

অত্যন্ত দুঃখের সাথে জানানো যাচ্ছে যে, আপনার কোম্পানির আওতাধীন গত জুলাই ৯, ২০১২ তারিখে ১২ তম ছাদের এর কাজ করার সময় আপনার কর্মীর কাজে অবহেলার কারনে এক টুকরা রড পাশের হোটেলে এর রাস্তাএ গিয়ে পরে। এতে তাদের একটি লাইট ক্ষতিগ্রস্ত হয়। কাজে অবহেলার কারনে কোন ক্ষয়ক্ষতি হলে তার দায়ভার নেওয়া প্রশংগে এর পূর্বে মে ০২, ২০১২ তারিখে আপনাকে একটি চিঠি দেওয়া হয়েছিল।

অতএব, এ সংক্রান্ত যাবতীয় ক্ষতিপূরণ এর দায় দায়িত্ব আপনাকে বহন করতে হবে যা আপনার বিল এর সাথে সম্বলনয় করা হবে। ক্ষতিগ্রস্তের সাথে ক্ষতিপূরণ এর টাকা মীমাংসা পূর্বক আপনাকে অবহিত করা হবে। আর ভবিষ্যতে এ ধরনের ঘটনা যেন না ঘটে তার ব্যবস্থা নেওয়ার জন্য নির্দেশ দেওয়া হল।

আদেশক্রমে

জি এম (প্রকৌশল)

সিটিস্কেপ ইন্টারন্যাশনাল লিমিটেড

সিটিস্কেপ টাওয়ার



Construction Safety



Taking precaution by extending net 6 feet beyond the existing safety net.

WEEKLY CHECK-LIST FOR **MANPOWER** AS ON: 18-07-2012



Name of Sub-Contractor:	Sohel Enterprise
--------------------------------	------------------

Shuttering Work:

Manpower	Required No.	Present No.	Remarks
Shutter Mistry		120	
Shutter Helper		112	

Re-bar Work:

Manpower	Required No.	Present No.	Remarks
Re-bar Fabricator		30	
Helper		28	

Concrete Work:

Manpower	Required No.	Present No.	Remarks
Mason		12	
Labour			

Housekeeping

Manpower	Required No.	Present No.	Remarks
Labour		28	

Over All Remarks by Project Incharge

Concrete volume = 124.5 m3

Suggestion/ Advice

Manpower is same as before.
_____ Consultant
_____ Chief Engineer

Project Incharge

Chief Engineer

Director

MANPOWER HISTOGRAM

