

CONSTRUCTION OF THE VIEW HOTEL AT KUAKATA

PROGRESS REPORT



21 FEB 2022

Generated by: Cityscape International Limited

TABLE OF CONTENTS

- o TOTAL PROGRESS
- o TOTAL MANPOWER CHART
- o CUMMULATIVE PROGRESS CHART
- o SCHEDULE LEAD-LAG CHART
- o LAST MONTH PROGRESS
 - o LAST MONTH MANPOWER HISTOGRAM
 - o LAST MONTH PROGRESS CHART
 - o DAILY PROGRESS REPORT
- o WORK PLAN AND PROGRESS
- o PROGRESS PHOTO



TOTAL PROGRESS REPORT

From 18-September-2020 to 21-February-2022

Project Code:	58	Name:	The View Hotel Kuakata			
Client:	Sikder Group	Contractor:				
Total Duration:	521	days	Total Working Days:	73	Total Manpower:	6905
Planning Progress =	100%	Actual Progress=	87.1%	SPI=	0.87	Behind Schedule


Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
1.1.01	Take-over Site for Construction		100	18-09-20	18-09-20	18-09-20	18-09-20	0	
2.1.01	Tower-1-Pile Work	301nos	100	19-09-20	07-11-20	05-11-20	06-11-20	1	
2.1.02	Tower-1-Pile Cap	26nos	100	22-10-20	18-12-20	05-11-20	18-12-20	0	
2.1.03	Tower-1-Padestal	31nos	100	07-11-20	23-12-20	28-11-20	21-12-20	2	
2.1.04	Tower-1-Lift Core Below GB	2nos	100	12-12-20	23-12-20	09-12-20	21-12-20	2	
2.1.05	Tower-1-Grade Beam	421rm	100	09-12-20	30-12-20	30-11-20	27-01-21	-28	
2.2.01.1	Tower-1-GF Column	31nos	100	24-12-20	04-01-21	09-12-20	27-01-21	-23	
2.2.01.2	Tower-1-GF-Lift Core	2nos	100	24-12-20	04-01-21	21-12-20	27-01-21	-23	
2.2.01.3	Tower-1-GF-Stair	2nos	100	24-12-20	15-01-21	21-12-20	27-01-21	-12	
2.2.01.4	Tower-1-1st Floor Slab	1505m2	100	10-01-21	20-01-21	15-12-20		0	
2.2.02.1	Tower-1-1st Floor Column	31nos	100	22-01-21	31-01-21	27-12-20	07-02-21	-7	
2.2.02.2	Tower-1-1st Floor Lift Core	2nos	100	02-02-21	07-02-21	05-02-21	07-02-21	0	
2.2.02.3	Tower-1-1st Floor Stair	2nos	100	22-01-21	18-02-21	05-02-21	10-02-21	8	
2.2.02.4	Tower-1-2nd Floor Slab	1672m2	100	08-02-21	18-02-21	08-01-21		0	
2.2.03.1	Tower-1-2nd Floor Column	31nos	100	19-02-21	01-03-21	05-02-21	23-02-21	6	
2.2.03.4	Tower-1-3rd Floor Slab	1672m2	100	01-03-21	11-03-21	16-02-21	28-02-21	11	
2.2.04.1	Tower-1-3rd Floor Column	31nos	100	12-03-21	22-03-21	28-02-21	25-03-21	-3	
2.2.04.2	Tower-1-3rd Floor Lift Core	2nos	100	12-03-21	22-03-21	11-03-21	25-03-21	-3	
2.2.04.3	Tower-1-3rd Floor Stair	2nos	100	12-03-21	02-04-21	11-03-21	01-04-21	1	
2.2.04.4	Tower-1-4th Floor Slab	1672m2	100	23-03-21	02-04-21	11-03-21	01-04-21	1	
2.2.05.1	Tower-1-4th	31nos	50	03-04-21	13-04-21	22-06-21	22-06-21	70	Completed


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
2.2.05.2	Tower-1-4th Floor-Lift Core	2nos		03-04-21	13-04-21			0	Started
2.2.05.3	Tower-1-4th Floor-Stair	2nos		03-04-21	24-04-21			0	Started
2.2.05.4	Tower-1-4th Floor-Roof Beam n Slab	1672m2	7	14-04-21	24-04-21	22-06-21	22-06-21	-59	Completed
3.1.01	Tower-2-Pile Boring	156nos	100	08-11-20	12-12-20	12-11-20	12-12-20	0	
3.1.02	Tower-2-Pile Cap	17nos	100	21-12-20	06-02-21	21-12-20	05-02-21	1	
3.1.03	Tower-2-Short Column	17nos	100	18-01-21	13-02-21	18-01-21	10-02-21	3	
3.1.04	Tower-2-Lift Core below Grade Beam	1nos	100	02-02-21	13-02-21	10-02-21	10-02-21	3	
3.1.05	Tower-2-Grade Beam	192m	100	03-02-21	05-03-21	23-02-21	02-03-21	3	
3.2.01.1	Tower-2-GF Column	17nos	100	05-04-21	15-05-21	13-03-21	25-03-21	51	
3.2.01.2	Tower-2-GF Lift Core	1nos	100	09-04-21	15-04-21	13-03-21	25-03-21	21	
3.2.01.3	Tower-2-GF Stair	1nos	100	09-04-21	26-04-21	25-03-21	19-04-21	7	
3.2.01.4	Tower-2-1st Floor Slab	929m2	100	16-04-21	26-04-21	12-04-21	19-04-21	7	
3.2.02.1	Tower-2-1st Floor-Column	17nos	100	27-04-21	07-05-21	28-04-21	26-09-21	-142	
3.2.02.2	Tower-2-1st Floor-Lift Core	1nos	100	01-05-21	07-05-21	29-04-21	26-09-21	-142	
3.2.02.3	Tower-2-1st Floor-Stair	1nos	100	01-05-21	28-05-21	04-05-21	21-09-21	-116	
3.2.02.4	Tower-2-2nd Floor-Slab	1115m2	100	08-05-21	28-05-21	29-04-21	26-09-21	-121	
3.2.03.1	Tower-2-2nd Floor-Column	17nos	65	02-10-21	12-10-21	30-09-21	21-02-22	-132	Completed
3.2.03.2	Tower-2-2nd Floor-Lift core	1no.	0	06-10-21	12-10-21			0	Started
3.2.03.3	Tower-2-2nd Floor-Stair	1no.	0	16-10-21	02-11-21			0	Started
3.2.03.4	Tower-2-3rd Floor Slab	929m2	30	23-10-21	02-11-21	28-10-21	08-01-22	-67	Completed
4.1	Porch-Short Column	nos	100	21-01-21	29-01-21	27-01-21	27-01-21	2	
4.2	Porch-Grade Beam	m	100	15-01-21	05-02-21	27-01-21	27-01-21	9	
4.3	Porch-Column	nos	100	30-01-21	10-02-21	27-01-21	05-02-21	5	
4.4	Porch-Beam and Slab	107m2	100	11-02-21	18-02-21	07-02-21	07-02-21	11	
5.01.1	Restaurant-GF Double Height Column	12nos	100	28-02-21	10-03-21	28-02-21	25-03-21	-15	
5.01.2	Restaurant-Porch Slab	223m2	100	25-02-21	10-03-21	02-03-21	02-03-21	8	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
5.01.3	Restaurant-GF Double Height Roof Sl	557m2	100	03-03-21	31-03-21	23-03-21	24-04-21	-24	
5.02.1	Restaurant-2nd Floor-Column	12nos	100	01-04-21	11-04-21	19-04-21	16-06-21	-66	
5.02.2	Restaurant-2nd Floor-Roof Slab	836m2	67	04-04-21	02-05-21	24-04-21	16-06-21	-45	Completed
6.1	Between Tower1-2-Short Column	nos	100	09-03-21	15-03-21	13-03-21	13-03-21	2	
6.2	Between Tower1-2-Grade Beam	m	100	16-03-21	29-03-21	25-03-21	25-03-21	4	
6.3	Between Tower1-2-Column	nos	100	30-03-21	12-04-21	11-04-21	11-04-21	1	
6.4	Between Tower1-2-GF Roof Slab	372m2	100	13-04-21	26-04-21	26-04-21	26-04-21	0	
6.5	Between Tower-1-2-1st Flr Roof Slab	372m2	100	27-04-21	10-05-21	05-06-21	05-06-21	-26	
7.1	East Side Soak Well Slab	1no.	100	10-01-22	27-01-22	27-01-22	27-01-22	0	
7.2	West Side Septic Tank	1no.	25	12-01-22	10-02-22	27-01-22	31-01-22	10	Completed
7.3	East Side Septic Tank	1no.	30	21-01-22	19-02-22	27-01-22	10-02-22	9	Completed


DAILY MANPOWER

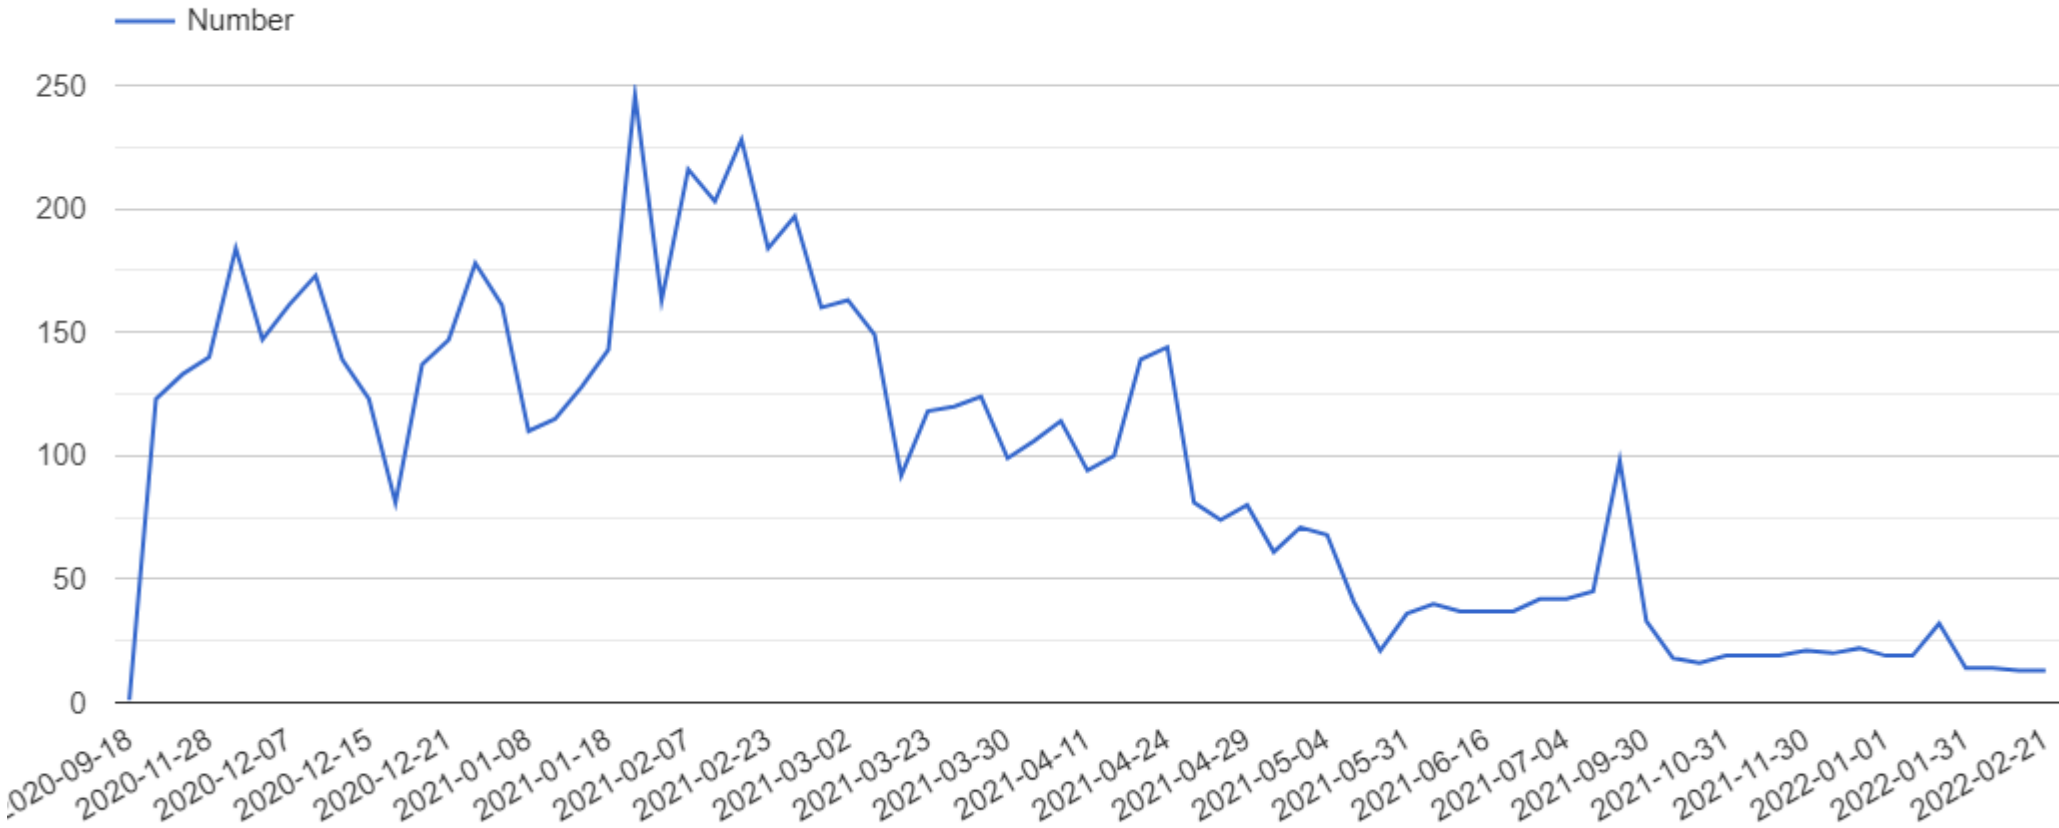


CUMMULATIVE ACTUAL WORK PROGRESS

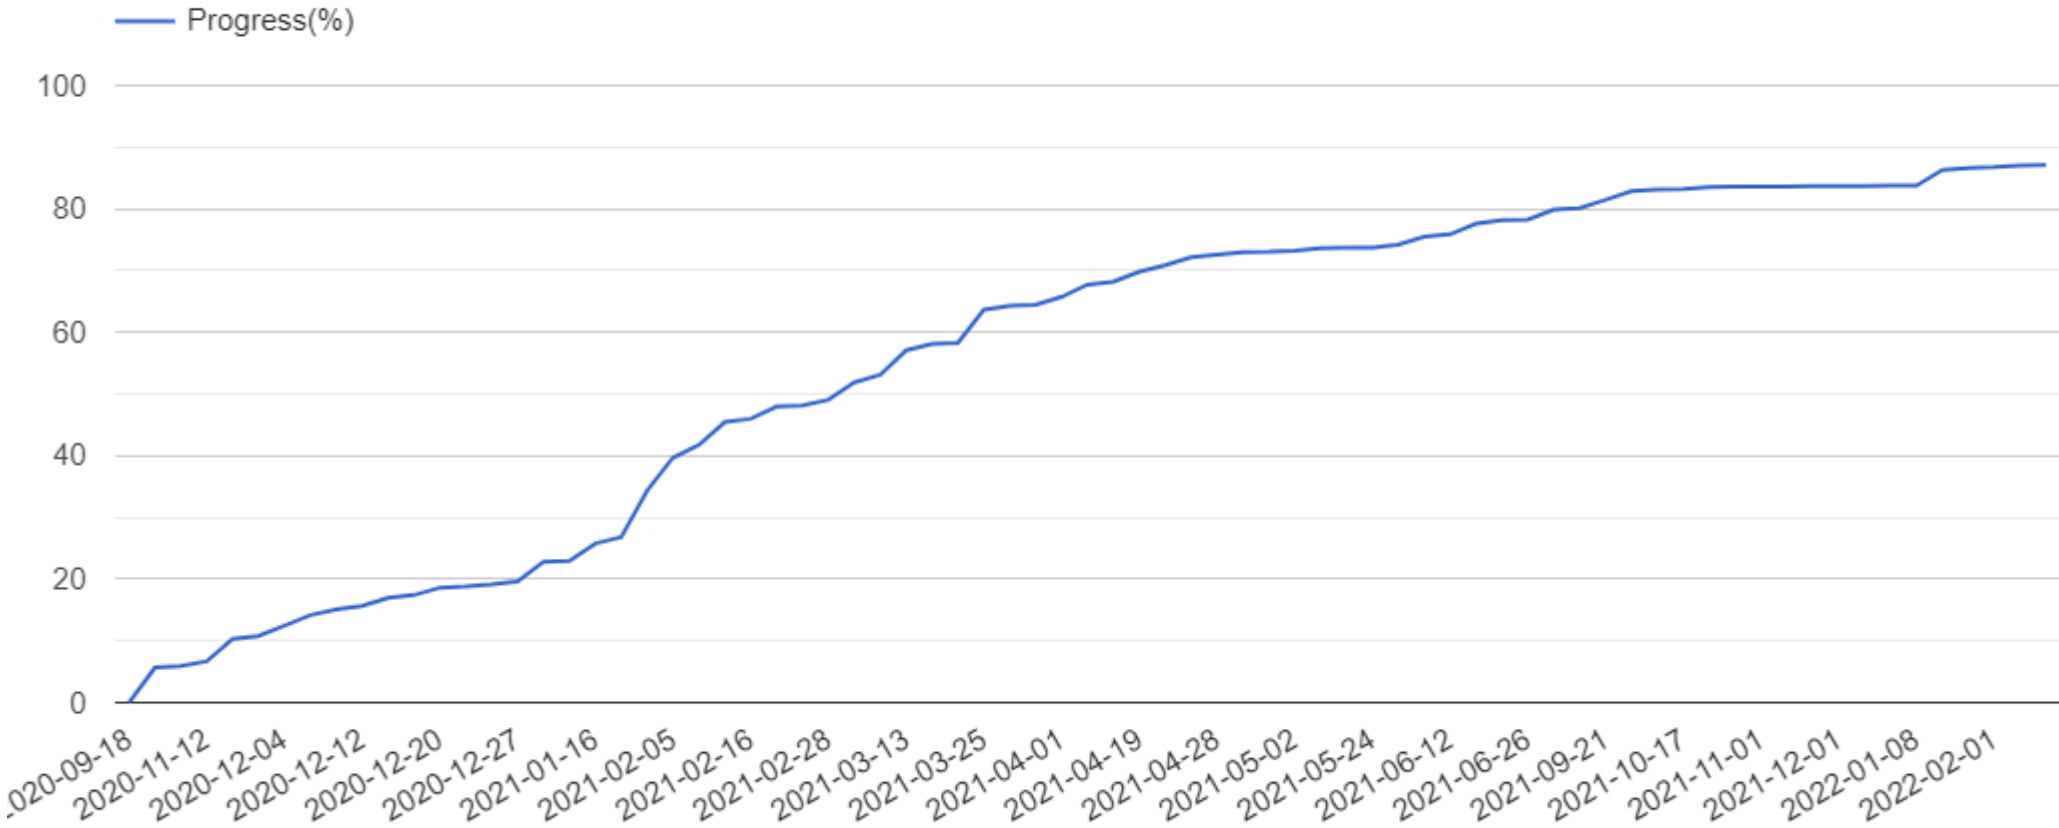


CUMMULATIVE PLAN WORK PROGRESS

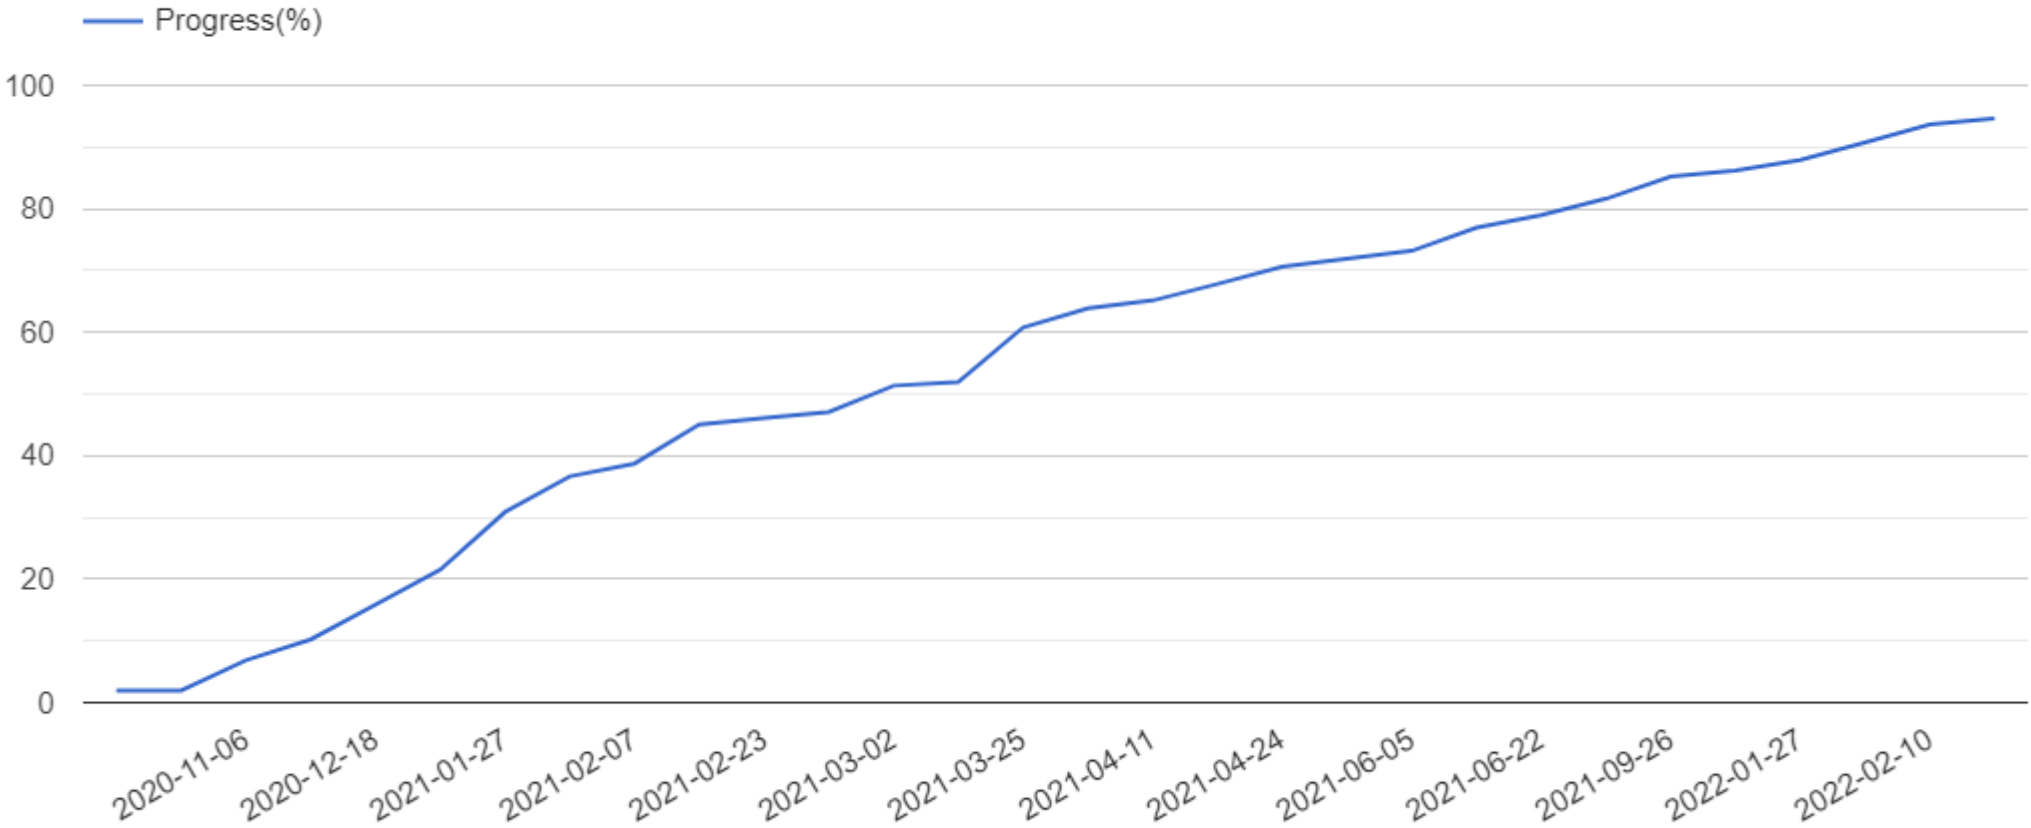

CUMMULATIVE WORK PROGRESS

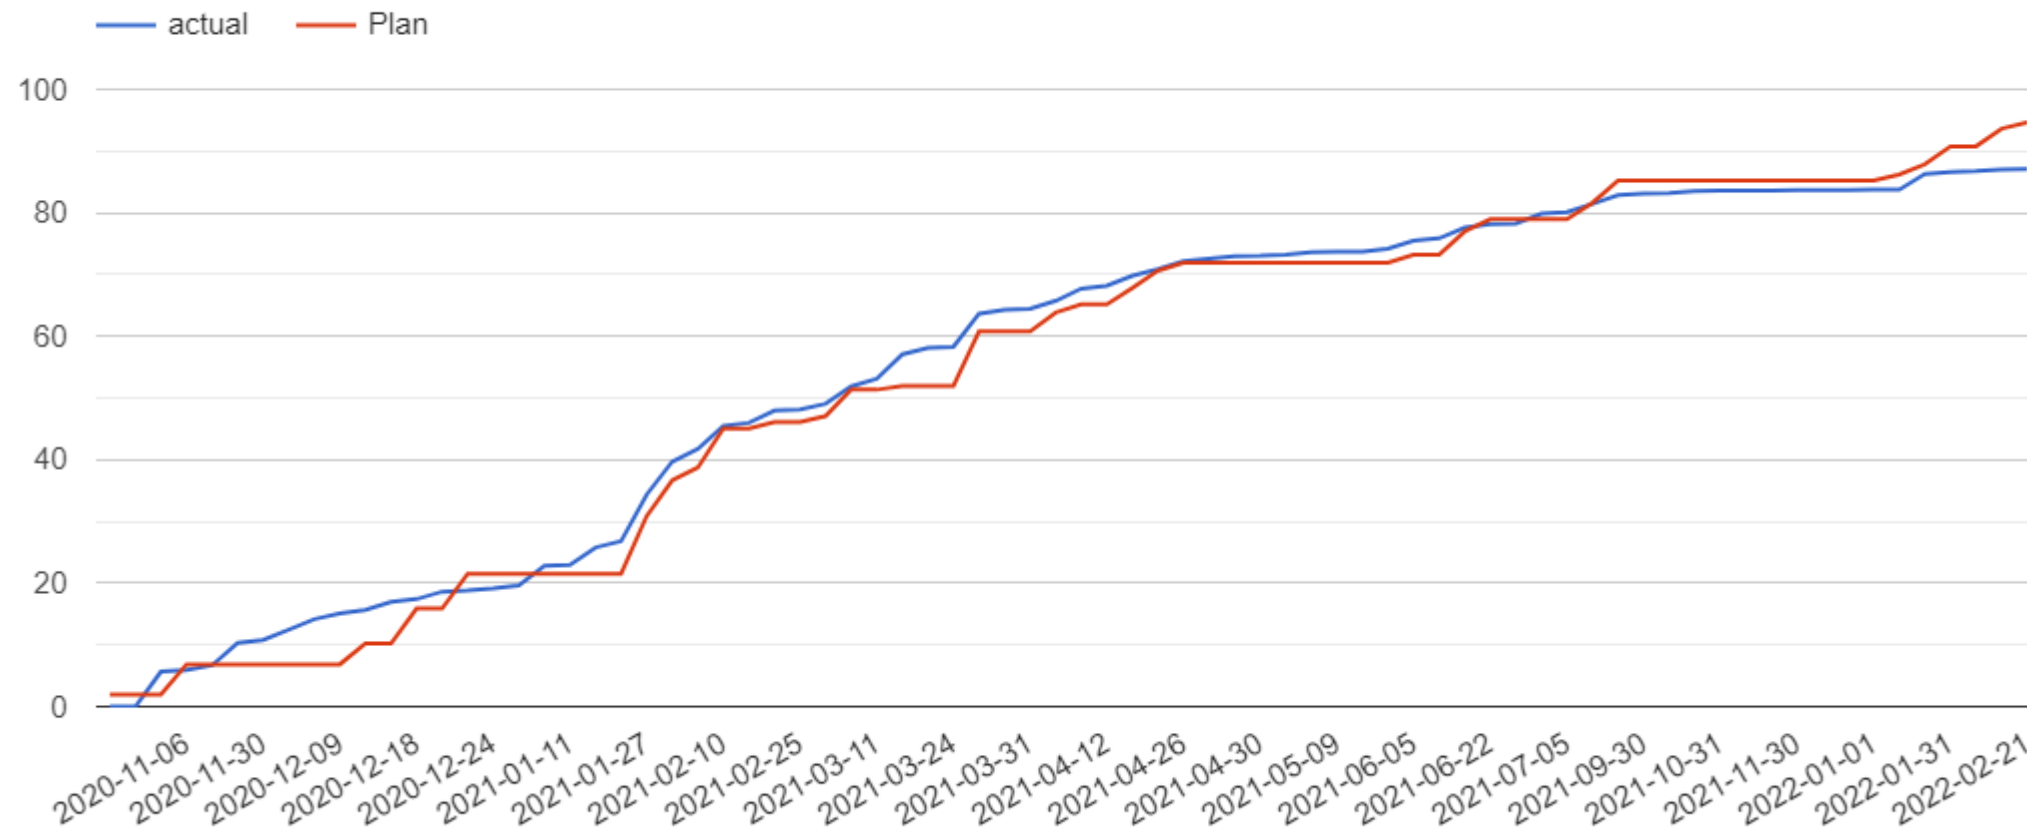

SCHEDULE AHEAD-BEHIND

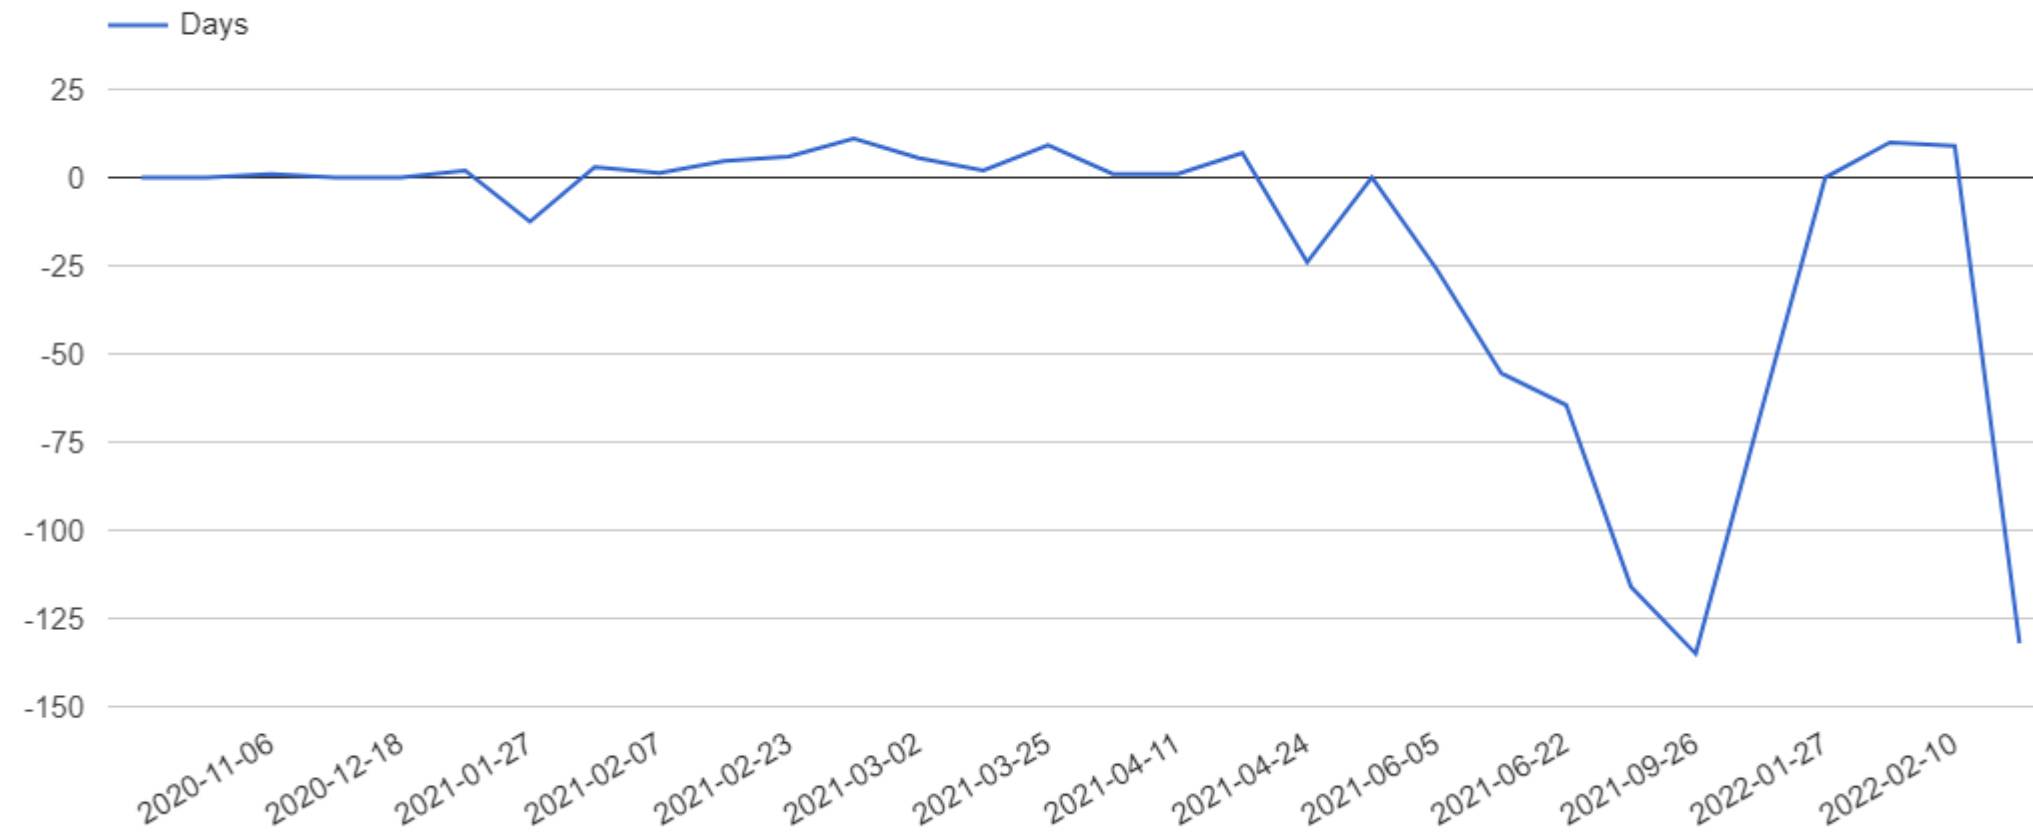

LAST MONTH REPORT
LAST DAY REPORT



MONTHLY PROGRESS REPORT


From 1-February-2022 to 21-February-2022

Project Code:	58	Name:	The View Hotel Kuakata
Client:	Sikder Group	Contractor:	Cityscape International Ltd.


Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
3.2.03.1	Tower-2-2nd Floor-Column	17nos	60	5	65	02-10-21	12-10-21	21-02-22
7.3	East Side Septic Tank	1no.	15	15	30	21-01-22	19-02-22	10-02-22

MANPOWER HISTOGRAM

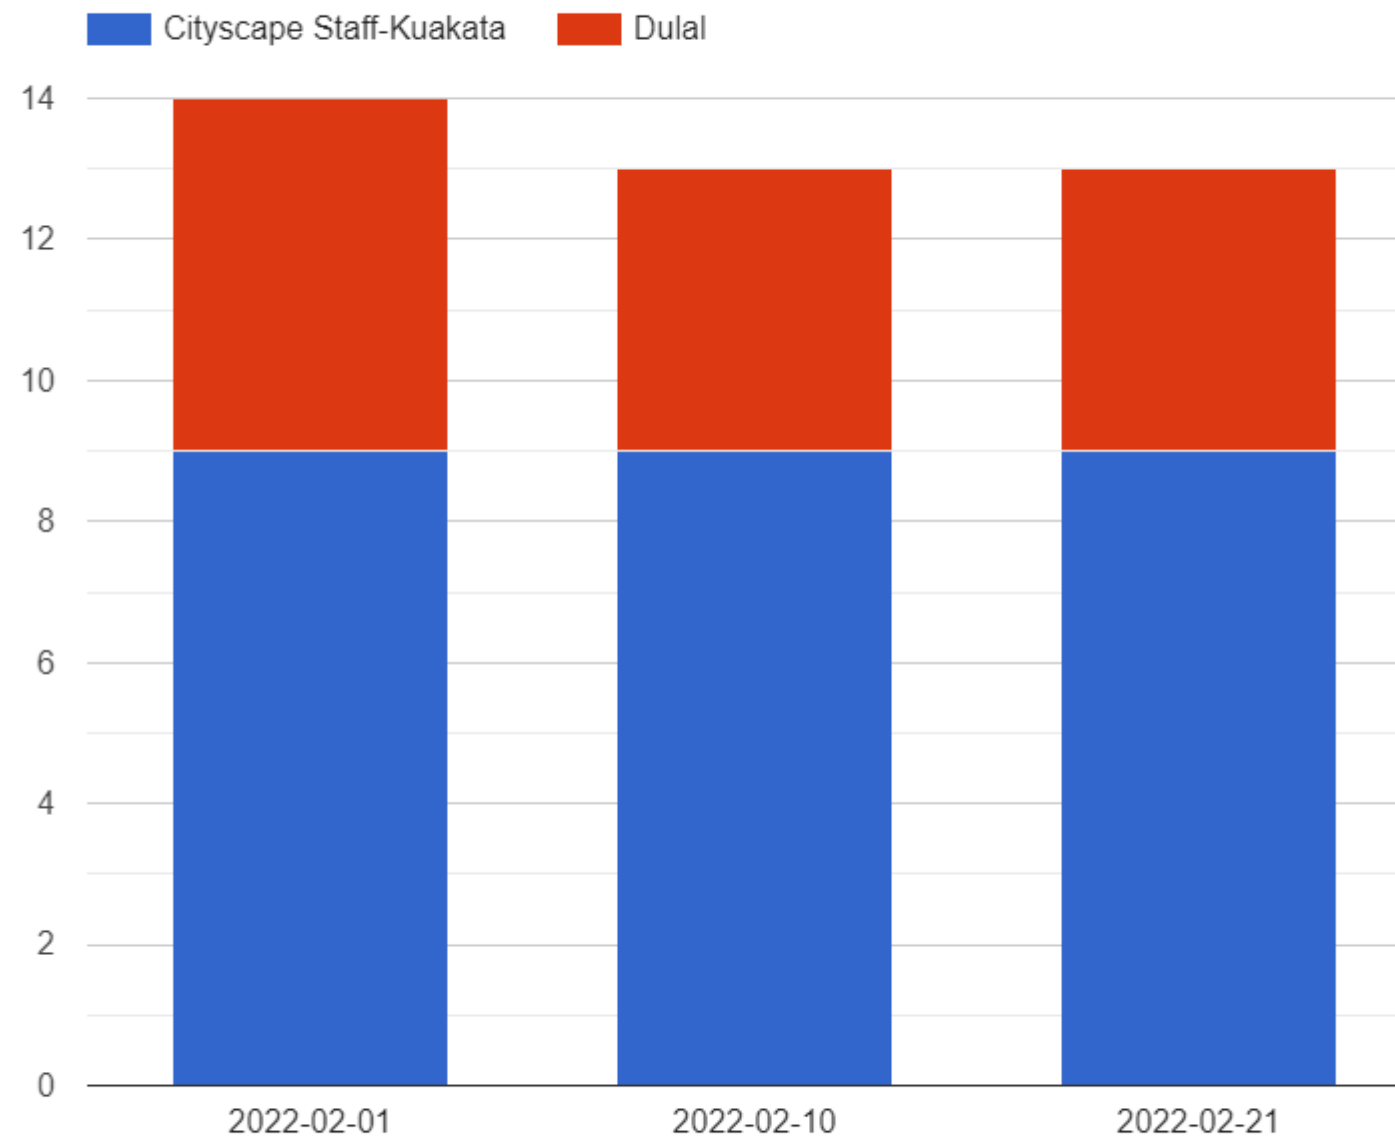

DAILY PROGRESS

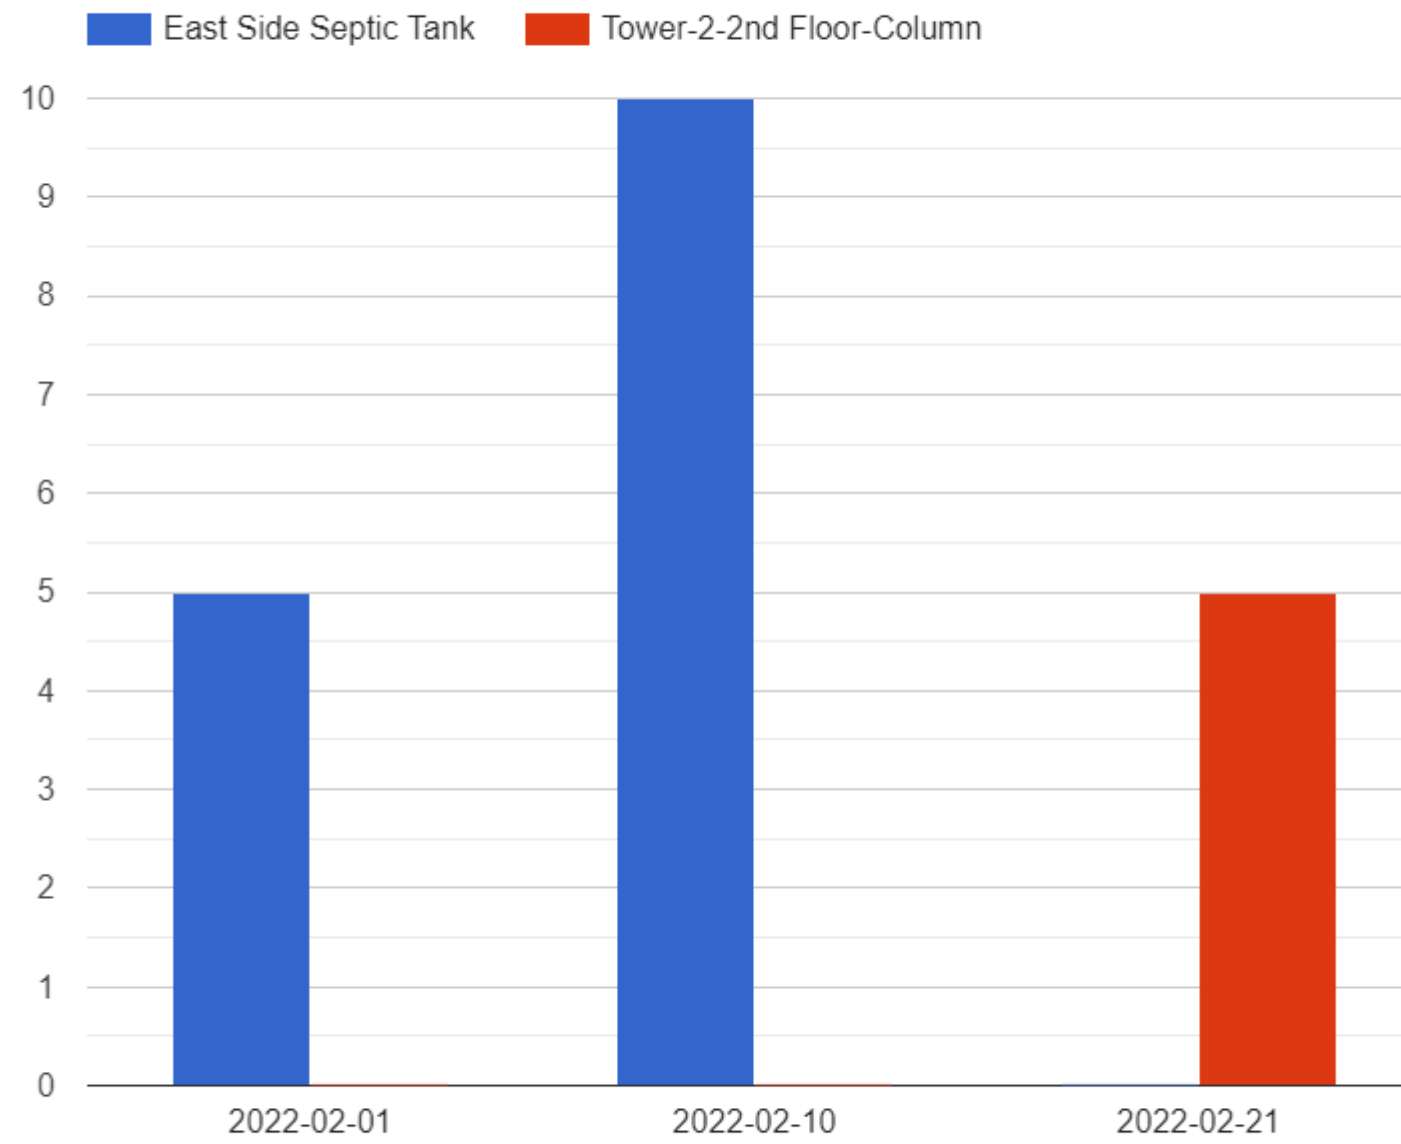



DAILY PROGRESS REPORT

Project:	The View Hotel Kuakata	Project Code:	58	Date:	21-February-2022
Client:	Sikder Group	Report	073	Day	Monday
Contractor:				Climate	Sunny
					17-24C

Manpower

SN	Description	Nos.
01	Cityscape Staff-Kuakata	9
05	Dulal	4
TOTAL		13

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
3.2.03.1	Tower-2-2nd Floor-Column	17nos	5	65	02-10-21	12-10-21

Site Photographs




Column/Wall Steel Shutter Cleaning, Oili

Column/Wall Steel Shutter Cleaning, Oili

Site Description	
Site Instruction	
Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

WORK PLAN AND PROGRESS

WORK PLAN (Rev-1.0) AND PROGRESS FOR THE VIEW HOTEL KUAKATA

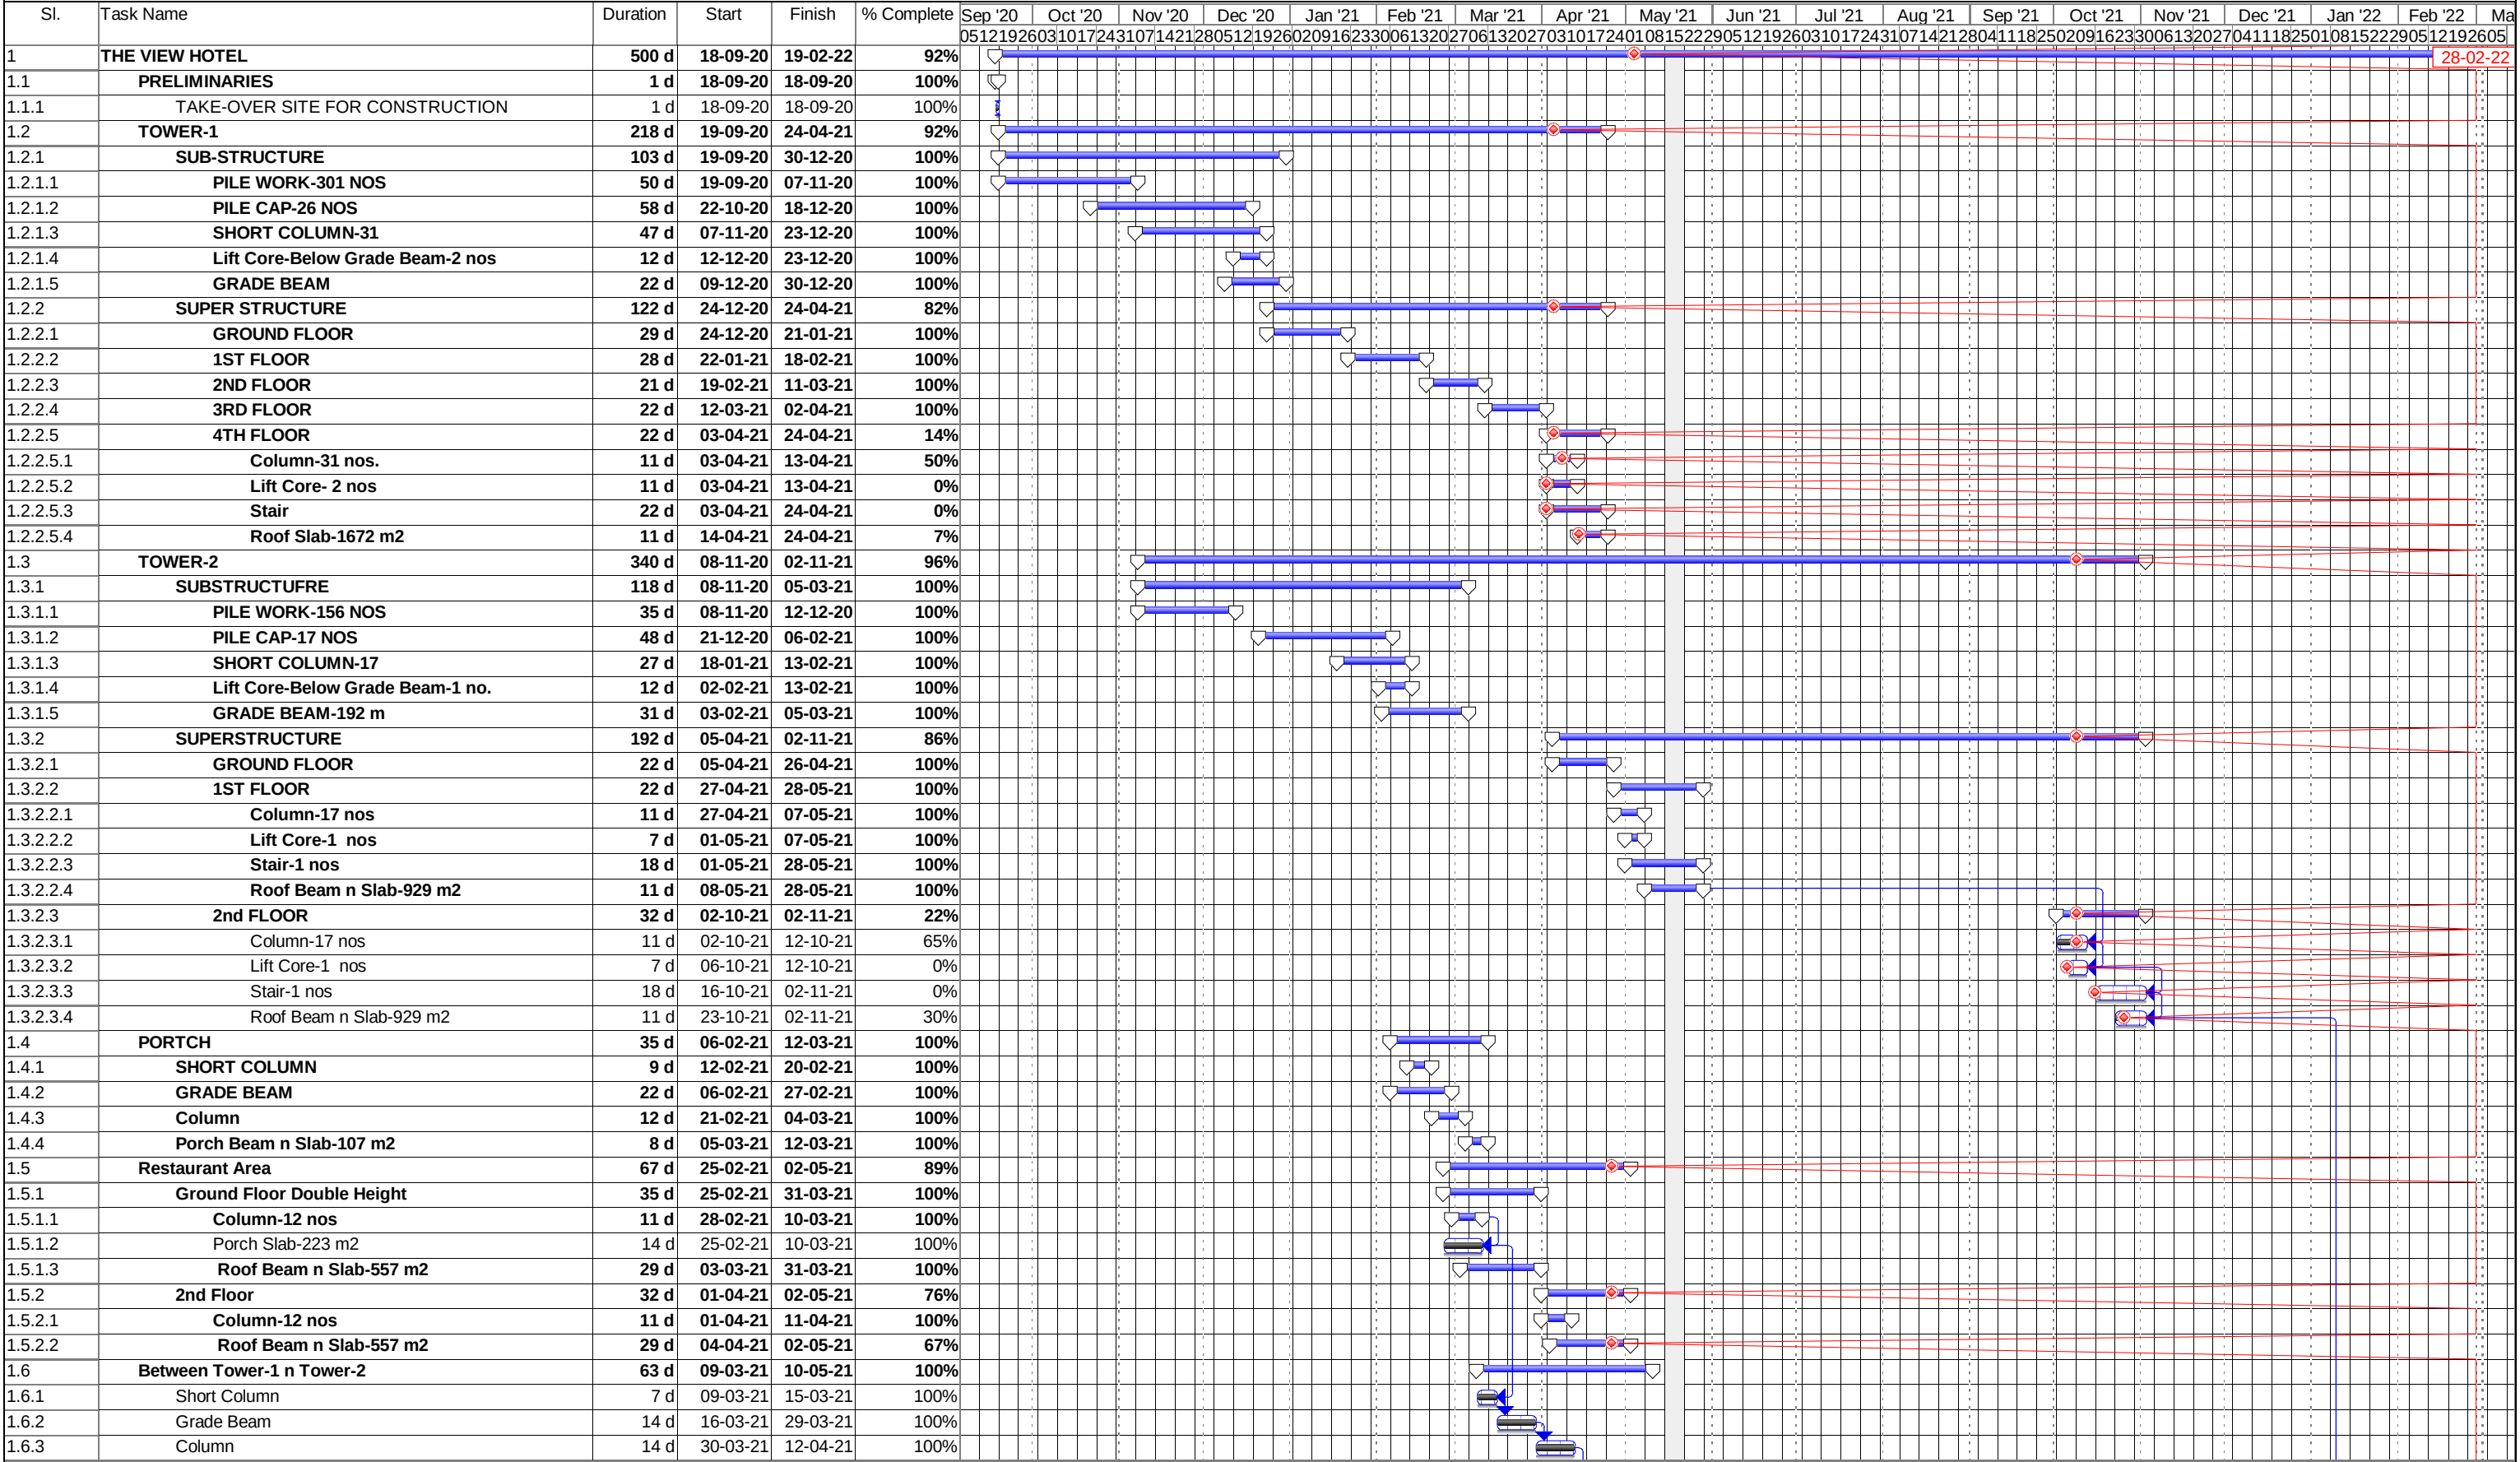

Date: 03-03-22 10:38
Sheet:1 /2

Task



Progress



Rolled Up Task



Rolled Up Progress



Group By Summary



Critical Task



Summary



Rolled Up Critical Task



Project Summary



This image shows a completely blank white rectangular area. It is surrounded by a thin, uniform black border that frames the entire content. There are no markings, text, or illustrations present on the white surface.

PROGRESS PHOTO

Site Photographs



on 18-09-20



on 18-09-20



on 06-11-20



on 06-11-20



Tower-1 Pile Cap on 12-11-20



Tower-2-Pile Work on 12-11-20





Tower-1-Pile Cap Work on 28-11-20



Tower-1 Pile Cap on 30-11-20



Tower-1-Pilehead breaking on 30-11-20



Tower-1-Grade Beam on 04-12-20



Tower-2-Pile Work on 04-12-20



Column Work on 07-12-20



Tower-1 Grade Beam on 07-12-20



Tower-1-Excavation for Pile Cap on 09-12-20



Tower-2-Pile Work on 09-12-20



Tower-1-Pile Cap Re-bar Fabrication on 12-12-20



Tower-1-Pilecap Concreting on 12-12-20



Tower-1-Column Re-bar work on 15-12-20



Tower-1-GF Beam Shuttering on 15-12-20



Tower-1-Grade Beam Re-bar Fabrication on 18-12-20



Tower-1-GF Beam Shuttering on 18-12-20



Tower-1-Lift Core Re-bar Work on 20-12-20



Tower-1-GF Slab Re-bar Work on 20-12-20



Tower-1-GF Roof Slab-2000 sft Concreting on 21-12-20



Tower-1-GF Roof Slab Concreting on 21-12-20



Tower-1-Grade Beam Shuttering on 24-12-20



Tower-2-Excavation for Pile Head Breakin on 24-12-20



Tower-1-GF Stair Shuttering on 27-12-20



Tower-2-Pile Head Breaking on 27-12-20



Tower-1-1st Floor Roof Slab Shuttering on 08-01-21



Tower-2-Pile Cap Concreting on 08-01-21



Tower-1-1st Floor Roof Slab 3600 sft Co on 11-01-21



Tower-1-1st Floor Roof Slab Concreting on 11-01-21



Tower-1-GF Roof Slab-3600sft Concreting on 16-01-21



Tower-1-GF Roof Slab Concreting on 16-01-21



Tower-1-GF Roof Slab 1800 sft Concreting on 18-01-21



Tower-1-1st Floor Roof Beam Shuttering on 18-01-21



Tower-1-GF Roof Slab-4250sft Concreting on 27-01-21



Tower-1-Lift Core and Slab Shuttering on 27-01-21



Tower-1-1st Floor Roof Slab 3600 sft Con on 05-02-21



Tower-2-GB Shutter Removing on 05-02-21



Tower-1-1st Floor Roof Slab 3600 sft Con on 07-02-21



Tower-1-1st Floor Roof Slab Concreting on 07-02-21



Tower-2-Grade Beam Shuttering on 10-02-21



Tower-1-1st floor Roof Slab 2450sft Conc on 10-02-21



Tower-1-2nd Floor Roof Slab-3600sft Conc on 16-02-21



Tower-2-Column Re-bar Work on 16-02-21



Tower-1-3rd Floor Column Re-bar Work on 23-02-21



Restaurant Area Slab Shuttering on 23-02-21



Tower-1-2nd Floor Roof Inspection on 25-02-21



Tower-1-2nd Floor Roof Curing on 25-02-21



Tower-1-3rd Floor Column Shuttering on 28-02-21



Resturant Area Slab Shuttering on 28-02-21



Restaurant-Double Height Slab Concreting on 02-03-21



Tower-1-3rd Floor Lift Core Re-bar Work on 02-03-21



Tower-1-3rd Floor Roof Slab Concreting on 11-03-21



View From South on 11-03-21



Tower-1-3rd Floor Roof Slab Shuttering on 13-03-21



Short Coulmn on 13-03-21



Restaurant GF Double Height Slab-6-9/A-B on 23-03-21



Tower-1-3rd Floor Roof Slab-Beam Shutter on 23-03-21



4th Floor Slab(3-5/B-E) Concreting-3600s on 24-03-21



Lift Core Wall Shuttering on 24-03-21



Tower-2: Lift Wall De-shuttering Work on 25-03-21



Column Shuttering Work on 25-03-21



Restaurant CE Double Ht Roof Slab Re bar on 20.03.21



Tower-1-3rd Flr Roof Slab(B-E/5-6)Concret on 30-03-21





Tower-1-3rd Floor Roof Slab Curing on 31-03-21



Restaurant-GF Doubl Ht Roof Slab-Re-bar on 01-04-21



Tower-1-3rd Floor Roof Slab Curing on 01-04-21





on 11-04-21





on 12-04-21



on 19-04-21



Tower-1-GF Roof Slab(G-I/6-7a)Concreting on 19-04-21



Restaurant GF Doubl Ht Slab-1-4/A-B-Conc on 24-04-21



on 24-04-21



Between Tower1-2-GF Roof Slab-Concreting on 26-04-21



Lift Core Wall Shuttering on 26-04-21



Beam Shuttering on 28-04-21



Column Concreting on 28-04-21



Column Concreting on 29-04-21



Beam Shuttering on 29-04-21



Beam Shuttering Work on 29-04-21



Column Shuttering Work on 30-04-21



Roof Slab Shuttering on 02-05-21



Tower-2-Lift Core Deshuttering on 02-05-21



Roof Slab Shuttering on 04-05-21



Roof Slab Shuttering on 04-05-21



Roof Beam Shuttering on 09-05-21



Curing Work on 09-05-21



Restaurant GF Double Height Roof Slab on 24-05-21



Roof Slab De-shuttering on 24-05-21



Slab Shuttering on 31-05-21



Beam Shuttering on 31-05-21



Between Tower1-2-1st Flr Roof Slab-Concr on 05-06-21





































Tower-2 on 17-10-21



Tower-2-2nd Floor-Column Re-bar Work on 17-10-21




































Re-bar Cutting on 08-01-22



Tower-2-3rd Floor-Re-bar Work on 08-01-22





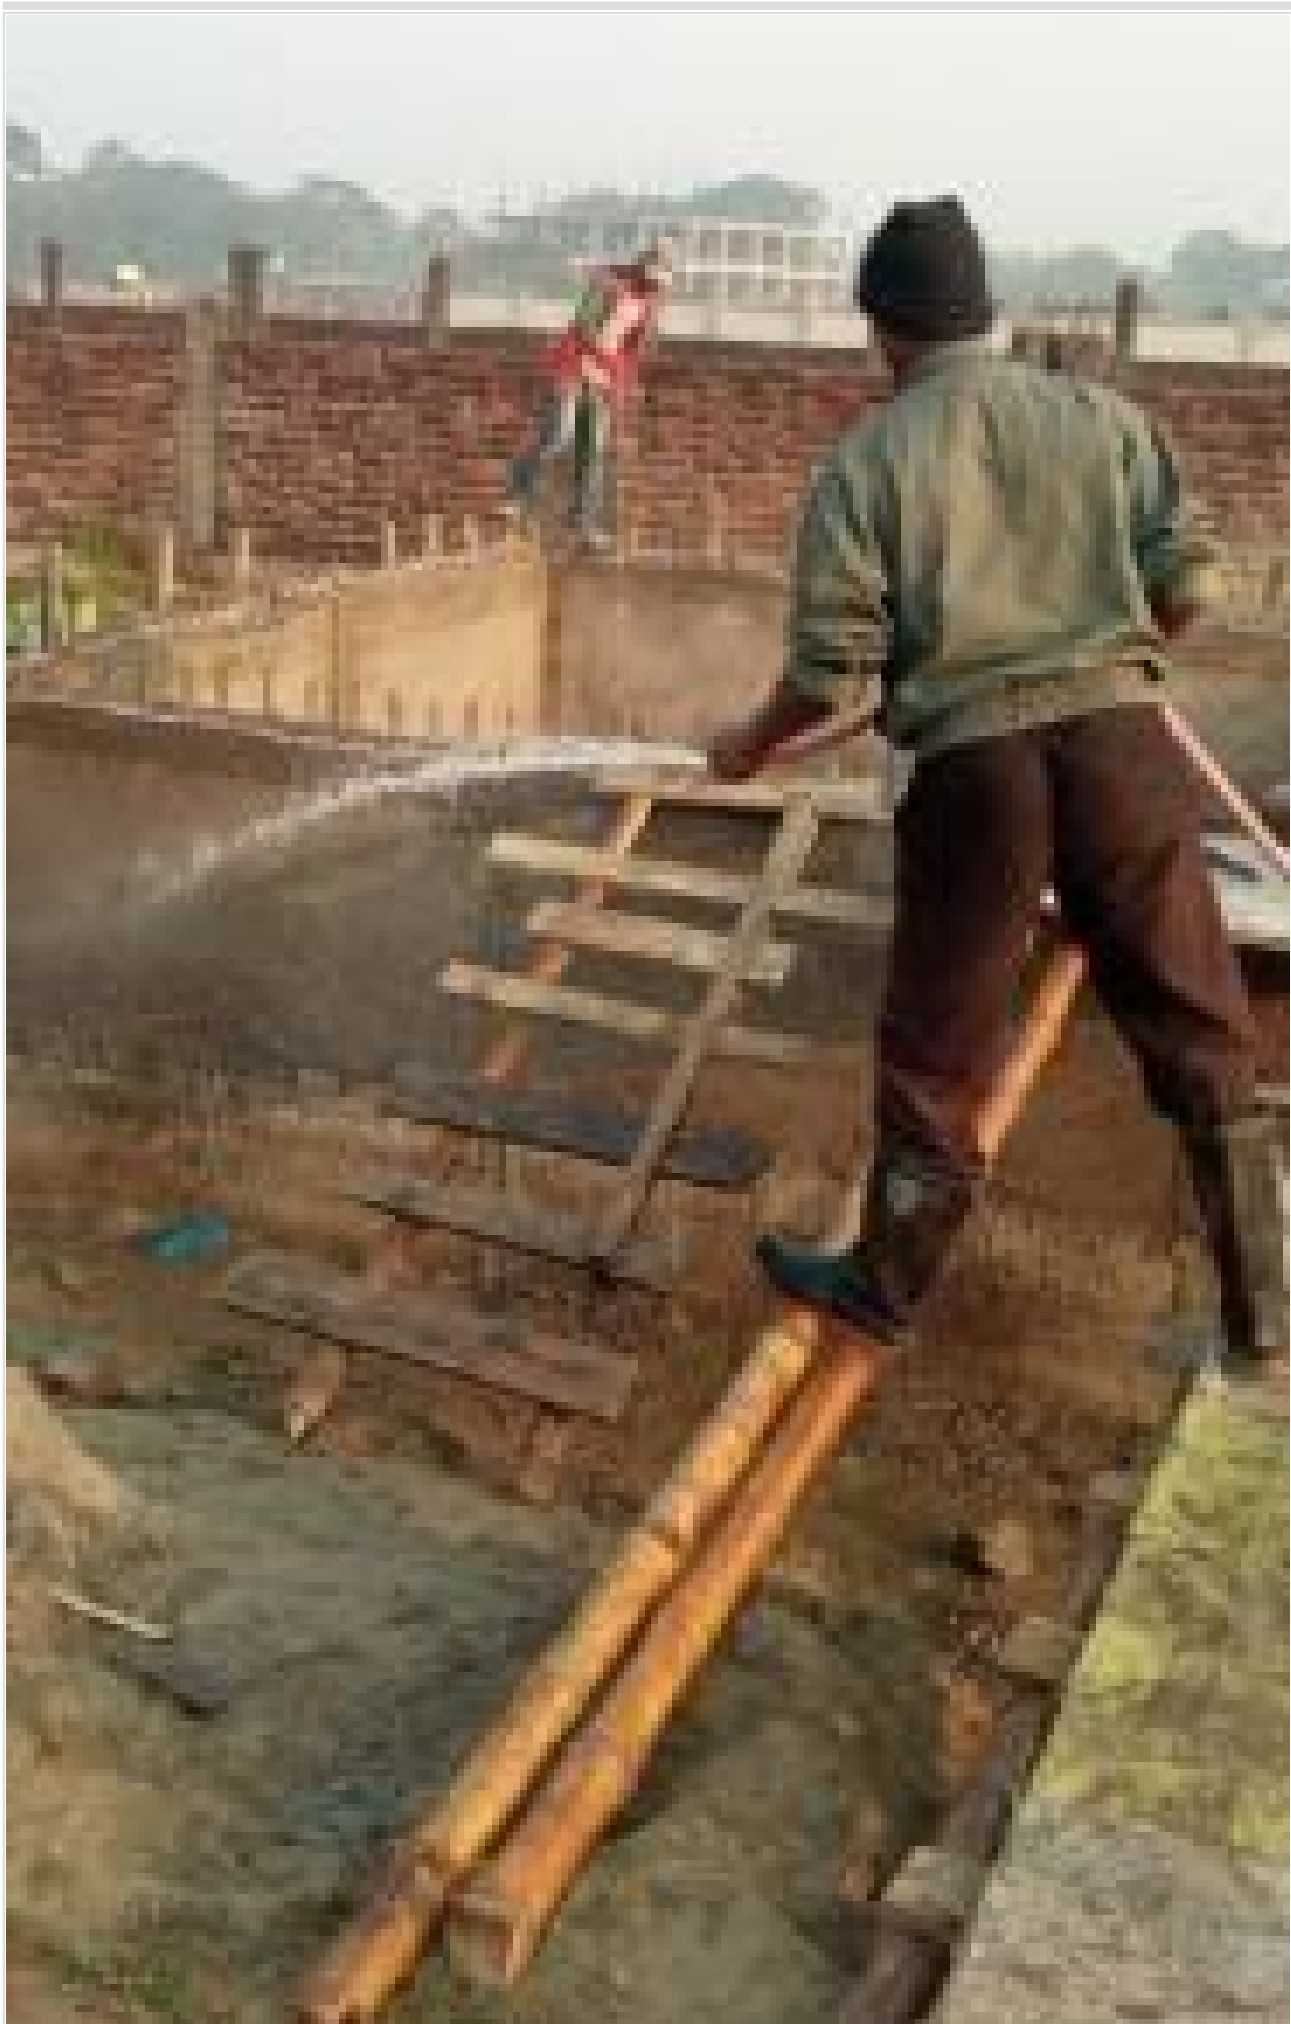





East Septic Tank Plastering on 01-02-22











Column/Wall Steel Shutter Cleaning, Oili on 21-02-22



TOTAL PROGRESS REPORT

From 18-September-2020 to 21-February-2022

Project Code:	58	Name:	The View Hotel Kuakata
Client:	Sikder Group	Contractor:	
Total Duration:	521	days	Total Working Days: 73 Total Manpower: 6905
Planning Progress =	100%	Actual Progress=	87.1% SPI= 0.87 Behind Schedule

Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
1.1.01	Take-over Site for Construction		100	18-09-20	18-09-20	18-09-20	18-09-20	0	
2.1.01	Tower-1-Pile Work	301nos	100	19-09-20	07-11-20	05-11-20	06-11-20	1	
2.1.02	Tower-1-Pile Cap	26nos	100	22-10-20	18-12-20	05-11-20	18-12-20	0	
2.1.03	Tower-1-Padestal	31nos	100	07-11-20	23-12-20	28-11-20	21-12-20	2	
2.1.04	Tower-1-Lift Core Below GB	2nos	100	12-12-20	23-12-20	09-12-20	21-12-20	2	
2.1.05	Tower-1-Grade Beam	421rm	100	09-12-20	30-12-20	30-11-20	27-01-21	-28	
2.2.01.1	Tower-1-GF Column	31nos	100	24-12-20	04-01-21	09-12-20	27-01-21	-23	
2.2.01.2	Tower-1-GF-Lift Core	2nos	100	24-12-20	04-01-21	21-12-20	27-01-21	-23	
2.2.01.3	Tower-1-GF-Stair	2nos	100	24-12-20	15-01-21	21-12-20	27-01-21	-12	
2.2.01.4	Tower-1-1st Floor Slab	1505m2	100	10-01-21	20-01-21	15-12-20		0	
2.2.02.1	Tower-1-1st Floor Column	31nos	100	22-01-21	31-01-21	27-12-20	07-02-21	-7	
2.2.02.2	Tower-1-1st Floor Lift Core	2nos	100	02-02-21	07-02-21	05-02-21	07-02-21	0	
2.2.02.3	Tower-1-1st Floor Stair	2nos	100	22-01-21	18-02-21	05-02-21	10-02-21	8	
2.2.02.4	Tower-1-2nd Floor Slab	1672m2	100	08-02-21	18-02-21	08-01-21		0	
2.2.03.1	Tower-1-2nd Floor Column	31nos	100	19-02-21	01-03-21	05-02-21	23-02-21	6	
2.2.03.4	Tower-1-3rd Floor Slab	1672m2	100	01-03-21	11-03-21	16-02-21	28-02-21	11	
2.2.04.1	Tower-1-3rd Floor Column	31nos	100	12-03-21	22-03-21	28-02-21	25-03-21	-3	
2.2.04.2	Tower-1-3rd Floor Lift Core	2nos	100	12-03-21	22-03-21	11-03-21	25-03-21	-3	
2.2.04.3	Tower-1-3rd Floor Stair	2nos	100	12-03-21	02-04-21	11-03-21	01-04-21	1	
2.2.04.4	Tower-1-4th Floor Slab	1672m2	100	23-03-21	02-04-21	11-03-21	01-04-21	1	
2.2.05.1	Tower-1-4th Floor-Column	31nos	50	03-04-21	13-04-21	22-06-21	22-06-21	-70	Completed

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
2.2.05.2	Tower-1-4th Floor-Lift Core	2nos		03-04-21	13-04-21			0	Started
2.2.05.3	Tower-1-4th Floor-Stair	2nos		03-04-21	24-04-21			0	Started
2.2.05.4	Tower-1-4th Floor-Roof Beam n Slab	1672m2	7	14-04-21	24-04-21	22-06-21	22-06-21	-59	Completed
3.1.01	Tower-2-Pile Boring	156nos	100	08-11-20	12-12-20	12-11-20	12-12-20	0	
3.1.02	Tower-2-Pile Cap	17nos	100	21-12-20	06-02-21	21-12-20	05-02-21	1	
3.1.03	Tower-2-Short Column	17nos	100	18-01-21	13-02-21	18-01-21	10-02-21	3	
3.1.04	Tower-2-Lift Core below Grade Beam	1nos	100	02-02-21	13-02-21	10-02-21	10-02-21	3	
3.1.05	Tower-2-Grade Beam	192m	100	03-02-21	05-03-21	23-02-21	02-03-21	3	
3.2.01.1	Tower-2-GF Column	17nos	100	05-04-21	15-05-21	13-03-21	25-03-21	51	
3.2.01.2	Tower-2-GF Lift Core	1nos	100	09-04-21	15-04-21	13-03-21	25-03-21	21	
3.2.01.3	Tower-2-GF Stair	1nos	100	09-04-21	26-04-21	25-03-21	19-04-21	7	
3.2.01.4	Tower-2-1st Floor Slab	929m2	100	16-04-21	26-04-21	12-04-21	19-04-21	7	
3.2.02.1	Tower-2-1st Floor-Column	17nos	100	27-04-21	07-05-21	28-04-21	26-09-21	-142	
3.2.02.2	Tower-2-1st Floor-Lift Core	1nos	100	01-05-21	07-05-21	29-04-21	26-09-21	-142	
3.2.02.3	Tower-2-1st Floor-Stair	1nos	100	01-05-21	28-05-21	04-05-21	21-09-21	-116	
3.2.02.4	Tower-2-2nd Floor-Slab	1115m2	100	08-05-21	28-05-21	29-04-21	26-09-21	-121	
3.2.03.1	Tower-2-2nd Floor-Column	17nos	65	02-10-21	12-10-21	30-09-21	21-02-22	-132	Completed
3.2.03.2	Tower-2-2nd Floor-Lift core	1no.	0	06-10-21	12-10-21			0	Started
3.2.03.3	Tower-2-2nd Floor-Stair	1no.	0	16-10-21	02-11-21			0	Started
3.2.03.4	Tower-2-3rd Floor Slab	929m2	30	23-10-21	02-11-21	28-10-21	08-01-22	-67	Completed
4.1	Porch-Short Column	nos	100	21-01-21	29-01-21	27-01-21	27-01-21	2	
4.2	Porch-Grade Beam	m	100	15-01-21	05-02-21	27-01-21	27-01-21	9	
4.3	Porch-Column	nos	100	30-01-21	10-02-21	27-01-21	05-02-21	5	
4.4	Porch-Beam and Slab	107m2	100	11-02-21	18-02-21	07-02-21	07-02-21	11	
5.01.1	Restaurant-GF Double Height Column	12nos	100	28-02-21	10-03-21	28-02-21	25-03-21	-15	
5.01.2	Restaurant-Porch Slab	223m2	100	25-02-21	10-03-21	02-03-21	02-03-21	8	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
5.01.3	Restaurant-GF Double Height Roof Sl	557m2	100	03-03-21	31-03-21	23-03-21	24-04-21	-24	
5.02.1	Restaurant-2nd Floor-Column	12nos	100	01-04-21	11-04-21	19-04-21	16-06-21	-66	
5.02.2	Restaurant-2nd Floor-Roof Slab	836m2	67	04-04-21	02-05-21	24-04-21	16-06-21	-45	Completed
6.1	Between Tower1-2-Short Column	nos	100	09-03-21	15-03-21	13-03-21	13-03-21	2	
6.2	Between Tower1-2-Grade Beam	m	100	16-03-21	29-03-21	25-03-21	25-03-21	4	
6.3	Between Tower1-2-Column	nos	100	30-03-21	12-04-21	11-04-21	11-04-21	1	
6.4	Between Tower1-2-GF Roof Slab	372m2	100	13-04-21	26-04-21	26-04-21	26-04-21	0	
6.5	Between Tower-1-2-1st Flr Roof Slab	372m2	100	27-04-21	10-05-21	05-06-21	05-06-21	-26	
7.1	East Side Soak Well Slab	1no.	100	10-01-22	27-01-22	27-01-22	27-01-22	0	
7.2	West Side Septic Tank	1no.	25	12-01-22	10-02-22	27-01-22	31-01-22	10	Completed
7.3	East Side Septic Tank	1no.	30	21-01-22	19-02-22	27-01-22	10-02-22	9	Completed

Site Photographs



on 18-09-20



on 18-09-20



on 06-11-20



on 06-11-20



Tower-1 Pile Cap on 12-11-20



Tower-2-Pile Work on 12-11-20



Tower-2-Piling Work on 28-11-20



Tower-1-Pile Cap Work on 28-11-20



Tower-1 Pile Cap on 30-11-20



Tower-1-Pilehead breaking on 30-11-20



Tower-1-Grade Beam on 04-12-20



Tower-2-Pile Work on 04-12-20



Column Work on 07-12-20



Tower-1 Grade Beam on 07-12-20



Tower-1-Excavation for Pile Cap on 09-12-20



Tower-2-Pile Work on 09-12-20



Tower-1-Pile Cap Re-bar Fabrication on 12-12-20



Tower-1-Pilecap Concreting on 12-12-20



Tower-1-Column Re-bar work on 15-12-20



Tower-1-GF Beam Shuttering on 15-12-20



Tower-1-Grade Beam Re-bar Fabrication on 18-12-20



Tower-1-GF Beam Shuttering on 18-12-20



Tower-1-Lift Core Re-bar Work on 20-12-20



Tower-1-GF Slab Re-bar Work on 20-12-20



Tower-1-GF Roof Slab-2000 sft Concreting on 21-12-20



Tower-1-GF Roof Slab Concreting on 21-12-20



Tower-1-Grade Beam Shuttering on 24-12-20



Tower-2-Excavation for Pile Head Breakin on 24-12-20



Tower-1-GF Stair Shuttering on 27-12-20



Tower-2-Pile Head Breaking on 27-12-20



Tower-1-1st Floor Roof Slab Shuttering on 08-01-21



Tower-2-Pile Cap Concreting on 08-01-21



Tower-1-1st Floor Roof Slab 3600 sft Co on 11-01-21



Tower-1-1st Floor Roof Slab Concreting on 11-01-21



Tower-1-GF Roof Slab-3600sft Concreting on 16-01-21



Tower-1-GF Roof Slab Concreting on 16-01-21



Tower-1-GF Roof Slab 1800 sft Concreting on 18-01-21



Tower-1-1st Floor Roof Beam Shuttering on 18-01-21



Tower-1-GF Roof Slab-4250sft Concreting on 27-01-21



Tower-1-Lift Core and Slab Shuttering on 27-01-21



Tower-1-1st Floor Roof Slab 3600 sft Con on 05-02-21



Tower-2-GB Shutter Removing on 05-02-21



Tower-1-1st Floor Roof Slab 3600 sft Con on 07-02-21



Tower-1-1st Floor Roof Slab Concreting on 07-02-21



Tower-2-Grade Beam Shuttering on 10-02-21



Tower-1-1st floor Roof Slab 2450sft Conc on 10-02-21



Tower-1-2nd Floor Roof Slab-3600sft Conc on 16-02-21



Tower-2-Column Re-bar Work on 16-02-21



Tower-1-3rd Floor Column Re-bar Work on 23-02-21



Restaurant Area Slab Shuttering on 23-02-21



Tower-1-2nd Floor Roof Inspection on 25-02-21



Tower-1-2nd Floor Roof Curing on 25-02-21



Tower-1-3rd Floor Column Shuttering on 28-02-21



Resturant Area Slab Shuttering on 28-02-21



Restaurant-Double Height Slab Concreting on 02-03-21



Tower-1-3rd Floor Lift Core Re-bar Work on 02-03-21



Tower-1-3rd Floor Roof Slab Concreting on 11-03-21



View From South on 11-03-21



Tower-1-3rd Floor Roof Slab Shuttering on 13-03-21



Short Coulmn on 13-03-21



Restaurant GF Double Height Slab-6-9/A-B on 23-03-21



Tower-1-3rd Floor Roof Slab-Beam Shutter on 23-03-21



4th Floor Slab(3-5/B-E) Concreting-3600s on 24-03-21



Lift Core Wall Shuttering on 24-03-21



Tower-2: Lift Wall De-shuttering Work on 25-03-21



Column Shuttering Work on 25-03-21



Restaurant-GF Double Ht Roof Slab-Re-bar on 30-03-21



Tower-1-3rd Flr Roof Slab(B-E/5-6)Concret on 30-03-21



Tower-1-3rd Floor Roof Slab(B-E/6-7)Conc on 31-03-21



Tower-1-3rd Floor Roof Slab Curing on 31-03-21



Restaurant-GF Doubl Ht Roof Slab-Re-bar on 01-04-21



Tower-1-3rd Floor Roof Slab Curing on 01-04-21



on 11-04-21



on 11-04-21



Tower-2-Gr.Fl'r Roof Slab(5a-6/H-J) Concr on 12-04-21



on 12-04-21



on 19-04-21



Tower-1-GF Roof Slab(G-I/6-7a)Concreting on 19-04-21



Restaurant GF Doubl Ht Slab-1-4/A-B-Conc on 24-04-21



on 24-04-21



Between Tower1-2-GF Roof Slab-Concreting on 26-04-21



Lift Core Wall Shuttering on 26-04-21



Beam Shuttering on 28-04-21



Column Concreting on 28-04-21



Column Concreting on 29-04-21



Beam Shuttering on 29-04-21



Beam Shuttering Work on 30-04-21



Column Shuttering Work on 30-04-21



Roof Slab Shuttering on 02-05-21



Tower-2-Lift Core Deshuttering on 02-05-21



Roof Slab Shuttering on 04-05-21



Roof Slab Shuttering on 04-05-21



Roof Beam Shuttering on 09-05-21



Curing Work on 09-05-21



Restaurant GF Double Height Roof Slab on 24-05-21



Roof Slab De-shuttering on 24-05-21



Slab Shuttering on 31-05-21



Beam Shuttering on 31-05-21



Between Tower1-2-1st Flr Roof Slab-Concr on 05-06-21



Slab Re-bar Work on 05-06-21



Restaurant-3rd Floor Slab Concreting on 12-06-21



Restaurant-3rd Floor Slab Re-bar Work on 12-06-21



Restaurant-3rd Floor Slab Concreting on 16-06-21



Restaurant-3rd Floor Slab Concreting on 16-06-21

Grid:1-6/ A"-B=3300 sft



Tower-1-4th Floor Concreting on 22-06-21



Tower-2-2nd Floor Slab Shuttering on 22-06-21

Grid:5-8=877sft-West Verandhah Concreting



Tower-1-4th Floor Concreting on 26-06-21



Tower-2-2nd Floor Slab Shuttering on 26-06-21

Grid:1-4/A-B=90sft Slab Concreting



Tower-2:2nd floor slab re-bar work on 04-07-21



Tower-2:2nd floor slab concreting on 04-07-21

G-I/6-7a: 3300 sft



Tower-2:2nd floor slab concreting on 05-07-21



Tower-2-Column Rod binding-shuttering on 05-07-21

G-I/5a-6: 1500 sft



Tower-2:2nd flr double height slab concr on 26-09-21



Tower-2:2nd floor slab concreting on 26-09-21

5-8/I-K: 3200 sft



Tower-2-2nd Floor-Column Concreting on 30-09-21



Tower-2-2nd Floor-Column Concreting on 30-09-21



Tower-2 on 17-10-21



Tower-2-2nd Floor-Column Re-bar Work on 17-10-21



Tower-2-3rd Floor Slab Shutter Repairing on 28-10-21



Tower-2-2nd Floor Column Concreting on 28-10-21



Tower-2-3rd Flr Slab-Plain Sheet laying on 31-10-21



Tower-2-3rd Flor Slab-Rod Lifting on 31-10-21



Tower-2-3rd Floor Beam Re-bar work on 01-11-21



Tower-2-3rd Floor Beam Re-bar fabricatio on 01-11-21



Tower-2-3rd Floor Beam shuttering on 14-11-21



Tower-2-3rd Floor Beam shuttering on 14-11-21



Tower-2-3rd Floor Slab Shuttering on 30-11-21



Hollow box jointing for slab shuttering on 30-11-21



Tower-2-3rd Floor Slab-shuttering on 01-12-21



MS Prop Repairing on 01-12-21



Re-bar Fabrication on 31-12-21



Tower-2:3rd floor slab re-bar work on 31-12-21



Re-bar Fabricating on 01-01-22



Tower-2-3rd Floor-Re-bar Work on 01-01-22



Re-bar Cutting on 08-01-22



Tower-2-3rd Floor-Re-bar Work on 08-01-22



Septic Tank Wall Concreting on 27-01-22



Soak Well Slab Concreted on 27-01-22



Septic Tank Wall Curing on 31-01-22



Septic Tank Wall Plastering on 31-01-22



East Septic Tank Plastering on 01-02-22



East Septic Tank Plastering on 01-02-22



East Septic Tank Slab Shuttering on 10-02-22



East Septic Tank Slab Shuttering on 10-02-22



Column/Wall Steel Shutter Cleaning, Oili on 21-02-22



Column/Wall Steel Shutter Cleaning, Oili on 21-02-22
