



## WEEKLY PROGRESS REPORT

From 22-March-2025 to 28-March-2025

Project Code:	31	Name:	New Hope Agrotech-Munshiganj
Client:	New Hope Agrotech BD Ltd.	Contractor:	Sarker Steel Ltd.

### Weekly Progress

WBS	Task	Total Qty	Upto Last Week(%)	This Week(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
07.1	AAC Block Work-Exterior	197m2	70	10	80	21-01-25	05-02-25	24-03-25
07.2	AAC Block Work-Interior	195m2	75	10	85	06-02-25	15-02-25	26-03-25
07.3	Plastering-Exterior Wall	416m2	30	10	40	06-02-25	15-02-25	24-03-25
07.4	Plastering-Interior Wall	392m2	25	5	30	16-02-25	25-02-25	22-03-25
07.6	Painting-Interior	392m2	5	15	20	18-03-25	27-03-25	27-03-25
08.3	Fire Works	1sum	0	10	10	26-02-25	27-03-25	28-03-25

## Site Photographs



Stair Railing fixing on 22-03-25

Site Description

Site Instruction



Welding work on 22-03-25



Interior AAC block work on 23-03-25

Site Description

Site Instruction



Interior painting work on 23-03-25



Exterior wall plastering on 24-03-25

Site Description

Site Instruction



Roof top concreting on 24-03-25






Interior painting on 25-03-25

Site sheeting on 25-03-25

Site Desription

Site Instruction

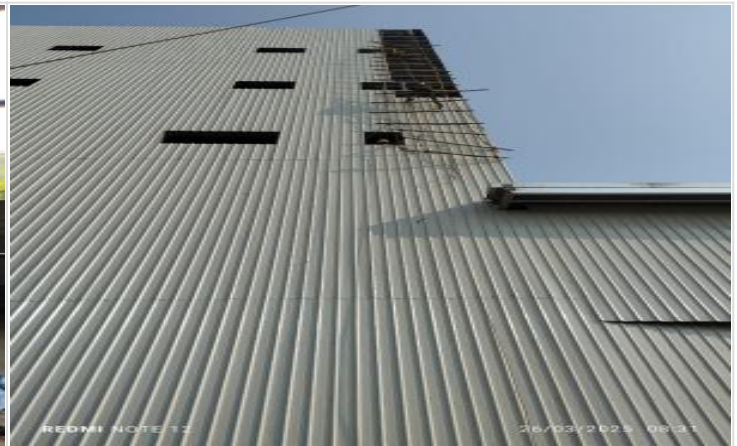

Interior AAC block work on 26-03-25

Site sheeting on 26-03-25

Site Desription

Site Instruction



Interior painting on 27-03-25

Interior painting on 27-03-25

Site Desription

Site Instruction



Fire works on 28-03-25

Cleaning works on 28-03-25

Site Desription	
Site Instruction	
Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
