

From 5-December-2020 to 15-June-2021

Project Code:	48	Name:	BTT Sales Center Purbachal			
Client:	Power Pac Holdings Ltd	Contractor:				
Total Duration:	192	days	Total Working Days:	45	Total Manpower:	2484
Planning Progress =	76%	Actual Progress=	84.4%	SPI=	1.11	Ahead Schedule

## Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
1	Drawing-Design		100	14-08-20	28-08-20	28-08-20	28-08-20	0	
2	Mobilization and Layout		100	18-08-20	24-08-20	24-08-20	24-08-20	0	
3.1	Pile Work	267nos	100	25-08-20	30-09-20	30-09-20	30-09-20	0	
3.2.1.1	Excavation for Pile Head Breaking	60nos	100	02-11-20	21-11-20	21-11-20	19-12-20	-28	
3.2.1.2	Pile Head Breaking	267nos	100	04-11-20	23-01-21	23-11-20	23-11-20	61	
3.2.1.3	Excavation for Pile cap	60nos	100	06-11-20	25-11-20	25-11-20	25-11-20	0	
3.2.1.4	Pile Cap-Brick Flat Soling	60nos	100	08-11-20	27-11-20	27-11-20	27-11-20	0	
3.2.1.5	Pile Cap-CC Work	60nos	100	09-11-20	28-11-20	28-11-20	28-11-20	0	
3.2.1.6	Pile Cap Re-bar Work	60nos	100	17-11-20	06-12-20	03-12-20	05-12-20	1	
3.2.1.7	Pile Cap-Form Work	60nos	100	19-11-20	08-12-20	03-12-20	05-12-20	3	
3.2.1.8	Pile Cap Concreting	60nos	100	21-11-20	10-12-20	03-12-20	29-12-20	-19	
3.2.2.1	Lift Core upto Mat-Re-bar Work	2nos	100	11-12-20	20-12-20	03-12-20	19-12-20	1	
3.2.2.2	Lift-Core upto Mat-Form Work	2nos	100	12-12-20	21-12-20	03-12-20	19-12-20	2	
3.2.2.3	Lift Core upto Mat-Concreting	2nos	100	13-12-20	22-12-20	19-12-20	19-12-20	3	
3.2.3.1	Mat-Bed Preparation	1311sqm	100	28-11-20	11-12-20	05-12-20	29-12-20	-18	
3.2.3.2	Mat-Brick Flat Soling	1311sqm	100	05-12-20	13-12-20	15-12-20	29-12-20	-16	
3.2.3.3	Mat-Lean Concrete	1311sqm	100	10-12-20	14-12-20	15-12-20	29-12-20	-15	
3.2.3.4	Mat-Re-bar Fabrication		100	15-12-20	29-12-20	29-12-20	05-01-21	-7	
3.2.3.5	Mat-Form works		100	28-12-20	03-01-21	05-01-21	05-01-21	-2	
3.2.3.6	Mat-Concreting	1311sqm	100	04-01-21	04-01-21	05-01-21	05-01-21	-1	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.3.1.1	South-Retaining Wall-Re-bar Work	385sqm	100	05-01-21	01-02-21	28-01-21	09-02-21	-8	
3.3.1.2	South-Retaining Wall-Form Work	385sqm	100	23-01-21	06-02-21	28-01-21	09-02-21	-3	
3.3.1.3	South-Retaining Wall-Concreting	385sqm	100	07-02-21	08-02-21	28-01-21	09-02-21	-1	
3.3.2.1	North-Retaining Wall-Re-bar Work	139m2	100	09-02-21	02-03-21	17-02-21	20-02-21	10	
3.3.2.2	North-Retaining Wall-Form Work	139m2	100	21-02-21	07-03-21	17-02-21	20-02-21	15	
3.3.2.3	North-Retaining Wall-Concreting	139m2	100	17-03-21	18-03-21	05-04-21	05-04-21	-18	
3.4.1.1	Basement-South-Column-Re-bar work	40nos	100	05-01-21	01-02-21	28-01-21	28-01-21	4	
3.4.1.2	Basement-South-Column-Shuttering	40nos	100	23-01-21	06-02-21	28-01-21	28-01-21	9	
3.4.1.3	Basement-South-Column-Concreting	40nos	100	07-02-21	08-02-21	28-01-21	28-01-21	11	
3.4.2	Basement-North Column	21nos	100	09-02-21	09-03-21	04-03-21	05-04-21	-27	
3.5	Basement-Lft Core and Water Reservo	289m2	100	26-02-21	09-03-21	20-03-21	05-04-21	-27	
3.6	Basement-Stair	3nos	100	09-02-21	22-04-21	05-04-21	25-04-21	-3	
3.7	Basement-Ramp	2nos	0	06-07-21	23-07-21			0	
3.8.1.1	South-GF-Slab Shuttering	743m2	100	16-02-21	27-02-21	17-02-21	15-03-21	-16	
3.8.1.2	South-GF-Slab Re-bar Work	743m2	100	28-02-21	09-03-21	07-03-21	15-03-21	-6	
3.8.1.4	South-GF-Slab Concreting	743m2	100	14-03-21	15-03-21	15-03-21	15-03-21	0	
3.8.2	North-Ground Floor Slab	495m2	100	02-04-21	22-04-21	10-04-21	25-04-21	-3	
3.9	Basement-Wall and Ceiling plaster	2415m2	11	30-05-21	30-07-21	07-03-21	15-06-21	45	
4.1	Ground Floor-Column	57nos	95	27-04-21	05-06-21	28-04-21	09-06-21	-4	Completed
4.2.1	Ground Floor-Roof Slab Shutter	822m2	49	03-05-21	20-06-21	03-05-21	15-06-21	5	
4.2.2	Gr.Floor Roof Slab-Re-bar Work	160nos	2	15-06-21	03-07-21	15-06-21	15-06-21	18	
4.2.3	Ground Floor-Roof Slab Concreting	822m2		05-07-21	05-07-21			0	
4.3	Ground Floor-Lift Core	2nos	52	25-05-21	15-06-21	30-05-21	07-06-21	8	

<b>WBS</b>	<b>Task</b>	<b>Total Qty</b>	<b>Total Done(%)</b>	<b>Shedule Start</b>	<b>Schedule Finish</b>	<b>Actual Start</b>	<b>Actual Finish</b>	<b>Lead-Lag(day)</b>	<b>Not Yet</b>
4.4	Ground Floor-Stair Case	2nos	80	25-05-21	05-07-21	31-05-21	15-06-21	20	

## Site Photographs



Pile Cap Re-bar Shuttering Work on 05-12-20



Pile Cap Re-bar Shuttering Work on 05-12-20



Pile Cap Concreting on 06-12-20



Pile Cap Concreting on 06-12-20



Mat CC Concreting on 15-12-20



Footing Curing on 15-12-20



Lift Core Concreting on 19-12-20



Footing Re-bar Placing on 19-12-20



Mat Re-bar Work on 29-12-20



Mat Re-bar Work on 29-12-20





Inspection before Mat Concreting on 05-01-21



Mat Concreting on 05-01-21



Retaining wall and Column Concreting on 28-01-21



Retaining wall and Column Concreting on 28-01-21



South Retaining wall 2nd Lift Concretin on 09-02-21



South Retaining wall 2nd Lift Concretin on 09-02-21



on 17-02-21



on 17-02-21

Project Closed 11-15 Feb 2021 due to Honorable Late Z.H. Sikder Death



Retaining Wall Shuttering on 18-02-21



Retaining Wall Shuttering on 18-02-21



Retaining Wall Concreting on 20-02-21



Retaining wall Concreting on 20-02-21



Toolbox Meeting on 25-02-21



Ground Floor Slab Shuttering on 25-02-21



Tool Box Meeting on 04-03-21



Night Shift Working on 04-03-21



GF Slab Re-bar Inspection on 07-03-21




Basement West Wall Plastering on 07-03-21





GF Slab Shuttering at Night Shift on 08-03-21

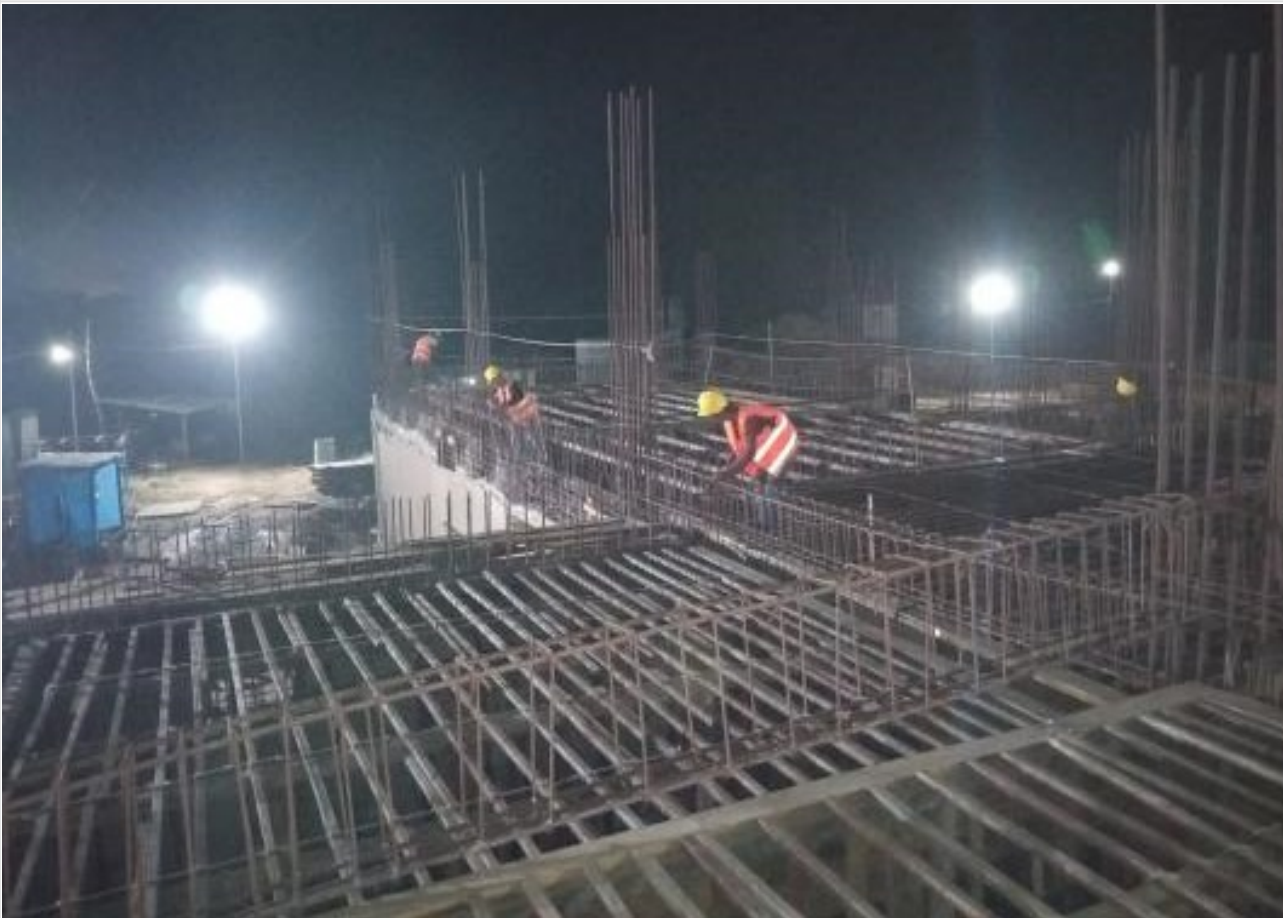

GF Slab Re-bar Work at Night Shift on 08-03-21



Ground Floor Slab Re-bar Work on 10-03-21



GF Slab Shuttering at Night Shift on 10-03-21



GF North-Slab 8000 sft Concreting on 15-03-21



GF Slab Concreting complete at night on 15-03-21



on 20-03-21



on 20-03-21



on 27-03-21



on 27-03-21



on 29-03-21



on 29-03-21



on 31-03-21



on 31-03-21



Ground Floor Column Re-bar Work on 01-04-21



Beam Shutter Making on 01-04-21



on 04-04-21





on 04-04-21



Lift Core Wall Concreting on 05-04-21



Water Reservoir Wall Concreting on 05-04-21



Column Shuttering on 10-04-21



Ground Floor Slab Shuttering on 10-04-21



Inspection before GF Slab Concreting on 25-04-21



Ground Floor Slab Concreting on 25-04-21



Toolbox Meeting on 28-04-21



G.M. Construction Visit on 28-04-21



Column Shutteeing on 30-04-21



Beam Shuttering on 30-04-21



Column Concreting on 03-05-21



Beam Shuttering on 03-05-21



Column Re-bar Work on 04-05-21





Column Shuttering Work on 04-05-21



Column Re-bar Work on 08-05-21



Column Shuttering Work on 08-05-21



Column Shuttering on 09-05-21



Column Curing on 09-05-21



Tool Box Meeting on 12-05-21



Ground Floor-Column Shuttering Work on 12-05-21



Tool Box Meeting on 20-05-21



Ground Floor Re-bar Work on 20-05-21

Project closed 13-19 May due to Eid-ul Fitre Vacation



Ground Floor-Column Concreting on 23-05-21



Ground Floor-Column Concreting on 23-05-21



Ground Floor-Column Concreting on 25-05-21



Ground Floor-Lift Core-Re-bar Work on 25-05-21



Ground Floor-Column Concreting on 26-05-21



Ground Floor-Roof Beam Shuttering on 26-05-21



Ground Floor-Lift Wall Shuttering on 30-05-21





Ground Floor-Column Concreting on 30-05-21



Ground Floor Stair Concreting on 31-05-21



Ground Floor Roof Slab Shuttering on 31-05-21



1st Floor Slab Shuttering on 03-06-21



1st Floor Slab Shutter Levelling on 03-06-21



Ground Floor Column Concreting on 06-06-21



1st Floor Beam Shuttering on 06-06-21



Ground floor Lift Core Shuttering on 07-06-21



Ground Floor Construction on 07-06-21



Ground Floor Stair Re-bar work on 09-06-21



1st floor Slab Shuttering on 09-06-21



Honourable RAJUK Charman Visit on 12-06-21



1st floor Slab Shuttering on 12-06-21



Ground Floor Lift Core Shuttering on 15-06-21



1st floor Slab Shuttering on 15-06-21
