



## TOTAL PROGRESS REPORT

From 22-December-2022 to 9-April-2023

Project Code:	59	Name:	Cityscape Tower-Retrofitting			
Client:	Cityscape	Contractor:	Cityscape International Ltd.			
Total Duration:	108	days	Total Working Days:	33	Total Manpower:	130
Planning Progress =	100%	Actual Progress=	78.3%	SPI=	0.78	Behind Schedule

### Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
01.1	Retrofit-Basement-3-Column-Lift	1sum	100	26-12-22	15-01-23	22-12-22	09-04-23	-84	
01.2	Retrofit-Basement-2-Column	1sum	100	16-01-23	05-02-23	26-01-23	09-04-23	-63	
01.3	Retrofit-Basement-1-Column	1sum	97	06-02-23	25-02-23	06-03-23	09-04-23	-43	Completed
01.4	Retrofit-upto GF-Column	1sum	0	26-02-23	15-03-23			0	Started
02	L-17 Slab extension work on west si	1sum	100	22-12-22	27-12-22	22-12-22	28-12-22	-1	

## Site Photographs



L-17 Slab Extension Re-bar Work on 22-12-22



L-17 Slab Extension Re-bar Work on 22-12-22



on 23-12-22





on 23-12-22



on 26-12-22





on 26-12-22



Level-17-Slab Extn Concreting on 28-12-22



Level-17-Slab Extn Concreting on 28-12-22



on 31-12-22





on 31-12-22



BUET Professor visiting on 02-01-23



on 02-01-23



on 03-01-23



on 03-01-23





Basement-3 Lift-wall Concreting on 09-01-23



Basement-3 Lift-wall Concreting on 09-01-23



on 11-01-23



on 11-01-23





on 17-01-23



on 17-01-23



on 26-01-23





on 26-01-23



Col.Retrofitting on 05-02-23



Shear Wall Retro. on 05-02-23





Basement-2-Column retrofitting on 08-02-23



Basement-2-Column retrofitting on 08-02-23

Work closed from 27-01-23 to 03-02-23

Labor Contractor claim for rate increasing





B-2 Col retrofit re-bar work on 15-02-23



Basement -3 Column Curing  
Ongoing

B-2 Col retrofit curing on 15-02-23





B-2-Col Re-bar work on 18-02-23



B2-Column Shuttering on 18-02-23





B-2 Col retrofit re-bar work on 20-02-23



B2-Col Retrofit re-bar work on 20-02-23





B-2 Col retrofit re-bar work on 22-02-23



B2-Col Retrofit re-bar work on 22-02-23



Retrofit-B-2 Column Shuttering on 27-02-23





Retrofit-B2-Column Concrete on 27-02-23



B-2-Column Retrofitting on 01-03-23









B-2-Col Re-bar work on 04-03-23



B2-Col Retrofit re-bar work on 04-03-23









B-1-Column retrofit curing on 06-03-23



B-1-Column retrofit re-bar work on 09-03-23
















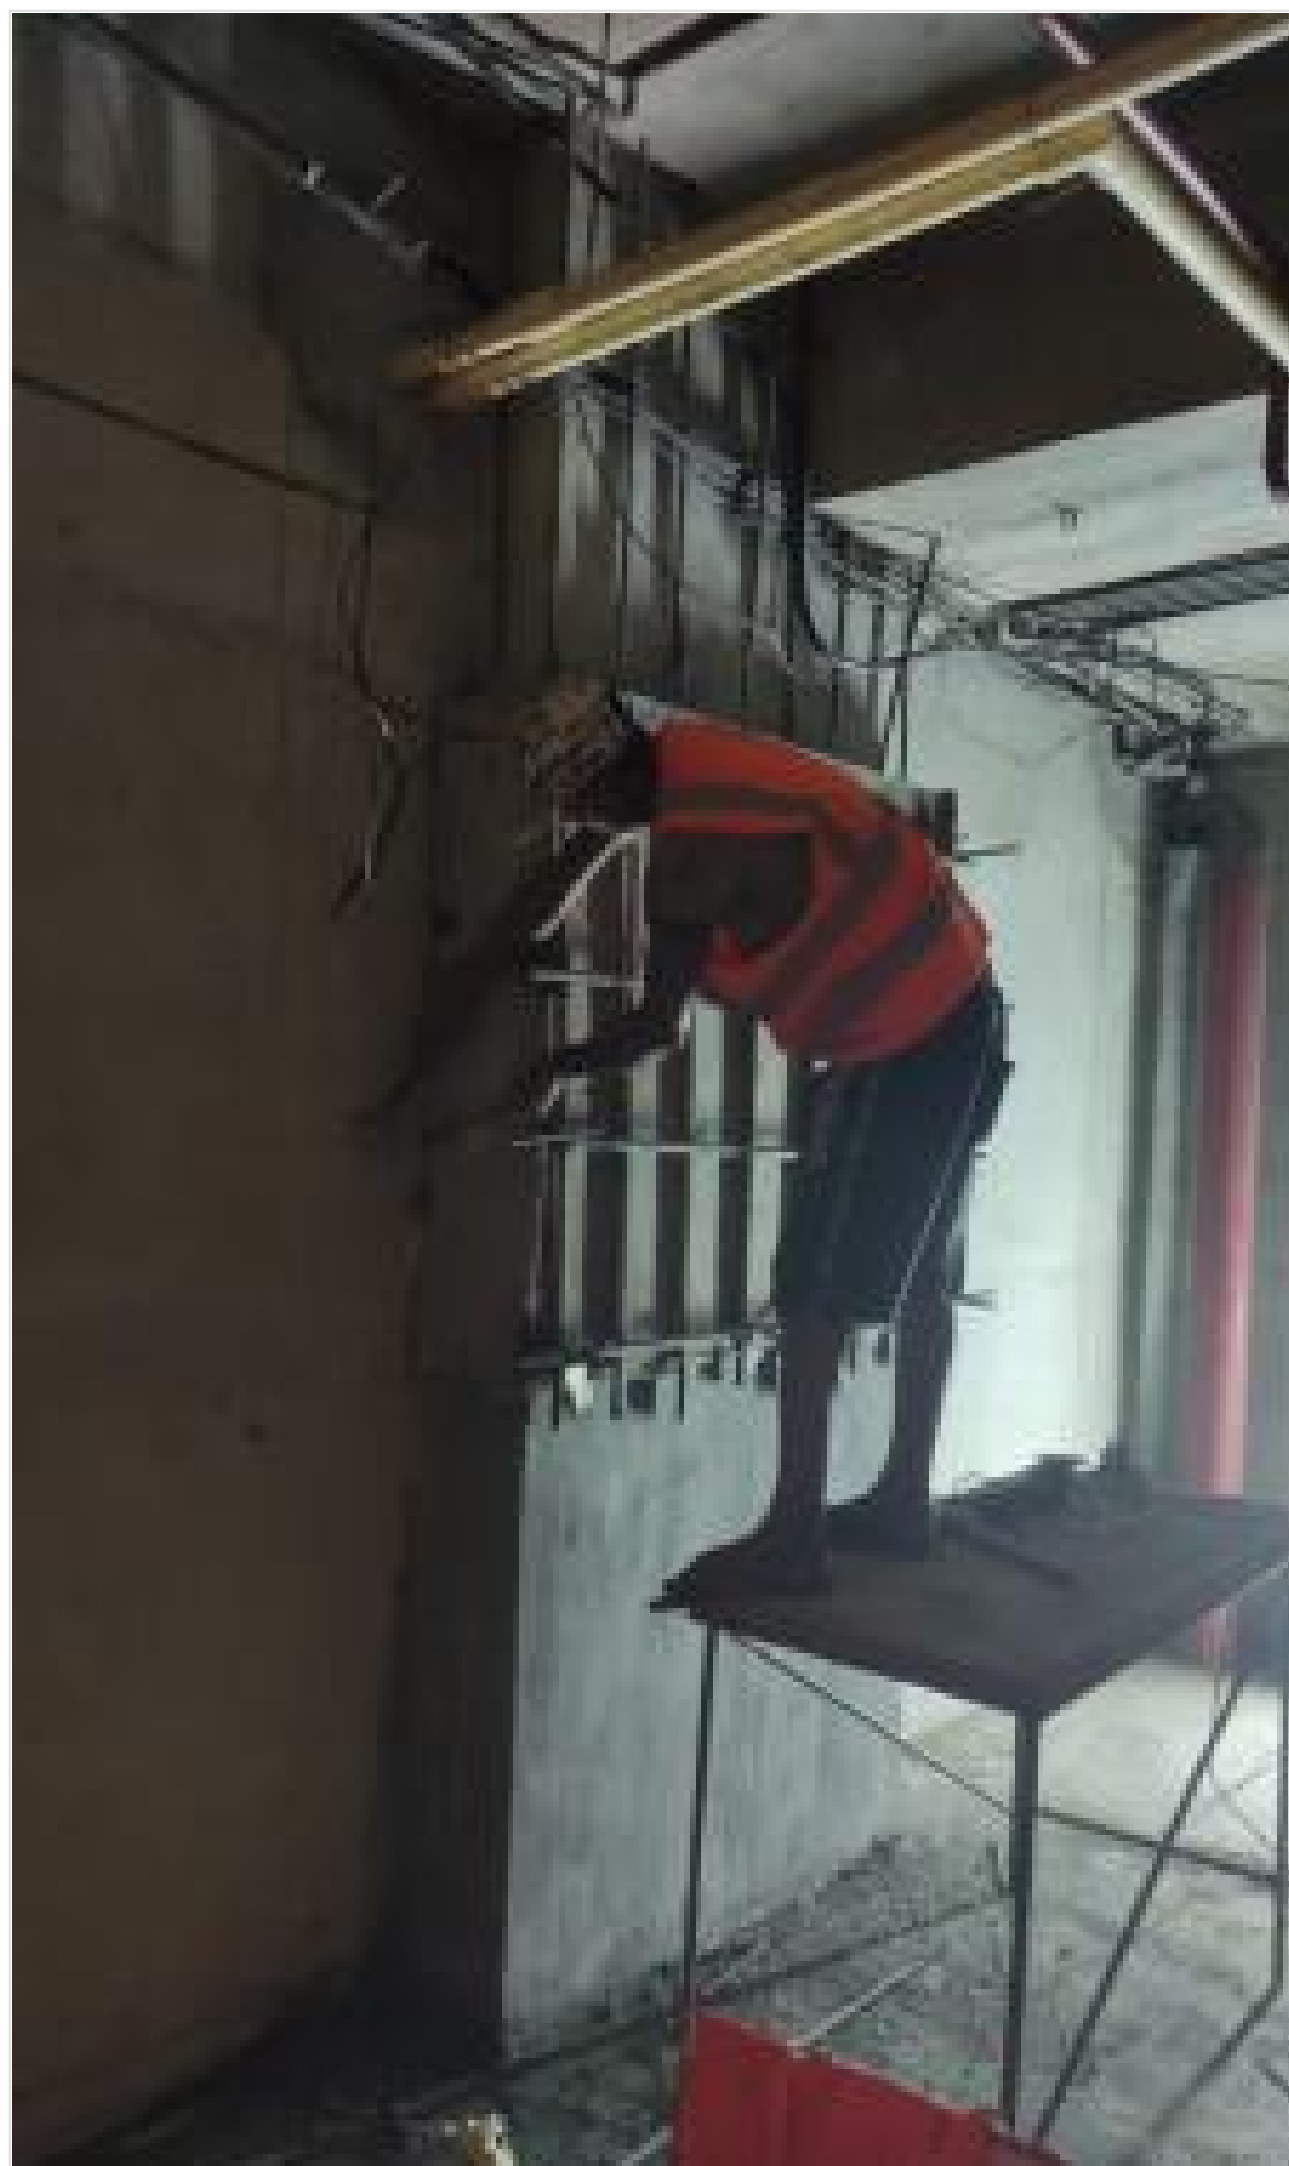



































B-3-Column retrofit concreting on 22-03-23



B-2-Column Retrofit shutter removing on 27-03-23









B-2 Column retrofit shuttering on 29-03-23



B-2-Column retrofit concreting on 29-03-23







B2-Col Retrofit re-bar work on 30-03-23



B-2-Column retrofit shuttering on 02-04-23























