

CONSTRUCTION OF URBAN RESILIENCE UNIT BUILDING AT MOHAKHALI, DHAKA

MONTHLY RUNNING PROGRESS



28 FEBRUARY 2022

Generated by: Elevate Builders Ltd.

TABLE OF CONTENTS

- o LAST MONTH PROGRESS
- o LAST MONTH MANPOWER HISTOGRAM
- o LAST MONTH PROGRESS CHART
- o DAILY PROGRESS REPORT
- o TOTAL PROGRESS
 - o TOTAL MANPOWER CHART
 - o CUMMULATIVE PROGRESS CHART
 - o SCHEDULE LEAD-LAG CHART
- o WORK PLAN AND PREOGRESS
- o PROGRESS PHOTO



MONTHLY PROGRESS REPORT

From 1-February-2022 to 28-February-2022


Project Code:	18	Name:	Urban Resilience Unit Building
Client:	Rajuk	Contractor:	Elevate Builders Ltd,

Monthly Progress


WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
1.3.10	Mobiliz-Shutter-RetainingWall-Basement-1	368m2	0	100	100	18-01-22	27-01-22	14-02-22
3.1.1.1.2	Basement-1-South-RetainingWall-1st-Formw	352m2	0	100	100	28-01-22	01-02-22	14-02-22
3.1.1.1.3	Basement-1-South-RetainingWall-1st-Inspe	176m2	0	100	100	02-02-22	02-02-22	14-02-22
3.1.1.1.4	Basement-1-South-RetainingWall-1st-Concr	176m2	0	100	100	03-02-22	03-02-22	14-02-22
3.1.1.2.1	Basement-1-South-RetainingWall-2nd-ReBar	176m2	0	100	100	05-02-22	06-02-22	18-02-22
3.1.1.2.2	Basement-1-South-RetainingWall-2nd-Formw	352m2	0	100	100	07-02-22	11-02-22	26-02-22
3.1.1.2.3	Basement-1-South-RetainingWall-2nd-Inspe	176m2	0	100	100	12-02-22	12-02-22	26-02-22
3.1.1.2.4	Basement-1-South-RetainingWall-2nd-Concr	176m2	0	100	100	13-02-22	13-02-22	26-02-22
3.1.2.1.2	Basement-1-South-Column-1st-Formwork	6nos	0	100	100	28-01-22	29-01-22	18-02-22
3.1.2.1.3	Basement-1-South-Column-1st-Inspection	6m2	0	100	100	30-01-22	30-01-22	18-02-22
3.1.2.1.4	Basement-1-South-Column-1st-Concreting	6nos	0	100	100	31-01-22	31-01-22	26-02-22
3.1.2.2.1	Basement-1-South-Column-2nd-ReBarWork	6nos	0	100	100	01-02-22	02-02-22	26-02-22
3.1.2.2.2	Basement-1-South-Column-2nd-Formwork	6nos	0	60	60	03-02-22	04-02-22	23-02-22
3.1.2.2.3	Basement-1-South-Column-2nd-Inspection	6nos	0	60	60	05-02-22	05-02-22	26-02-22
3.1.2.2.4	Basement-1-South-Column-2nd-Concreting	6nos	0	60	60	06-02-22	06-02-22	26-02-22

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
3.1.4.1	Basement-1-South-Stair-Form Work	1no.	0	60	60	23-02-22	28-02-22	12-02-22
3.1.4.2	Basement-1-South-Stair-Re-bar Work	1no.	0	60	60	28-02-22	03-03-22	26-02-22
3.2.1.1.1	Basement-1-North-RetainingWall-1st-ReBar	176m2	20	30	50	13-02-22	14-02-22	28-02-22
3.2.2.1.1	Basement-1-Shear Wall-1st-ReBarWork	108m2	60	10	70	13-02-22	14-02-22	28-02-22
3.2.3.1.1	Basement-1-North-Column-1st-Re-bar Work	1no.	0	100	100	10-02-22	11-02-22	03-02-22

MANPOWER HISTOGRAM

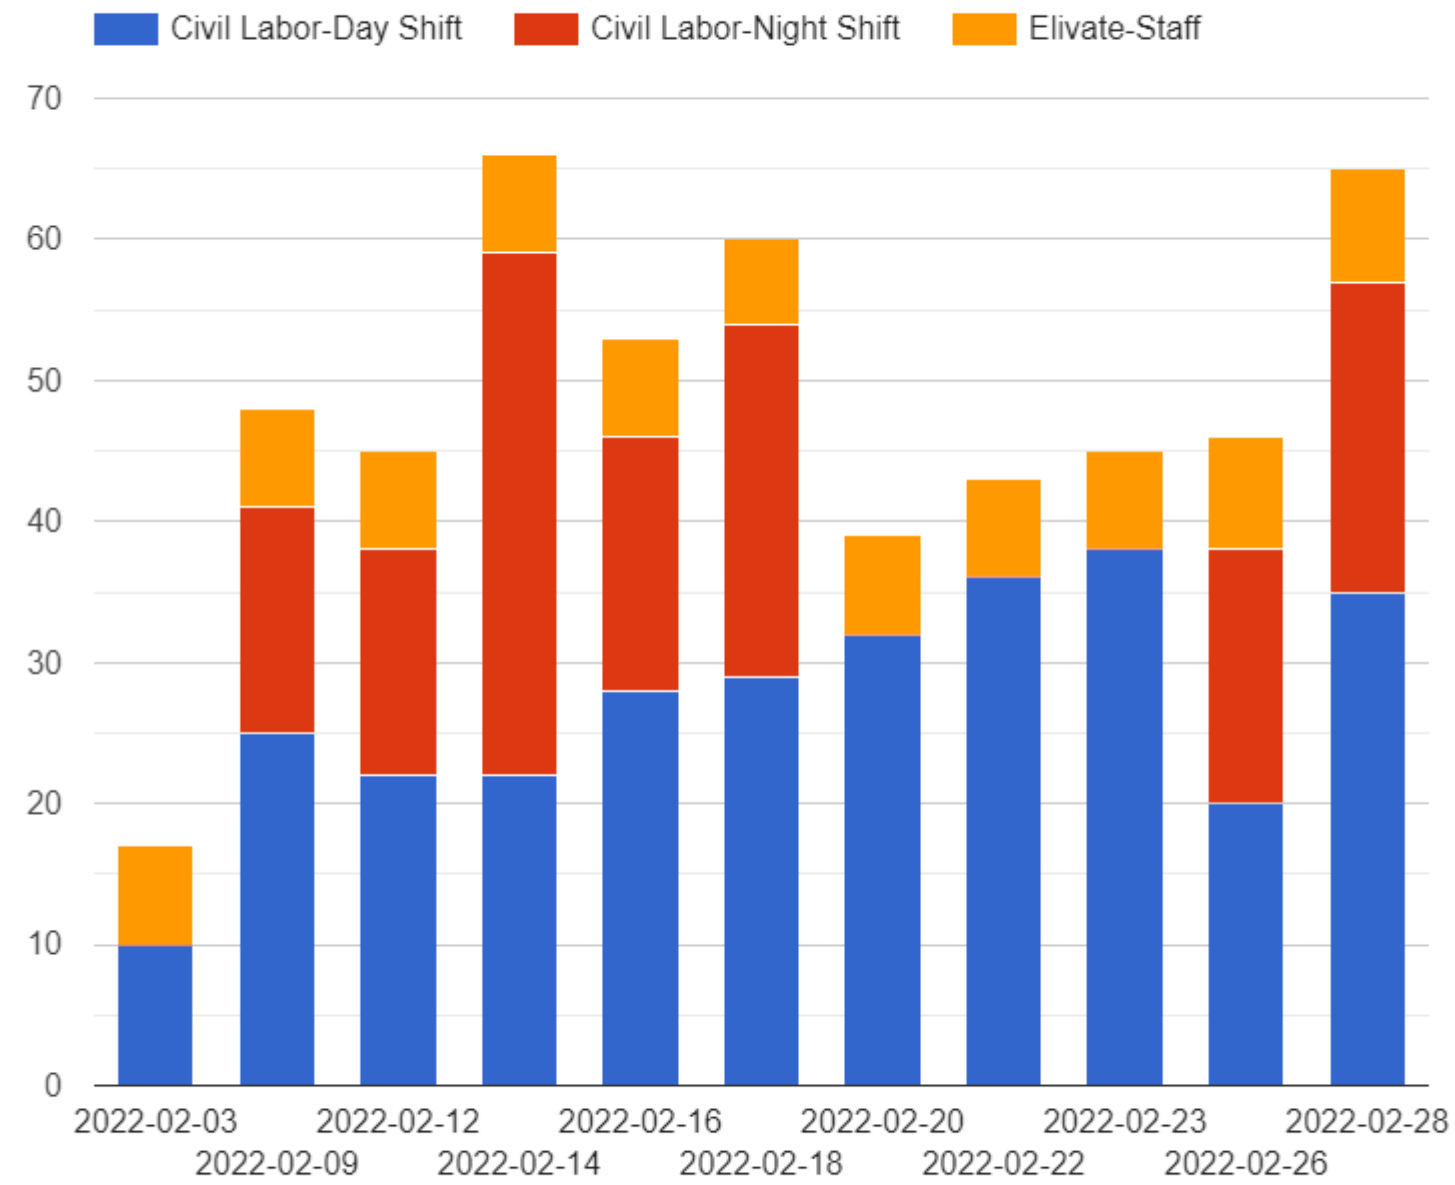

DAILY PROGRESS

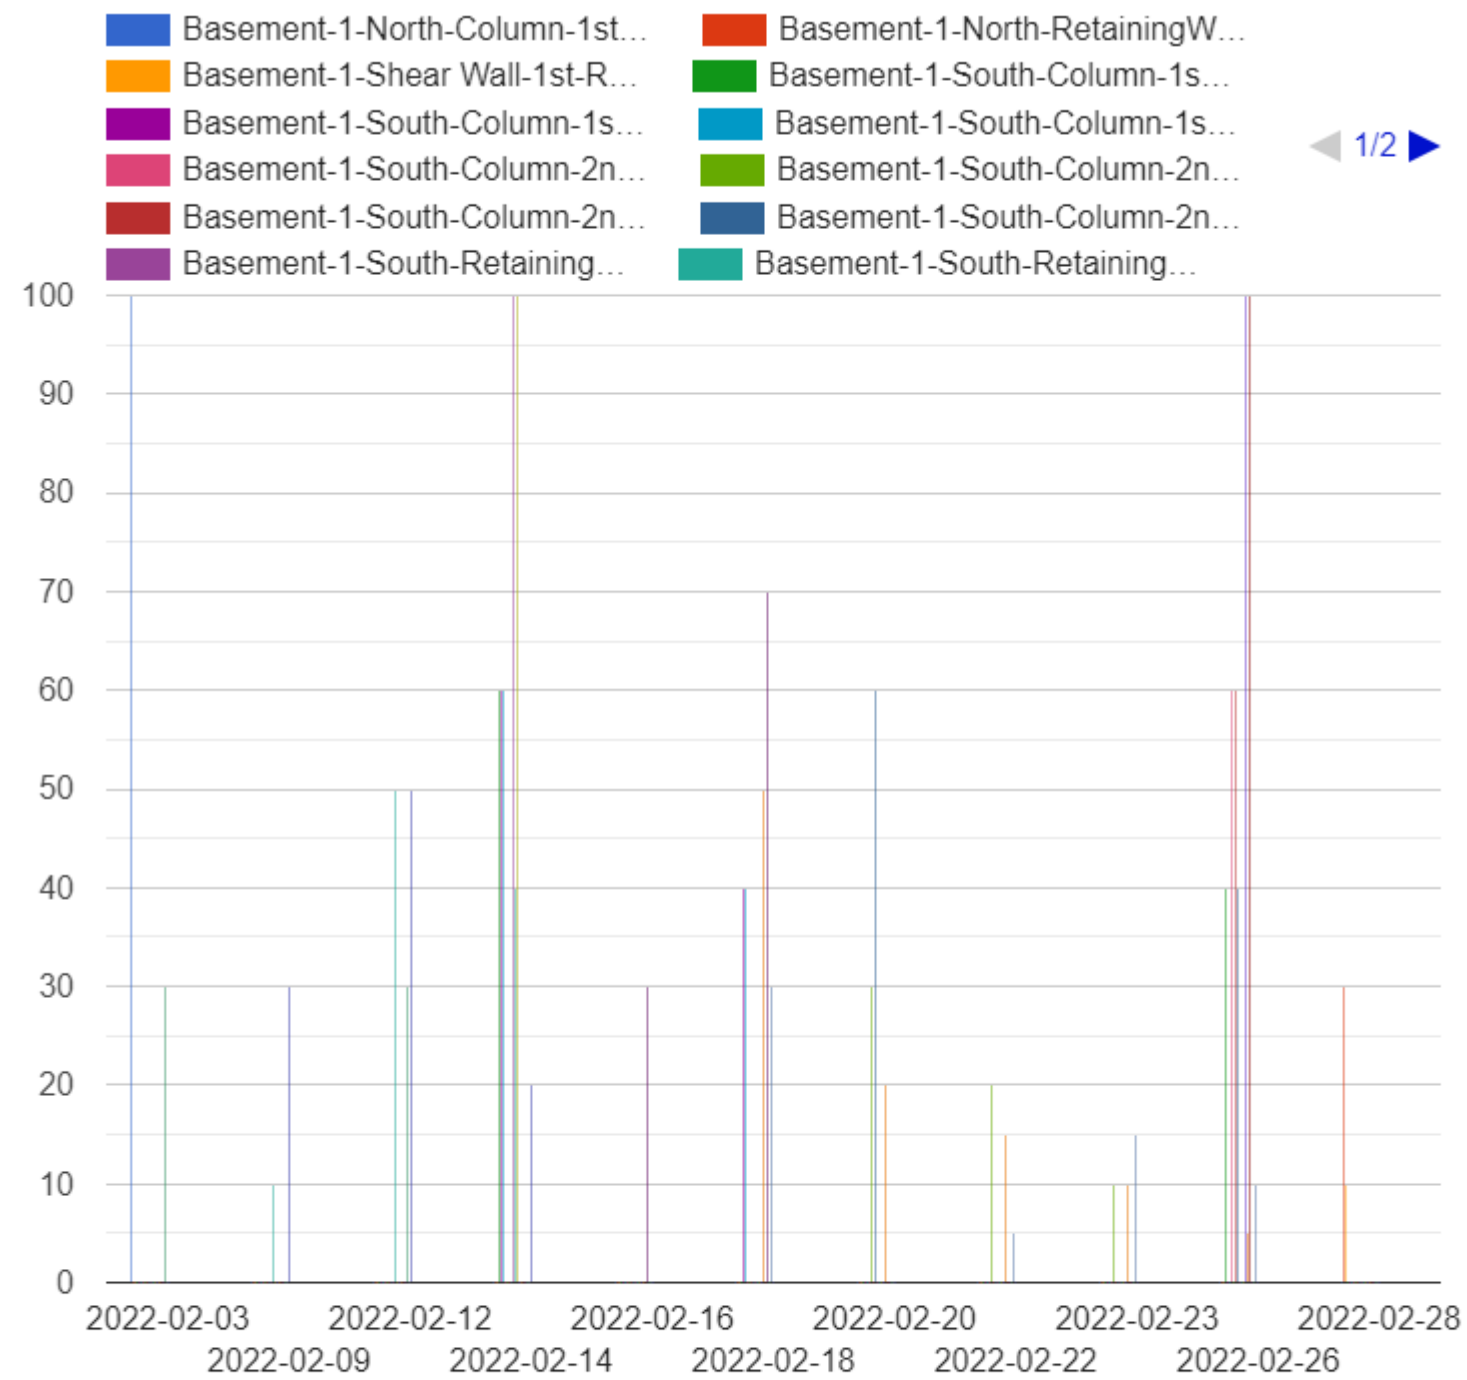



DAILY PROGRESS REPORT

Project:	Urban Resilience Unit Building	Project Code:	18	Date:	28-February-2022
Client:	Rajuk	Report	070	Day	Monday
Contractor:	Elevate Builders Ltd,			Climate	Sunny
					17-28C

Manpower

SN	Description	Nos.
01	Elivate-Staff	8
02	Civil Labor-Day Shift	35
03	Civil Labor-Night Shift	22
TOTAL		65

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
3.2.1.1.1	Basement-1-North-RetainingWall-1st-ReBar	176m2	30	50	13-02-22	14-02-22
3.2.2.1.1	Basement-1-Shear Wall-1st-ReBarWork	108m2	10	70	13-02-22	14-02-22

Site Photographs



B-1-North retaining wall rebar work



Basement-1-North Retaining wall-1st Lift

Site Description

Site Instruction

Entry by:

Planning Engineer

Generated by:

www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

TOTAL REPORT



TOTAL PROGRESS REPORT

From 16-October-2021 to 28-February-2022

Project Code:	18	Name:	Urban Resilience Unit Building
Client:	Rajuk	Contractor:	Elevate Builders Ltd,

Total Progress


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)
1.1	Mobilization-Labour	0	100	18-10-21	30-10-21	16-10-21	12-11-21	-13
1.2	Mobilization-Material	0	100	18-10-21	31-10-21	16-10-21	02-11-21	-2
1.3.01	Mobilization-Shutter-Scaffolding	50set	100	18-10-21	02-11-21	20-10-21	13-11-21	-11
1.3.02	Mobilization-Shutter-Pipe, Clamp, Base Plat	164m	100	18-10-21	02-11-21	21-10-21	13-11-21	-11
1.3.03	Mobilization-Shutter-Retaining Wall	368m2	100	18-10-21	31-10-21	24-10-21	04-11-21	-4
1.3.04	Mobilization-Shutter-Column	7set	100	18-10-21	24-10-21	10-11-21	10-11-21	-17
1.3.05	Mobilization-Shutter-Shear Wall	225m2	100	08-11-21	15-11-21	14-11-21	18-11-21	-3
1.3.06	Mobiliz-Shutter-Basement-1-South-Slab	862m2	100	09-11-21	19-11-21	16-11-21	11-01-22	-53
1.3.07	Mobilize-Shutter-Basement-1-North-Slab	862m2	100	23-11-21	03-12-21	29-12-21	12-01-22	-40
1.3.09	Mobilize Shutter-Ramp	1nos	100	15-01-22	22-01-22	27-12-21	28-01-22	-6
1.3.10	Mobiliz-Shutter-Retaining Wall-Basement-1	368m2	100	18-01-22	27-01-22	09-02-22	14-02-22	-18
2.1.1.1	Basement-2-South-Retaining Wall-2nd-Re-ba	147m2	100	10-11-21	14-11-21	21-10-21	18-11-21	-4
2.1.1.2	Basement-2-South-Retaining Wall-2nd-Formw	294m2	100	14-11-21	18-11-21	15-11-21	18-11-21	0
2.1.1.3	Basement-2-South-Retaining Wall-2nd-Inspe	147m2	100	19-11-21	19-11-21	18-11-21	18-11-21	1
2.1.1.4	Basement-2-South-Retaining Wall-2nd-Concr	147m2	100	20-11-21	20-11-21	18-11-21	18-11-21	2
2.1.2.1.1	Basement-2-South-Column-2nd-Re-bar	6nos	100	12-11-21	14-11-21	14-11-21	18-11-21	-4
2.1.2.1.2	Basement-2-South-Column-2nd-Formwork	6nos	100	14-11-21	16-11-21	14-11-21	18-11-21	-2
2.1.2.1.3	Basement-2-South-Column-2nd-Inspection	6nos	100	16-11-21	17-11-21	18-11-21	18-11-21	-1
2.1.2.1.4	Basement-2-South-Column-2nd-Concreting	6nos	100	17-11-21	17-11-21	18-11-21	18-11-21	-1
2.1.3.1	Basement-1-South-Slab-Formwork	862m2	100	21-11-21	26-11-21	25-11-21	11-01-22	-46
2.1.3.2	Basement-1-South-Slab-Re-bar Work	862m2	100	27-11-21	29-11-21	14-12-21	11-01-22	-43
2.1.3.3	Basement-1-South-Slab-Levelling	862m2	100	30-11-21	30-11-21	11-01-22	12-01-22	-43
2.1.3.4	Basement-1-South-Slab-Inspection	862m2	100	01-12-21	01-12-21	17-01-22	17-01-22	-47
2.1.3.5	Basement-1-South-Slab-Concreting	862m2	100	02-12-21	02-12-21	17-01-22	17-01-22	-46

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)
2.1.4.1	Basement-2-South-Stair-Form Work	1no.	100	23-11-21	28-11-21	19-12-21	11-01-22	-44
2.1.4.2	Basement-2-South-Stair-Rebar Work	1no.	100	28-11-21	01-12-21	19-12-21	11-01-22	-41
2.1.4.3	Basement-2-South-Stair-Inspection	1no.	100	01-12-21	01-12-21	17-01-22	17-01-22	-47
2.1.4.4	Basement-2-South-Stair-Concreting	1no.	100	02-12-21	02-12-21	17-01-22	17-01-22	-46
2.2.1.1.1	Basement-2-North-RetainingWall-1st-Re-ba	92m2	100	29-10-21	31-10-21	24-10-21	05-11-21	-5
2.2.1.1.2	Basement-2-North-RetainingWall-1st-Formw	184m2	100	31-10-21	04-11-21	30-10-21	05-11-21	-1
2.2.1.1.3	Basement-2-North-RetainingWall-1st-Inspe	92m2	100	05-11-21	05-11-21	04-11-21	04-11-21	1
2.2.1.1.4	Basement-2-North-RetainingWall-1st-Concr	92m2	100	06-11-21	06-11-21	05-11-21	05-11-21	1
2.2.1.2.1	Basement-2-North-RetainingWall-2nd-Re-ba	147m2	100	07-11-21	07-11-21	10-11-21	12-11-21	-5
2.2.1.2.2	Basement-2-North-RetainingWall-2nd-Formw	294m2	100	08-11-21	10-11-21	10-11-21	12-11-21	-2
2.2.1.2.3	Basement-2-North-RetainingWall-2nd-Inspe	147m2	100	11-11-21	11-11-21	12-11-21	12-11-21	-1
2.2.1.2.4	Basement-2-North-RetainingWall-2nd-Concr	147m2	100	12-11-21	12-11-21	12-11-21	12-11-21	0
2.2.2.1.1	Basement-2-Shear Wall-1st-ReBarWork	90m2	100	15-11-21	17-11-21	20-11-21	26-11-21	-9
2.2.2.1.2	Basement-2-Shear Wall-1st-Formwork	180m2	100	17-11-21	22-11-21	21-11-21	26-11-21	-4
2.2.2.1.3	Basement-2-Shear Wall-1st-Inspection	90m2	100	22-11-21	23-11-21	26-11-21	26-11-21	-3
2.2.2.1.4	Basement-2-Shear Wall-1st-Concreting	90m2	100	23-11-21	24-11-21	26-11-21	26-11-21	-2
2.2.2.2.1	Basement-2-Shear Wall-2nd-ReBarWork	90m2	100	25-11-21	27-11-21	30-11-21	10-12-21	-13
2.2.2.2.2	Basement-2-Shear Wall-2nd-Formwork	180m2	100	27-11-21	02-12-21	05-12-21	10-12-21	-8
2.2.2.2.3	Basement-2-Shear Wall-2nd-Inspection	90m2	100	02-12-21	03-12-21	10-12-21	10-12-21	-7
2.2.2.2.4	Basement-2-Shear Wall-2nd-Concreting	90m2	100	03-12-21	04-12-21	10-12-21	10-12-21	-6
2.2.3.1.1	Basement-2-Water Reservoir-1st-RebarWork	109m2	100	20-11-21	22-11-21	20-11-21	26-11-21	-4
2.2.3.1.2	Basement-2-Water Reservoir-1st-Formwork	217m2	100	22-11-21	24-11-21	22-11-21	26-11-21	-2
2.2.3.1.3	Basement-2-Water Reservoir-1st-Inspectio	109m2	100	25-11-21	25-11-21	26-11-21	26-11-21	-1
2.2.3.1.4	Basement-2-Water Reservoir-1st-Concretin	109m2	100	26-11-21	26-11-21	26-11-21	26-11-21	0
2.2.3.2.1	Basement-2-Water Reservoir-2nd-ReBarWork	109m2	100	21-01-22	21-01-22	30-11-21	28-01-22	-7
2.2.3.2.2	Basement-2-Water Reservoir-2nd-Formwork	217m2	100	22-01-22	26-01-22	01-12-21	28-01-22	-2
2.2.3.2.3	Basement-2-Water Reservoir-2nd-Inspectio	109m2	100	26-01-22	26-01-22	10-12-21	30-01-22	-4


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)
2.2.3.2.4	Basement-2-Water Reservoir-2nd-Concretin	109m2	100	26-01-22	26-01-22	10-12-21	30-01-22	-4
2.2.4.1.1	Basement-2-North-Column-1st-ReBarWork	1no	100	21-11-21	23-11-21	24-11-21	24-11-21	-1
2.2.4.1.2	Basement-2-North-Column-1st-Formwork	1no	100	23-11-21	25-11-21	25-11-21	25-11-21	0
2.2.4.1.3	Basement-2-North-Column-1st-Inspection	1no	100	25-11-21	26-11-21	26-11-21	25-11-21	1
2.2.4.1.4	Basement-2-North-Column-1st-Concreting	1no	100	26-11-21	27-11-21	26-11-21	26-11-21	1
2.2.4.2.1	Basement-2-North-Column-2nd-ReBarWork	1no	100	28-11-21	30-11-21	05-12-21	10-12-21	-10
2.2.4.2.2	Basement-2-North-Column-2nd-Formwork	1no.	100	30-11-21	02-12-21	05-12-21	10-12-21	-8
2.2.4.2.3	Basement-2-North-Column-2nd-Inspection	1no.	100	02-12-21	03-12-21	10-12-21	10-12-21	-7
2.2.4.2.4	Basement-2-North-Column-2nd-Concreting	1no.	100	03-12-21	04-12-21	10-12-21	10-12-21	-6
2.2.5.1	Basement-1-North-Slab-Formwork	862m2	100	05-12-21	09-12-21	27-12-21	11-01-22	-33
2.2.5.2	Basement-1-North-Slab-Re-bar Work	862m2	100	10-12-21	11-12-21	31-12-21	11-01-22	-31
2.2.5.3	Basement-1-North-Slab-Levelling	862m2	100	12-12-21	12-12-21	11-01-22	12-01-22	-31
2.2.5.4	Basement-1-North-Slab-Inspection	862m2	100	13-12-21	13-12-21	17-01-22	17-01-22	-35
2.2.5.5	Basement-1-North-Slab-Concreting	862m2	100	14-12-21	14-12-21	17-01-22	17-01-22	-34
2.2.6.1	Basement-2-North-Stair-Formwork	1no.	100	05-12-21	10-12-21	27-12-21	11-01-22	-32
2.2.6.2	Basement-2-North-Stair-Rebar work	1no.	100	10-12-21	13-12-21	27-12-21	11-01-22	-29
2.2.6.3	Basement-2-North-Stair-Inspection	1no.	100	13-12-21	14-12-21	17-01-22	17-01-22	-34
2.2.6.4	Basement-2-North-Stair-Concreting	1no.	100	14-12-21	14-12-21	17-01-22	17-01-22	-34
2.2.7.1	Basement-2-Ramp-Formwork	1no.	100	22-01-22	25-01-22	27-12-21	30-01-22	-5
2.2.7.2	Basement-2-Ramp-Rebar-work	1no.	100	25-01-22	26-01-22	27-12-21	30-01-22	-4
2.2.7.3	Basement-2-Ramp-Inspection	1no.	100	26-01-22	26-01-22	30-01-22	30-01-22	-4
2.2.7.4	Basement-2-Ramp-Concreting	1no.	100	26-01-22	26-01-22	30-01-22	30-01-22	-4
3.1.1.1.1	Basement-1-South-RetainingWall-1st-ReBar	176m2	100	26-01-22	28-01-22	20-01-22	24-01-22	4
3.1.1.1.2	Basement-1-South-RetainingWall-1st-Formw	352m2	100	28-01-22	01-02-22	09-02-22	14-02-22	-13
3.1.1.1.3	Basement-1-South-RetainingWall-1st-Inspe	176m2	100	02-02-22	02-02-22	14-02-22	14-02-22	-12
3.1.1.1.4	Basement-1-South-RetainingWall-1st-Concr	176m2	100	03-02-22	03-02-22	14-02-22	14-02-22	-11
3.1.1.2.1	Basement-1-South-RetainingWall-2nd-ReBar	176m2	100	05-02-22	06-02-22	16-02-22	18-02-22	-12

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)
3.1.1.2.2	Basement-1-South-RetainingWall-2nd-Formw	352m2	100	07-02-22	11-02-22	18-02-22	26-02-22	-15
3.1.1.2.3	Basement-1-South-RetainingWall-2nd-Inspe	176m2	100	12-02-22	12-02-22	26-02-22	26-02-22	-14
3.1.1.2.4	Basement-1-South-RetainingWall-2nd-Concr	176m2	100	13-02-22	13-02-22	26-02-22	26-02-22	-13
3.1.2.1.1	Basement-1-South-Column-1st-Re-Bar Work	6nos	100	26-01-22	27-01-22	24-01-22	24-01-22	3
3.1.2.1.2	Basement-1-South-Column-1st-Formwork	6nos	100	28-01-22	29-01-22	14-02-22	18-02-22	-20
3.1.2.1.3	Basement-1-South-Column-1st-Inspection	6m2	100	30-01-22	30-01-22	14-02-22	18-02-22	-19
3.1.2.1.4	Basement-1-South-Column-1st-Concreting	6nos	100	31-01-22	31-01-22	14-02-22	26-02-22	-26
3.1.2.2.1	Basement-1-South-Column-2nd-ReBarWork	6nos	100	01-02-22	02-02-22	20-02-22	26-02-22	-24
3.1.2.2.2	Basement-1-South-Column-2nd-Formwork	6nos	60	03-02-22	04-02-22	20-02-22	23-02-22	-19
3.1.2.2.3	Basement-1-South-Column-2nd-Inspection	6nos	60	05-02-22	05-02-22	26-02-22	26-02-22	-21
3.1.2.2.4	Basement-1-South-Column-2nd-Concreting	6nos	60	06-02-22	06-02-22	26-02-22	26-02-22	-20
3.1.4.1	Basement-1-South-Stair-Form Work	1no.	60	23-02-22	28-02-22	03-02-22	12-02-22	16
3.1.4.2	Basement-1-South-Stair-Re-bar Work	1no.	60	28-02-22	03-03-22	18-02-22	26-02-22	5
3.2.1.1.1	Basement-1-North-RetainingWall-1st-ReBar	176m2	50	13-02-22	14-02-22	26-01-22	28-02-22	-14
3.2.2.1.1	Basement-1-Shear Wall-1st-ReBarWork	108m2	70	13-02-22	14-02-22	24-01-22	28-02-22	-14
3.2.3.1.1	Basement-1-North-Column-1st-Re-bar Work	1no.	100	10-02-22	11-02-22	03-02-22	03-02-22	8


DAILY MANPOWER

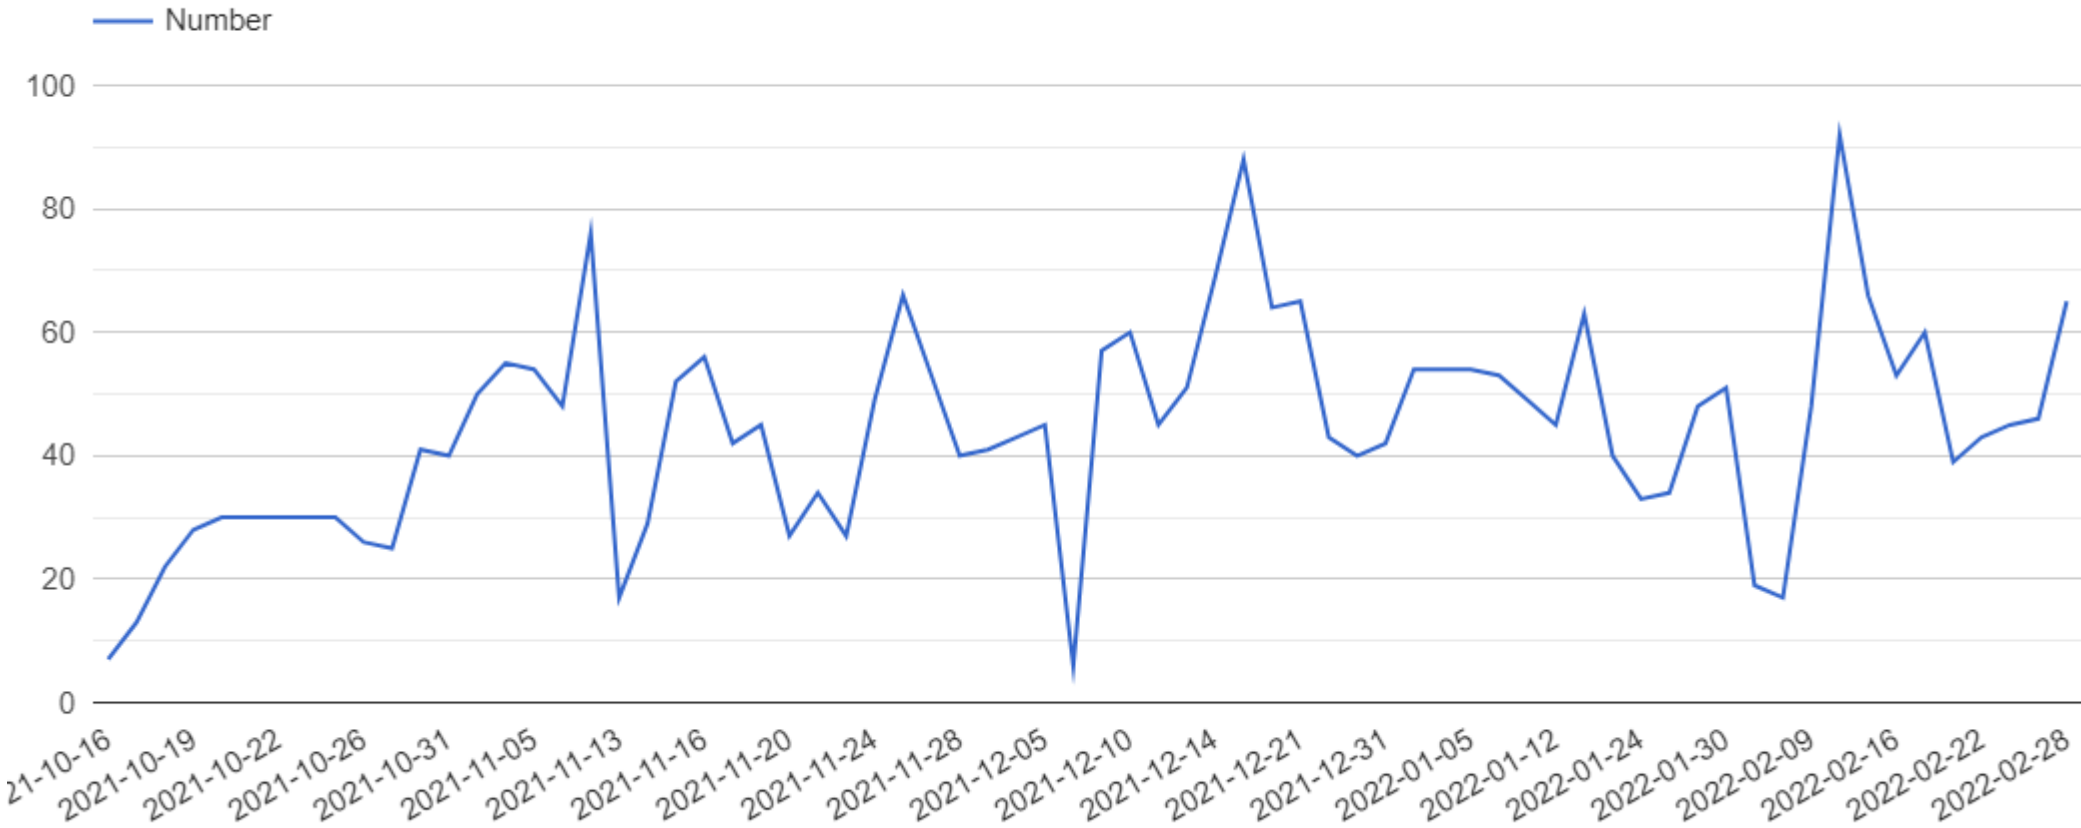

CUMMULATIVE WORK PROGRESS

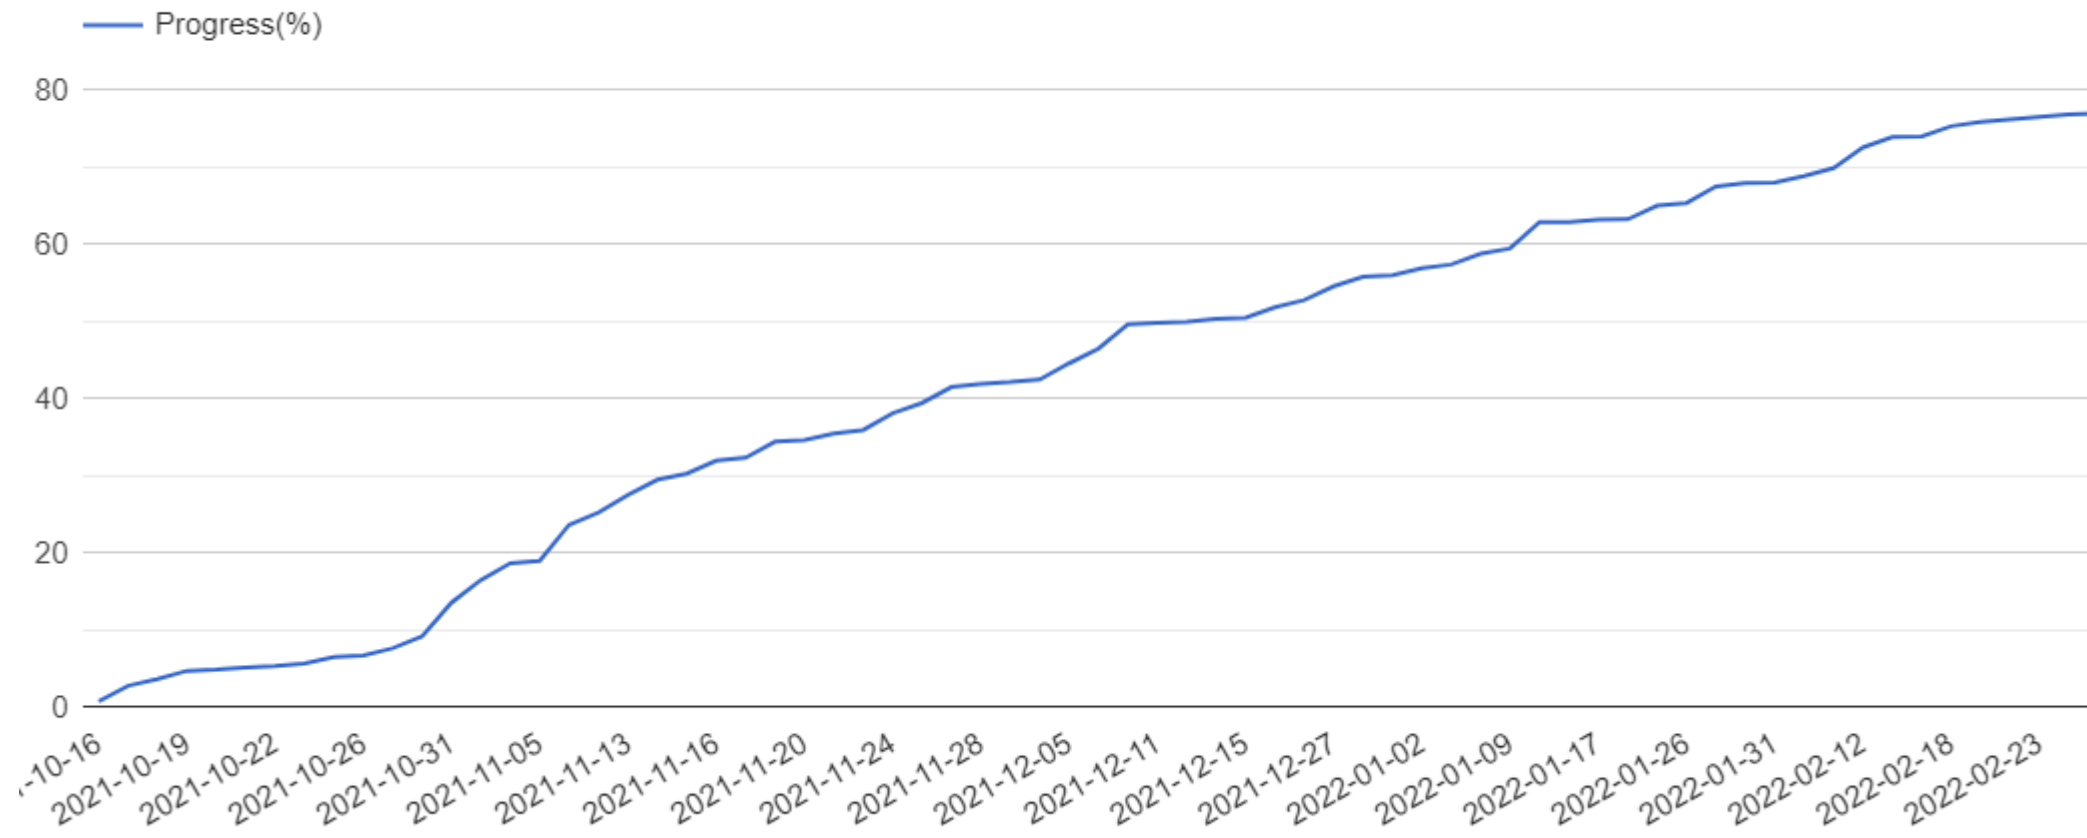

SCHEDULE AHEAD-BEHIND

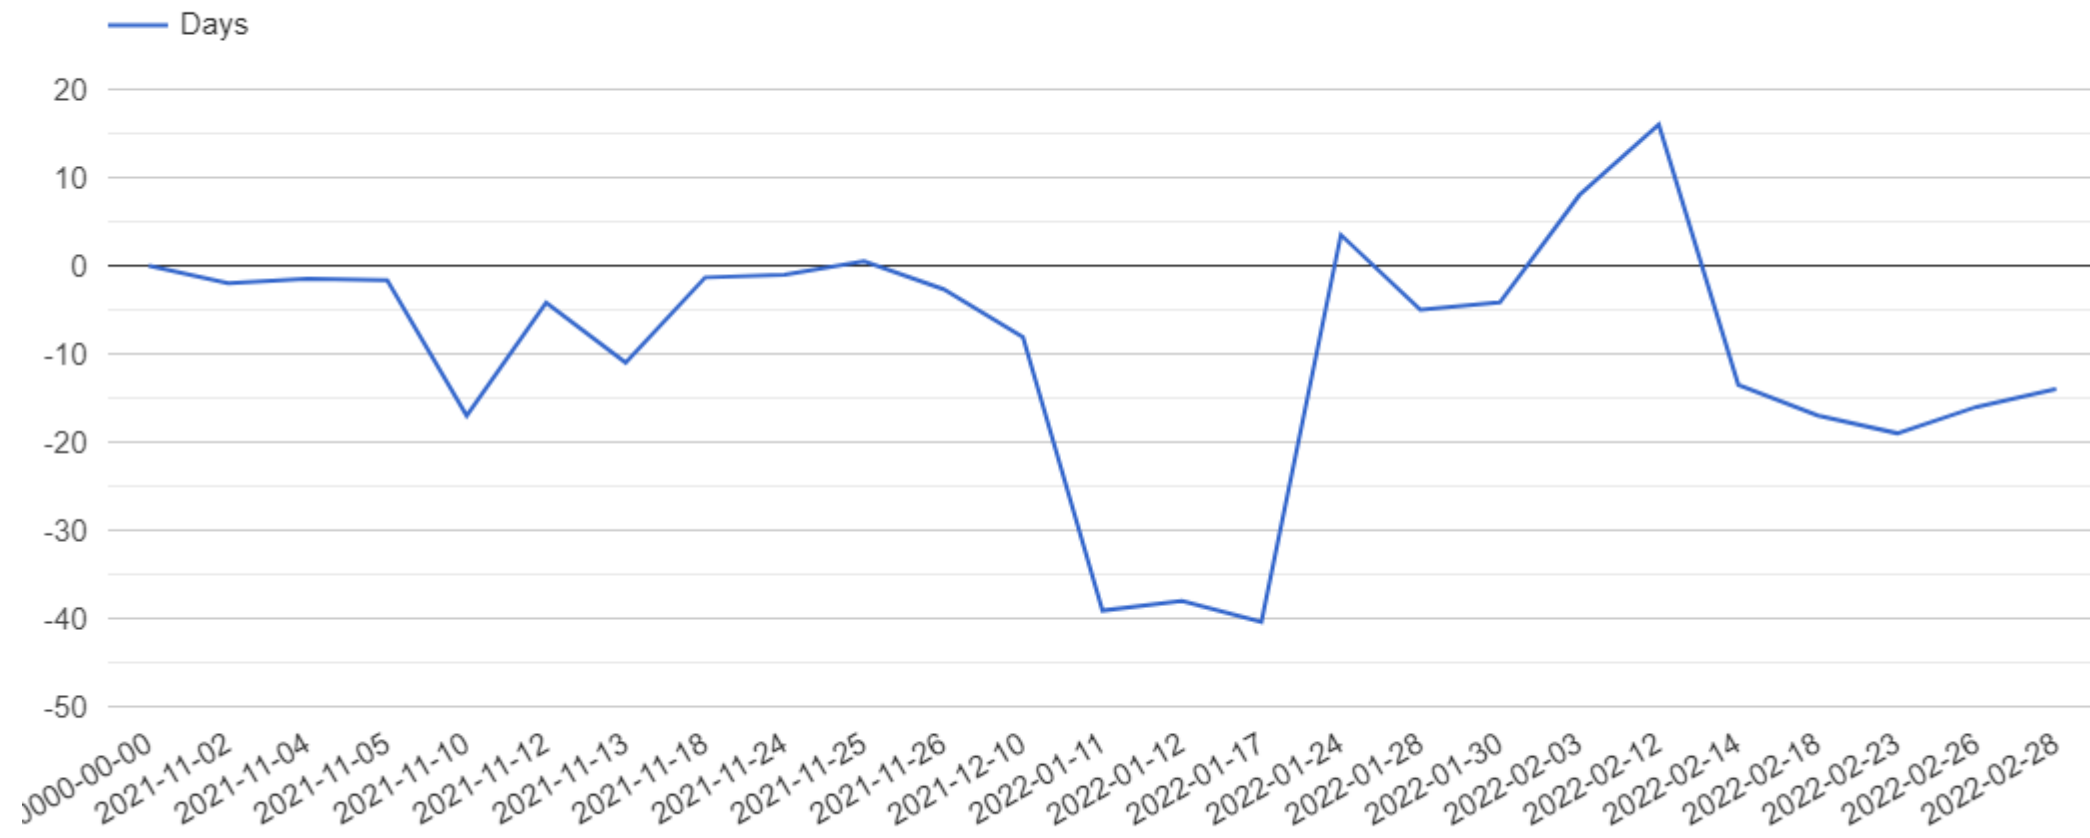

WORK PLAN AND PROGRESS

WORK PLAN (REV-2.0) AND PROGRESS FOR URBAN RESILIENCE UNIT BUILDING

Sl.	Task Name	Duration	Start	Finish	% Complete	'21	Nov '21			Dec '21			Jan '22			Feb '22			Mar '22														
						16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19	26	05	12						
1	Urban Resilience Unit Building	149 d	18-10-21	15-03-22	72%																												
1.1	Mobilization	119 d	18-10-21	14-02-22	93%																												
1.1.1	Labour	13 d	18-10-21	30-10-21	100%																												
1.1.2	Materials	14 d	18-10-21	31-10-21	100%																												
1.1.3	Shutter	119 d	18-10-21	14-02-22	91%																												
1.1.3.1	Scaffolding	16 d	18-10-21	02-11-21	100%																												
1.1.3.2	Pipe, Clamp and Base plate. U-Head	16 d	18-10-21	02-11-21	100%																												
1.1.3.3	Retaining Wall-184m2	14 d	18-10-21	31-10-21	100%																												
1.1.3.4	Column	7 d	18-10-21	24-10-21	100%																												
1.1.3.5	Shear Wall	7 d	08-11-21	15-11-21	100%																												
1.1.3.6	Slab Shutter-South-Basement-1	10 d	09-11-21	19-11-21	100%																												
1.1.3.7	Slab Shutter-North-Basement-1	10 d	23-11-21	03-12-21	100%																												
1.1.3.8	Slab Shutter-South-Ground Floor	10 d	04-02-22	14-02-22	0%																												
1.1.3.9	Ramp	7 d	15-01-22	22-01-22	100%																												
1.1.3.10	Retaining Wall-Basement-1	10 d	18-01-22	27-01-22	100%																												
1.2	Basement-2	90 d	29-10-21	26-01-22	100%																												
1.3	Basement-1	49 d	26-01-22	15-03-22	25%																												
1.3.1	South Part	38 d	26-01-22	04-03-22	53%																												
1.3.1.1	Retaining Wall	19 d	26-01-22	13-02-22	88%																												
1.3.1.1.1	1st Lift	9 d	26-01-22	03-02-22	100%																												
1.3.1.1.2	2nd Lift	9 d	05-02-22	13-02-22	75%																												
1.3.1.1.2.1	Re-bar Work	2 d	05-02-22	06-02-22	100%																												
1.3.1.1.2.2	Form Work	5 d	07-02-22	11-02-22	95%																												
1.3.1.1.2.3	Inspection	1 d	12-02-22	12-02-22	0%																												
1.3.1.1.2.4	Concreting	1 d	13-02-22	13-02-22	0%																												
1.3.1.2	Column	12 d	26-01-22	06-02-22	80%																												
1.3.1.2.1	1st Lift	6 d	26-01-22	31-01-22	100%																												
1.3.1.2.1.1	Re-bar Work	2 d	26-01-22	27-01-22	100%																												
1.3.1.2.1.2	Form Work	2 d	28-01-22	29-01-22	100%																												
1.3.1.2.1.3	Inspection	1 d	30-01-22	30-01-22	100%																												
1.3.1.2.1.4	Concreting	1 d	31-01-22	31-01-22	100%																												
1.3.1.2.2	2nd Lift	6 d	01-02-22	06-02-22	60%																												
1.3.1.2.2.1	Re-bar Work	2 d	01-02-22	02-02-22	60%																												
1.3.1.2.2.2	Form Work	2 d	03-02-22	04-02-22	60%																												
1.3.1.2.2.3	Inspection	1 d	05-02-22	05-02-22	60%																												
1.3.1.2.2.4	Concreting	1 d	06-02-22	06-02-22	60%																												
1.3.1.3	Roof Slab	17 d	16-02-22	04-03-22	0%																												
1.3.1.4	Stair	10 d	23-02-22	04-03-22	48%																												
1.3.1.4.1	Form Work	5 d	23-02-22	28-02-22	60%																												
1.3.1.4.2	Re-bar Work	3 d	28-02-22	03-03-22	60%																												
1.3.1.4.3	Inspection	1 d	03-03-22	04-03-22	0%																												
1.3.1.4.4	Concreting	1 d	04-03-22	04-03-22	0%																												
1.3.2	North Part	34 d	10-02-22	15-03-22	5%																												
1.3.2.1	Retaining Wall	19 d	13-02-22	03-03-22	3%																												
1.3.2.1.1	1st Lift	8 d	13-02-22	20-02-22	6%																												
1.3.2.1.1.1	Re-bar Work	1 d	13-02-22	14-02-22	50%																												

WORK PLAN (REV-2.0) AND PROGRESS FOR URBAN RESILIENCE UNIT BUILDING

Sl.	Task Name	Duration	Start	Finish	% Complete	'21		Nov '21				Dec '21				Jan '22				Feb '22				Mar '2		
						16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19	26	05
1.3.2.1.1.2	Form Work	5 d	14-02-22	18-02-22	0%																					
1.3.2.1.1.3	Inspection	1 d	19-02-22	19-02-22	0%																					
1.3.2.1.1.4	Concreting	1 d	20-02-22	20-02-22	0%																					
1.3.2.1.2	2nd Lift	9 d	23-02-22	03-03-22	0%																					
1.3.2.2	Shear Wall	18 d	13-02-22	02-03-22	8%																					
1.3.2.2.1	1st Lift	8 d	13-02-22	20-02-22	16%																					
1.3.2.2.1.1	Re-bar Work	2 d	13-02-22	14-02-22	70%																					
1.3.2.2.1.2	Form Work	5 d	14-02-22	18-02-22	0%																					
1.3.2.2.1.3	Inspection	1 d	19-02-22	19-02-22	0%																					
1.3.2.2.1.4	Concreting	1 d	20-02-22	20-02-22	0%																					
1.3.2.2.2	2nd Lift	9 d	22-02-22	02-03-22	0%																					
1.3.2.3	Column	15 d	10-02-22	24-02-22	14%																					
1.3.2.3.1	1st Lift	7 d	10-02-22	16-02-22	29%																					
1.3.2.3.1.1	Re-bar Work	2 d	10-02-22	11-02-22	100%																					
1.3.2.3.1.2	Form Work	3 d	12-02-22	14-02-22	0%																					
1.3.2.3.1.3	Inspection	1 d	15-02-22	15-02-22	0%																					
1.3.2.3.1.4	Concreting	1 d	16-02-22	16-02-22	0%																					
1.3.2.3.2	2nd Lift	7 d	18-02-22	24-02-22	0%																					
1.3.2.4	Roof Slab	11 d	05-03-22	15-03-22	0%																					
1.3.2.5	Stair	10 d	06-03-22	15-03-22	0%																					
1.3.2.6	Ramp	5 d	11-03-22	15-03-22	0%																					

Task



Summary



Rolled Up Progress



Critical Task



Rolled Up Task



Project Summary



Progress



Rolled Up Critical Task



Group By Summary



PROGRESS PHOTO

Site Photographs



South stair shutter on 03-02-22



Overall site on 03-02-22

Site Description

Site Instruction



South Retaining wall on 09-02-22



South Retaining wall shuttering on 09-02-22

Site Description

Site Instruction



Basement-1-South Retaining wall on 12-02-22



Basement-1-South Retaining Wall-Shutteri on 12-02-22

Site Description

Site Instruction



Ready mix on 14-02-22



Concreting on 14-02-22

Site Description

Site Instruction




Basement-1-South retaining wall 2nd lift on 16-02-22



Basement-1-south retaining wall-Re-bar on 16-02-22

Site Description

Site Instruction

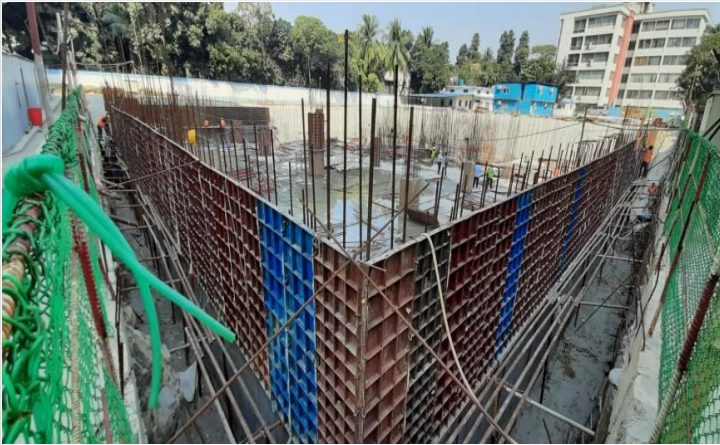

South 2nd lift retaining wall on 18-02-22



Shuttering work on 18-02-22

Site Description

Site Instruction



Retaining wall shuttering on 20-02-22

Column shuttering on 20-02-22

Site Description

2nd Half was rain

Site Instruction



South retaining wall on 22-02-22

South stair work on 22-02-22

Site Description

Site Instruction



Basement-1-South retaining wall on 23-02-22

Basement-1-South Column shuttering on 23-02-22

Site Description

Site Instruction



Ready-mix Concrete Truck and Pump on 26-02-22



B-1-South 2nd Retaining wall concreting on 26-02-22

Site Description

Site Instruction



B-1-North retaining wall rebar work on 28-02-22



Basement-1-North Retaining wall-1st Lift on 28-02-22

Site Description

Site Instruction

Entry by:
Planning Engineer

Generated by:
www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
