

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

Sl.	Task Name	Duration	Start	Finish	% Complete	Timeline																																																																																									
						Jan '16						Feb '16						Mar '16						Apr '16						May '16						Jun '16						Jul '16						Aug '16						Sep '16						Oct '16						Nov '16						Dec '16						Jan '17						Feb '17						Mar '17					
1	AIR FORCE STUDIO APT-JESSORE	418 d	17-01-16	31-03-17	2%																																																																																										
1.1	Agreement	3 d	10-02-16	12-02-16	0%																																																																																										
1.2	Civil Work	416 d	17-01-16	29-03-17	3%																																																																																										
1.2.1	Preliminarey Works	56 d	17-01-16	12-03-16	70%																																																																																										
1.2.1.1	Hand-over of Site to Start	2 d	17-01-16	18-01-16	100%																																																																																										
1.2.1.2	Soil Test	6 d	17-01-16	22-01-16	40%																																																																																										
1.2.1.3	Structural Design-Foundation	15 d	23-01-16	06-02-16	100%																																																																																										
1.2.1.4	Mobilization and Site office Construction	30 d	12-02-16	12-03-16	50%																																																																																										
1.2.1.5	Tree Cutting by Client	3 d	19-01-16	21-01-16	100%																																																																																										
1.2.1.6	Layout	5 d	07-02-16	11-02-16	100%																																																																																										
1.2.2	Substructure	118 d	15-02-16	11-06-16	2%																																																																																										
1.2.2.1	Pile Work-314 nos	81 d	15-02-16	05-05-16	14%																																																																																										
1.2.2.1.1	Pile Boring	60 d	15-02-16	14-04-16	34%																																																																																										
1.2.2.1.2	Excavation for Pile Head Breaking	45 d	15-03-16	28-04-16	0%																																																																																										
1.2.2.1.3	Pile Head Breaking	45 d	22-03-16	05-05-16	0%																																																																																										
1.2.2.2	Pile Cap- 50 nos	56 d	18-03-16	12-05-16	0%																																																																																										
1.2.2.2.1	CC Work	45 d	18-03-16	08-05-16	0%																																																																																										
1.2.2.2.2	Re-bar fixing	45 d	19-03-16	10-05-16	0%																																																																																										
1.2.2.2.3	Shuttering	45 d	19-03-16	11-05-16	0%																																																																																										
1.2.2.2.4	Concreting	45 d	19-03-16	12-05-16	0%																																																																																										
1.2.2.3	Under Ground Water Reservoir	42 d	29-04-16	09-06-16	0%																																																																																										
1.2.2.3.1	Base	20 d	29-04-16	18-05-16	0%																																																																																										
1.2.2.3.1.1	Excavation	10 d	29-04-16	08-05-16	0%																																																																																										
1.2.2.3.1.2	CC Work	7 d	05-05-16	11-05-16	0%																																																																																										
1.2.2.3.1.3	Re-bar Fixing	10 d	05-05-16	14-05-16	0%																																																																																										
1.2.2.3.1.4	Shuttering	10 d	08-05-16	17-05-16	0%																																																																																										
1.2.2.3.1.5	Concreting	10 d	09-05-16	18-05-16	0%																																																																																										
1.2.2.3.2	Wall	19 d	12-05-16	30-05-16	0%																																																																																										
1.2.2.3.2.1	1st Lift	13 d	12-05-16	24-05-16	0%																																																																																										
1.2.2.3.2.1.1	Re-bar Fixing	10 d	12-05-16	21-05-16	0%																																																																																										
1.2.2.3.2.1.2	Shuttering	10 d	14-05-16	23-05-16	0%																																																																																										
1.2.2.3.2.1.3	Concreting	10 d	15-05-16	24-05-16	0%																																																																																										
1.2.2.3.2.2	2nd Lift	13 d	18-05-16	30-05-16	0%																																																																																										
1.2.2.3.2.2.1	Re-bar Fixing	10 d	18-05-16	27-05-16	0%																																																																																										
1.2.2.3.2.2.2	Shuttering	10 d	20-05-16	29-05-16	0%																																																																																										
1.2.2.3.2.2.3	Concreting	10 d	21-05-16	30-05-16	0%																																																																																										
1.2.2.3.3	Top Slab	10 d	31-05-16	09-06-16	0%																																																																																										
1.2.2.3.3.1	Shuttering	5 d	31-05-16	04-06-16	0%																																																																																										
1.2.2.3.3.2	Re-bar Fixing	4 d	05-06-16	08-06-16	0%																																																																																										
1.2.2.3.3.3	Concreting	1 d	09-06-16	09-06-16	0%																																																																																										
1.2.2.3.4	Tower Crane Fondation	15 d	13-05-16	27-05-16	0%																																																																																										
1.2.2.4	Shear Wall	64 d	20-03-16	22-05-16	0%																																																																																										
1.2.2.4.1	Base	17 d	29-04-16	15-05-16	0%																																																																																										
1.2.2.4.1.1	Excavation	10 d	29-04-16	08-05-16	0%																																																																																										
1.2.2.4.1.2	CC Work	10 d	01-05-16	10-05-16	0%																																																																																										
1.2.2.4.1.3	Re-bar Fixing	10 d	03-05-16	12-05-16	0%																																																																																										
1.2.2.4.1.4	Shuttering	10 d	05-05-16	14-05-16	0%																																																																																										
1.2.2.4.1.5	Concreting	10 d	06-05-16	15-05-16	0%																																																																																										
1.2.2.4.2	Wall	14 d	09-05-16	22-05-16	0%																																																																																										
1.2.2.4.2.1	Re-bar Fixing	10 d	09-05-16	18-05-16	0%																																																																																										
1.2.2.4.2.2	Shuttering	10 d	12-05-16	21-05-16	0%																																																																																										
1.2.2.4.2.3	Concreting	10 d	13-05-16	22-05-16	0%																																																																																										
1.2.2.4.3	Padestal-35 nos	58 d	20-03-16	16-05-16	0%																																																																																										
1.2.2.4.3.1	Re-bar Fixing	45 d	20-03-16	14-05-16	0%																																																																																										
1.2.2.4.3.2	Shuttering	45 d	20-03-16	15-05-16	0%																																																																																										
1.2.2.4.3.3	Concreting	45 d	20-03-16	16-05-16	0%																																																																																										
1.2.2.5	Anchor Bolt Setting	14 d	17-05-16	30-05-16	0%																																																																																										
1.2.2.6	Back Filling	15 d	16-05-16	30-05-16	0%																																																																																										
1.2.2.7	Grade Beam	27 d	09-05-16	04-06-16	0%																																																																																										
1.2.2.7.1	Re-bar Fixing	25 d	09-05-16	02-06-16	0%																																																																																										

Date: 19-04-16 5:51 PM
Sheet:1 /6

Task

Critical Task

Progress

Summary

Rolled Up Task

Rolled Up Critical Task

Project Summary

Group By Summary

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

Sl.	Task Name	Duration	Start	Finish	% Complete	Jan '16			Feb '16			Mar '16			Apr '16			May '16			Jun '16			Jul '16			Aug '16			Sep '16			Oct '16			Nov '16			Dec '16			Jan '17			Feb '17			Mar '17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
						09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

Sl.	Task Name	Duration	Start	Finish	% Complete	Jan '16			Feb '16			Mar '16			Apr '16			May '16			Jun '16			Jul '16			Aug '16			Sep '16			Oct '16			Nov '16			Dec '16			Jan '17			Feb '17			Mar '17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
						09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10

Date: 19-04-16 5:51 PM
 Sheet:3 /6

Task		Progress		Rolled Up Task		Rolled Up Progress		Group By Summary	
Critical Task		Summary		Rolled Up Critical Task		Project Summary			

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE


[illegible]


WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

[illegible]

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

[illegible]

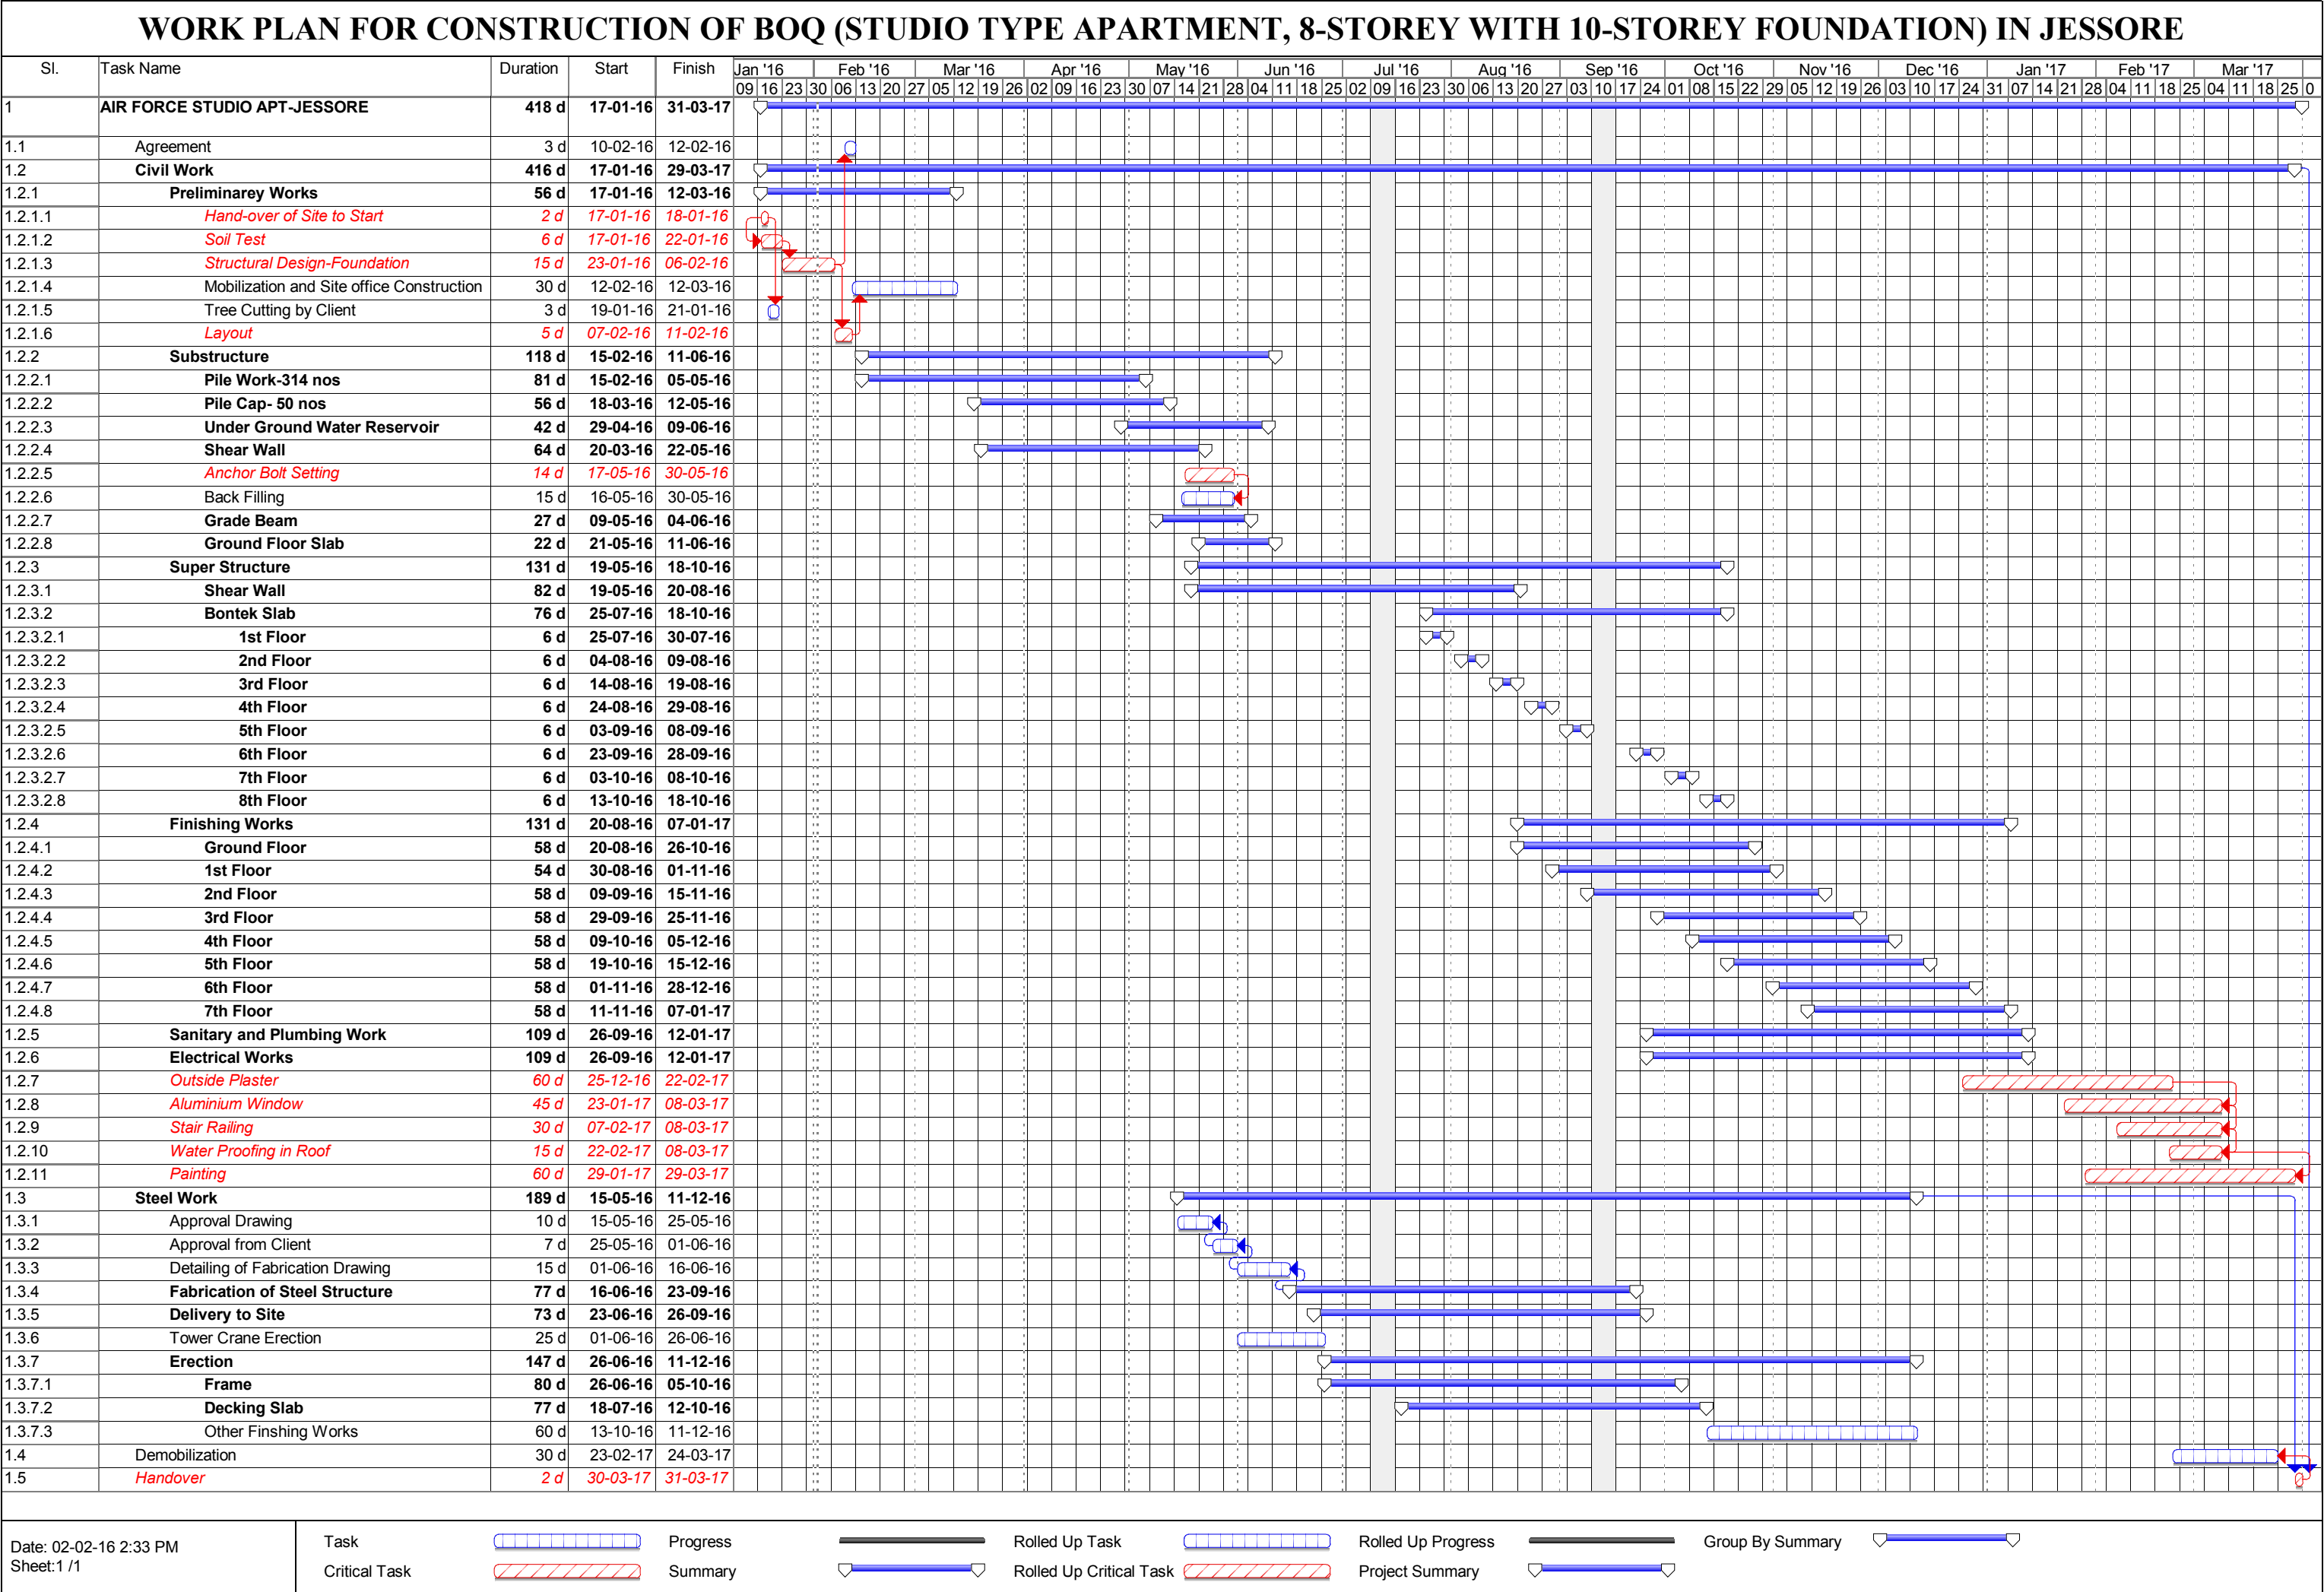

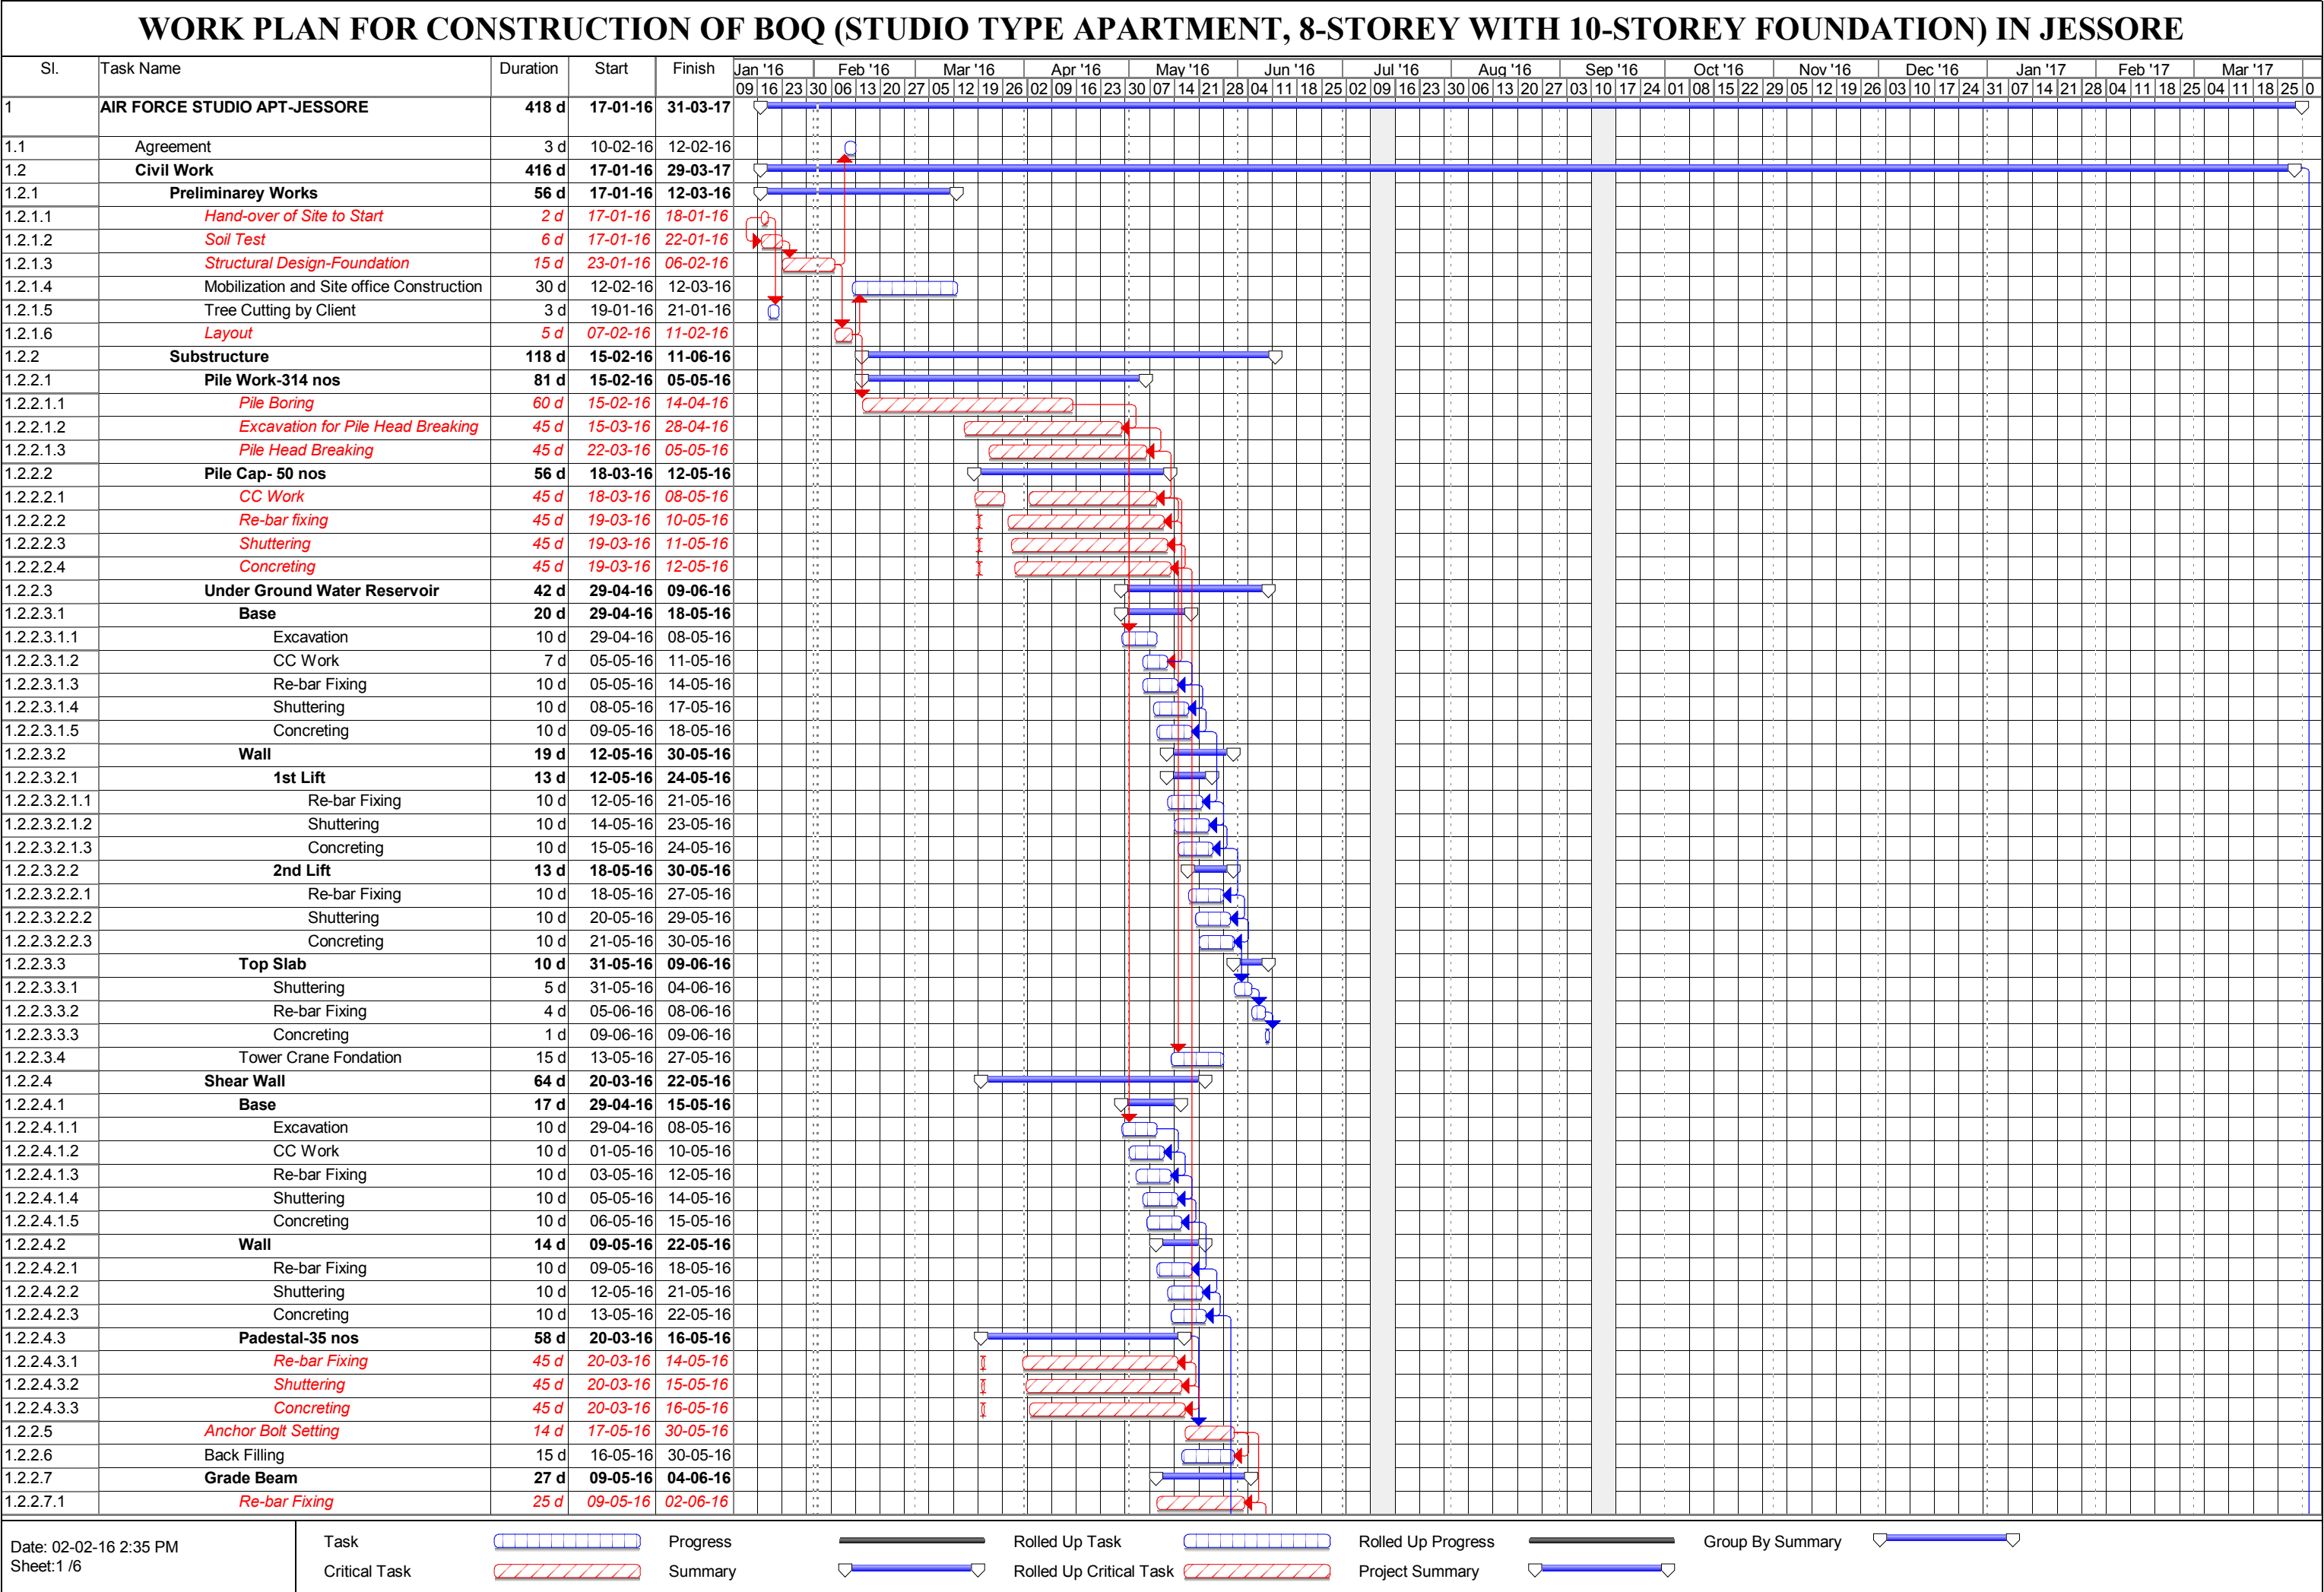

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

Sr.	Task Name	Duration	Start	Finish
1.2.2.7.2	Shuttering	25 d	11-05-16	04-06-16
1.2.2.7.3	Concreting	25 d	11-05-16	04-06-16
1.2.2.8	Ground Floor Slab	22 d	21-05-16	11-06-16
1.2.2.8.1	Sand Filling work	15 d	21-05-16	04-06-16
1.2.2.8.2	Brick Flat Soling	10 d	29-05-16	07-06-16
1.2.2.8.3	Re-bar work	10 d	01-06-16	10-06-16
1.2.2.8.4	Concreting	10 d	02-06-16	11-06-16
1.2.3	Super Structure	131 d	19-05-16	18-10-16
1.2.3.1	Shear Wall	82 d	19-05-16	20-08-16
1.2.3.1.1	Ground Floor	15 d	19-05-16	02-06-16
1.2.3.1.1.1	1st Lift	10 d	19-05-16	28-05-16
1.2.3.1.1.1.1	Re-bar Work	7 d	19-05-16	25-05-16
1.2.3.1.1.1.2	Shuttering	7 d	21-05-16	27-05-16
1.2.3.1.1.1.3	Concreting	7 d	22-05-16	28-05-16
1.2.3.1.1.2	2nd Lift	10 d	24-05-16	02-06-16
1.2.3.1.1.2.1	Re-bar Work	7 d	24-05-16	30-05-16
1.2.3.1.1.2.2	Shuttering	7 d	26-05-16	01-06-16
1.2.3.1.1.2.3	Concreting	7 d	27-05-16	02-06-16
1.2.3.1.2	1st Floor	15 d	29-05-16	12-06-16
1.2.3.1.2.1	1st Lift	10 d	29-05-16	07-06-16
1.2.3.1.2.1.1	Re-bar Work	7 d	29-05-16	04-06-16
1.2.3.1.2.1.2	Shuttering	7 d	31-05-16	06-06-16
1.2.3.1.2.1.3	Concreting	7 d	01-06-16	07-06-16
1.2.3.1.2.2	2nd Lift	10 d	03-06-16	12-06-16
1.2.3.1.2.2.1	Re-bar Work	7 d	03-06-16	09-06-16
1.2.3.1.2.2.2	Shuttering	7 d	05-06-16	11-06-16
1.2.3.1.2.2.3	Concreting	7 d	06-06-16	12-06-16
1.2.3.1.3	2nd Floor	15 d	08-06-16	22-06-16
1.2.3.1.3.1	1st Lift	10 d	08-06-16	17-06-16
1.2.3.1.3.1.1	Re-bar Work	7 d	08-06-16	14-06-16
1.2.3.1.3.1.2	Shuttering	7 d	10-06-16	16-06-16
1.2.3.1.3.1.3	Concreting	7 d	11-06-16	17-06-16
1.2.3.1.3.2	2nd Lift	10 d	13-06-16	22-06-16
1.2.3.1.3.2.1	Re-bar Work	7 d	13-06-16	19-06-16
1.2.3.1.3.2.2	Shuttering	7 d	15-06-16	21-06-16
1.2.3.1.3.2.3	Concreting	7 d	16-06-16	22-06-16
1.2.3.1.4	3rd Floor	15 d	15-06-16	29-06-16
1.2.3.1.4.1	1st Lift	10 d	15-06-16	24-06-16
1.2.3.1.4.1.1	Re-bar Work	7 d	15-06-16	21-06-16
1.2.3.1.4.1.2	Shuttering	7 d	17-06-16	23-06-16
1.2.3.1.4.1.3	Concreting	7 d	18-06-16	24-06-16
1.2.3.1.4.2	2nd Lift	10 d	20-06-16	29-06-16
1.2.3.1.4.2.1	Re-bar Work	7 d	20-06-16	26-06-16
1.2.3.1.4.2.2	Shuttering	7 d	22-06-16	28-06-16
1.2.3.1.4.2.3	Concreting	7 d	23-06-16	29-06-16
1.2.3.1.5	4th Floor	15 d	25-06-16	21-07-16
1.2.3.1.5.1	1st Lift	10 d	25-06-16	16-07-16
1.2.3.1.5.1.1	Re-bar Work	7 d	25-06-16	01-07-16
1.2.3.1.5.1.2	Shuttering	7 d	27-06-16	03-07-16
1.2.3.1.5.1.3	Concreting	7 d	28-06-16	16-07-16
1.2.3.1.5.2	2nd Lift	10 d	30-06-16	21-07-16
1.2.3.1.5.2.1	Re-bar Work	7 d	30-06-16	18-07-16
1.2.3.1.5.2.2	Shuttering	7 d	02-07-16	20-07-16
1.2.3.1.5.2.3	Concreting	7 d	03-07-16	21-07-16
1.2.3.1.6	5th Floor	15 d	17-07-16	31-07-16
1.2.3.1.6.1	1st Lift	10 d	17-07-16	26-07-16
1.2.3.1.6.1.1	Re-bar Work	7 d	17-07-16	23-07-16
1.2.3.1.6.1.2	Shuttering	7 d	19-07-16	25-07-16
1.2.3.1.6.1.3	Concreting	7 d	20-07-16	26-07-16
1.2.3.1.6.2	2nd Lift	10 d	22-07-16	31-07-16

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

[illegible]

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

[illegible]

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

Sl.	Task Name	Duration	Start	Finish	Jan '16				Feb '16				Mar '16				Apr '16				May '16				Jun '16				Jul '16				Aug '16				Sep '16				Oct '16				Nov '16				Dec '16				Jan '17				Feb '17				Mar '17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
					09	16	23	30	06	13	20	27	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	18	25	0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
1.2.5.6.1	Pipe Work	10 d	15-11-16	24-11-16																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														</

Date: 02-02-16 2:35 PM
Sheet:5 /6

Task		Progress
Critical Task		Summary

Critical Task		Summary
---------------	---	---------

Summary

Progress Summary

Summary

Rolled Up Task
Rolled Up Critical Task

Rolled Up Critical Task



Rolled Up Progress
Project Summary

Project Summary

Group By Summary

A diagram of a horizontal beam. The left end is supported by a triangular pin support. The right end is supported by a roller support, represented by a horizontal line with a single vertical line passing through its center.

WORK PLAN FOR CONSTRUCTION OF BOQ (STUDIO TYPE APARTMENT, 8-STOREY WITH 10-STOREY FOUNDATION) IN JESSORE

[illegible]
